



LBCC Bond Program Master Schedule

Status as of March 1, 2017

Activity Name	At Completion Duration	Start	Finish	16	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	034
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q

Long Beach Community College Bond Program Schedule - March 1, 2017

Liberal Arts Campus

Building D - Science

Design Building D	122	01-Jul-15 A	31-Oct-15 A
Design Building D Demo	27	01-Aug-15 A	28-Aug-15 A
Bid / Award Building D Demo	0	01-Nov-15 A	01-Nov-15 A
DSA Building D	148	01-Nov-15 A	28-Mar-16 A
Bid / Award Building D	306	01-Nov-15 A	02-Sep-16 A
Construction Building D Demo (Fall 2015)	56	28-Nov-15 A	23-Jan-16 A
Construction Building D (Fall 2016 - Fall 2017)	511	07-Sep-16 A	30-Jan-18
FF&E / Move Management Building D	366	30-Dec-16 A	30-Dec-17
Expected Substantial Completion Phase 1	0		28-Apr-17
Expected Substantial Completion Phase 2	0		12-Jun-17
Ready to Hold Classes Building D 1st Floor (Fall 2017)	0		11-Jul-17
Expected Substantial Completion Phase 3	0		07-Aug-17
Expected Substantial Completion Phase 4	0		25-Sep-17
Ready to Hold Classes Building D 2nd Floor (Spring 2018)	0		30-Dec-17

Building P - Language Arts


Design Building P	239	22-Apr-15 A	17-Dec-15 A
Design Swing Space for Building P	67	01-Aug-15 A	06-Oct-15 A
DSA Building P	280	12-Jan-16 A	17-Oct-16 A
Award Swing Space Building P	65	05-May-16 A	08-Jul-16 A
Bid / Award Building P	104	26-Oct-16 A	06-Feb-17
Move Into Swing Space Building M/N from Building P	3	27-Dec-16 A	29-Dec-16 A
Construction Building P (Spring 2017 - Summer 2018)	436	14-Feb-17	25-Apr-18
FF&E / Move Management Building P from M/N (Summer 2018)	220	27-Dec-17	03-Aug-18
Expected Contractual Substantial Completion Building P	0		25-Apr-18
Ready to Hold Classes Building P (Fall 2018)	0		03-Aug-18

Building J - Auditorium

Design Building J	176	01-Oct-15 A	24-Mar-16 A
Design Swing Space for Building J	220	01-Oct-15 A	07-May-16 A
DSA Building J	301	03-Sep-16 A	30-Jun-17
Bid / Award Swing Space for Building J	90	01-Mar-17*	29-May-17
Bid / Award Building J	85	01-Jul-17	23-Sep-17
Construction Swing Space for Building J	20	05-Jul-17	24-Jul-17
Move Into Swing Space Building FF from Building J (Summer 2017)	10	25-Jul-17	03-Aug-17
Construction Building J (Summer 2017 - Fall 2018)	550	26-Sep-17	29-Mar-19
FF&E / Move Management Building J from Public Theater & Building FF (Fall 2018)	241	31-Oct-18	28-Jun-19
Expected Substantial Completion Building J	0		28-Feb-19
Ready to Hold Classes Building J (Fall 2019)	0		28-Jun-19

Outdoor Kinesiology Labs

Pre-Design Physical Ed Lab	152	28-Oct-16 A	28-Mar-17
Design Physical Ed Lab	460	28-Oct-16 A	30-Jan-18
DSA Physical Ed Lab	280	31-Jan-18	06-Nov-18
Bid / Award Physical Ed Lab	90	07-Nov-18	04-Feb-19
Move Into Swing Space from Physical Ed Lab	10	17-Dec-18*	26-Dec-18
Construction Physical Ed Lab	247	05-Feb-19	09-Oct-19

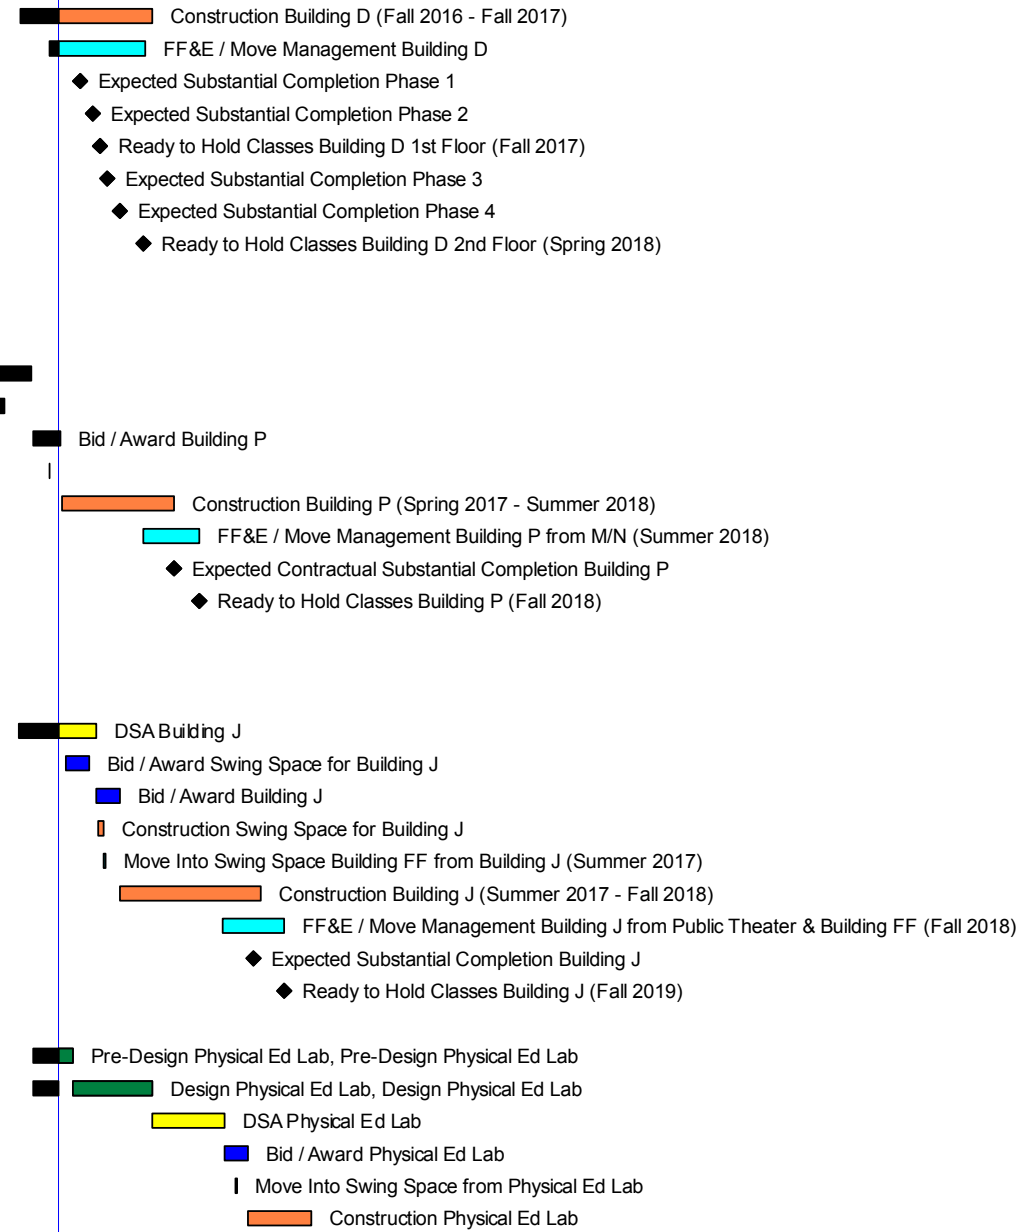


■ PRE	■ Bid / Award	■ CONST	■ Actual
■ DESIGN	■ DSA	■ FF&E	◆ Milestone



LBCC Bond Program Master Schedule

Status as of March 1, 2017

Activity Name	At Completion Duration	Start	Finish	16	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	034	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
FF&E / Move Management Physical Ed Lab	261	13-May-19	28-Jan-20																				
Expected Substantial Completion Physical Ed Lab	0		10-Sep-19																				
Ready to Hold Classes Physical Ed Lab	0		28-Jan-20																				
LAC Walkway and Wayfindings																							
Pre-Design Building	49	01-Feb-17*	21-Mar-17																				
Design Building	154	22-Mar-17	22-Aug-17																				
DSA Review Building	280	23-Aug-17	29-May-18																				
Bid / Award	90	30-May-18	27-Aug-18																				
NTP Construction	0	28-Aug-18																					
Construction	2664	28-Aug-18	12-Dec-25																				
Expected Substantial Completion	0		12-Dec-25																				
Building W - Aquatic Center																							
Pre-Design Aquatic Center	184	01-Aug-17*	31-Jan-18																				
Design Aquatic Center	117	01-Feb-18	28-May-18																				
DSA Aquatic Center	280	15-Nov-18	21-Aug-19																				
Bid / Award Aquatic Center	90	22-Aug-19	19-Nov-19																				
Construction Aquatic Center	548	29-Jan-20	29-Jul-21																				
FF&E / Move Management Aquatic Center	333	02-Mar-21	28-Jan-22																				
Expected Substantial Completion Aquatic Center	0		30-Jun-21																				
Ready to Hold Classes Aquatic Center (Spring 2022)	0		28-Jan-22																				
Building M - Liberal Arts																							
Pre-Design Building M	165	05-Jul-17*	16-Dec-17																				
Design Building M	266	17-Dec-17	08-Sep-18																				
DSA Review Building M	280	16-Sep-18	22-Jun-19																				
Construction Swing Space Building M	40	08-Jun-19	17-Jul-19																				
Bid / Award Building M	90	23-Jun-19	20-Sep-19																				
Expected Substantial Completion Swing Space Building M	0		17-Jul-19																				
Move Into Swing Space Building B from Building M	20	18-Jul-19	06-Aug-19																				
NTP Construction Building M	0	07-Aug-19																					
Construction Building M	925	21-Sep-19	02-Apr-22																				
Expected Substantial Completion Building M	0		02-Apr-22																				
FF&E / Move Management from Building B to Building M	82	03-Apr-22	23-Jun-22																				
Building E - College Center																							
Design Building E	429	03-Oct-20	05-Dec-21																				
DSA Review Swing Space for Building E	280	16-Sep-21	22-Jun-22																				
DSA Review Building E	280	09-Dec-21	14-Sep-22																				
Bid / Award Swing Space for Building E	93	23-Jun-22	23-Sep-22																				
Bid / Award Building E	92	15-Sep-22	15-Dec-22																				
Construction Swing Space for Building E	75	24-Sep-22	07-Dec-22																				
Expected Substantial Completion Swing Space for Building E	0		08-Nov-22																				
Move Into Swing Space Building B from Building E	30	08-Dec-22	06-Jan-23																				
Construction Building E	640	12-Jan-23	12-Oct-24																				
FF&E / Move Management Building E from Building B	206	15-Jun-24	06-Jan-25																				
Expected Substantial Completion	0		13-Sep-24																				
Ready to Hold Classes Building E (Spring 2025)	0		06-Jan-25																				
Building O2 - Economic & Workforce Development/Foundation																							
Pre-Design Building O2	180	14-Apr-23*	10-Oct-23																				

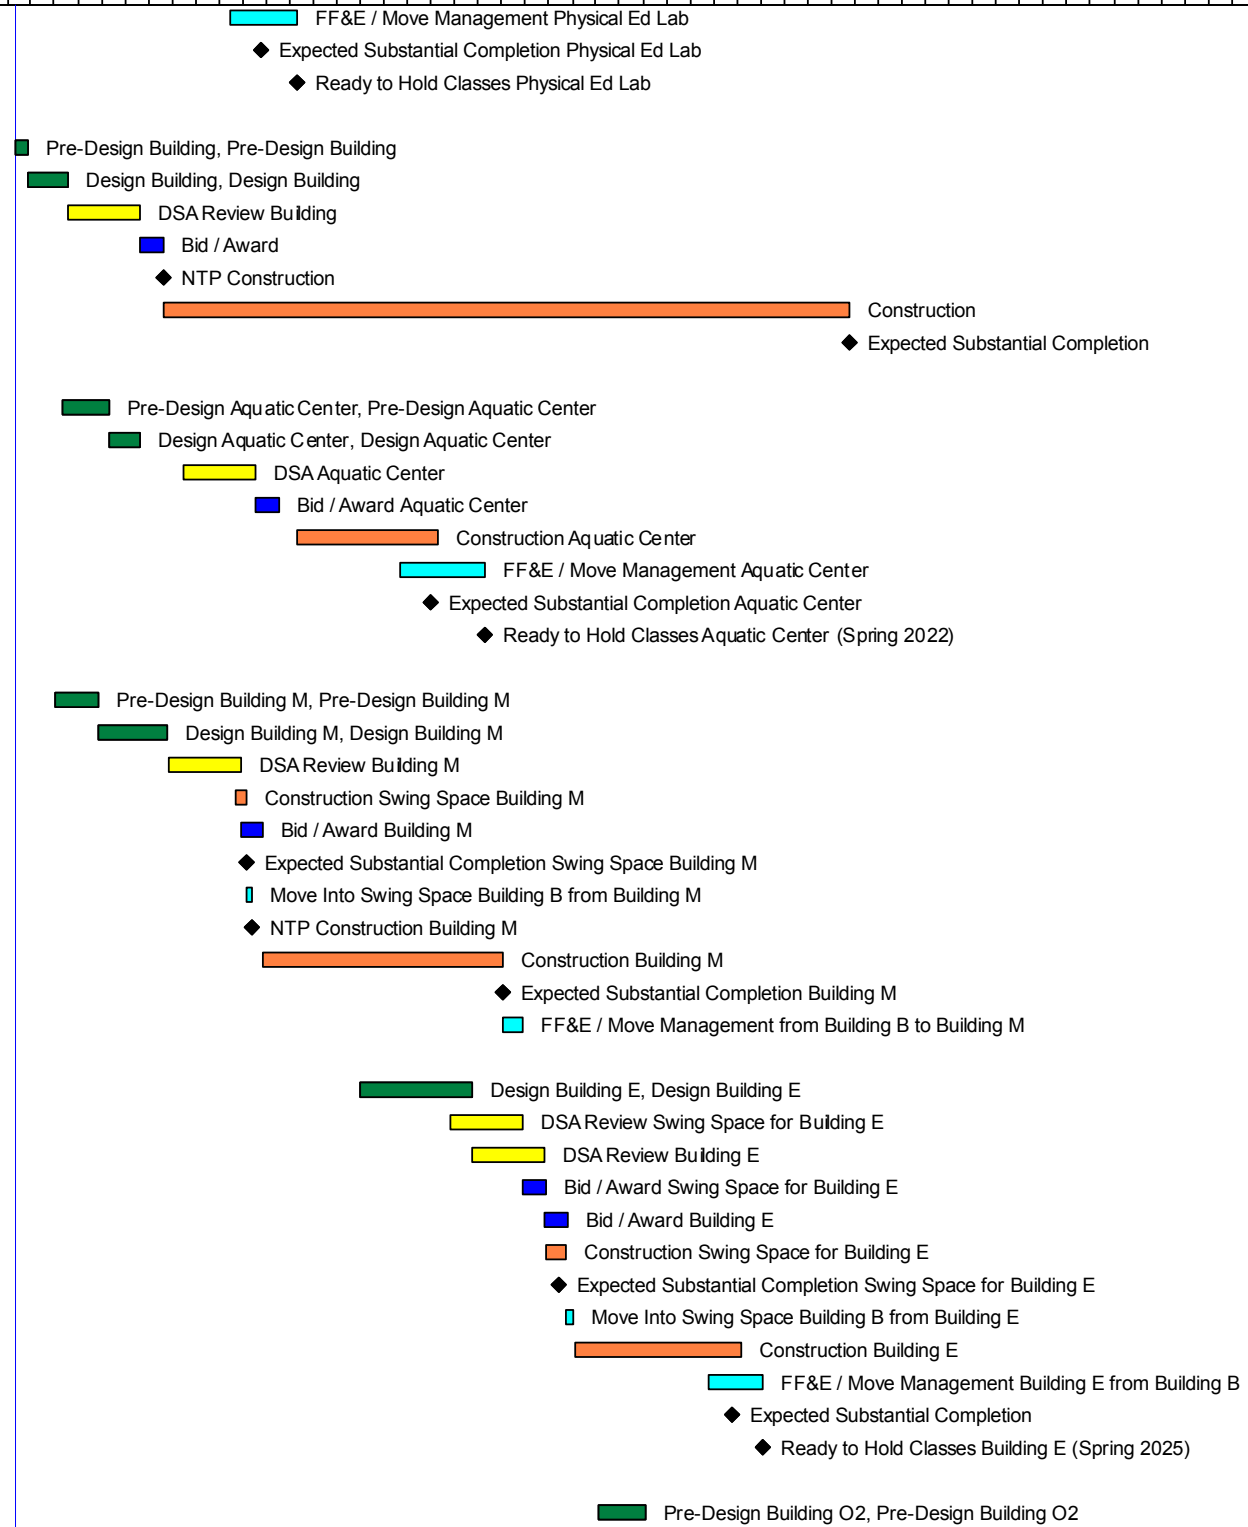


■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone



LBCC Bond Program Master Schedule

Status as of March 1, 2017

Activity Name	At Completion Duration	Start	Finish	16	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	034	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Design Building O2	280	11-Oct-23	16-Jul-24																				
DSA Review Building O2	280	17-Jul-24	22-Apr-25																				
Construction Swing Space Building O2	40	23-Apr-25	01-Jun-25																				
Bid / Award Building O2	90	23-Apr-25	21-Jul-25																				
Expected Substantial Completion Swing Space Building O2	0		01-Jun-25																				
Move Into Swing Space Building B from Building O2	20	22-Jun-25	11-Jul-25																				
NTP Construction Building O2	0	12-Jul-25																					
Construction Building O2	550	22-Jul-25	22-Jan-27																				
FF&E / Move Management from Building B to Building O2	339	27-Jul-26	30-Jun-27																				
Expected Substantial Completion Building O2	0		22-Jan-27																				
Building G - Music																							
Pre-Design Building G	216	04-Aug-25*	07-Mar-26																				
Design Building G	273	08-Mar-26	05-Dec-26																				
DSA Review Building G	280	06-Dec-26	11-Sep-27																				
Design Swing Space for Building G	67	01-Jun-27	06-Aug-27																				
Bid / Award Swing Space for Building G	90	07-Aug-27	04-Nov-27																				
Bid / Award Building G	90	12-Sep-27	10-Dec-27																				
Construction Swing Space Building for G	40	05-Nov-27	14-Dec-27																				
Expected Substantial Completion Swing Space Building for G	0		14-Dec-27																				
Move Into Swing Space Building B from Building G	15	15-Dec-27	29-Dec-27																				
Construction Building G	780	30-Dec-27	16-Feb-30																				
Expected Substantial Completion Building G	0		18-Jan-30																				
FF&E / Move Management Building G from Building B	162	18-Jan-30	28-Jun-30																				
Ready to Hold Classes Building G	0		28-Jun-30																				
Building H - Theater Arts																							
Pre-Design Building H	217	04-Aug-25*	08-Mar-26																				
Design Building H	273	09-Mar-26	06-Dec-26																				
DSA Review Building H	280	07-Dec-26	12-Sep-27																				
Bid / Award Building H	92	13-Sep-27	13-Dec-27																				
Move Into Public Theater from Building H	20	15-Dec-27	03-Jan-28																				
Construction Building H	780	30-Dec-27	16-Feb-30																				
Expected Substantial Completion	0		18-Jan-30																				
FF&E / Move Management Building H from Building Public Theater	146	18-Jan-30	12-Jun-30																				
Ready to Hold Classes Building H	0		12-Jun-30																				
Building K - Art																							
Pre-Design Building K	210	06-Aug-28*	03-Mar-29																				
Design Building K	224	04-Mar-29	13-Oct-29																				
DSA Review Building K	280	14-Oct-29	20-Jul-30																				
Bid / Award Building K	90	21-Jul-30	18-Oct-30																				
Move Into Swing Space Building B from Building K	10	20-Dec-30	29-Dec-30																				
NTP Construction Building K	0	30-Dec-30																					
Construction Building K	420	30-Dec-30	22-Feb-32																				
FF&E / Move Management Building K from Building B	149	09-Jan-32	05-Jun-32																				
Expected Substantial Completion Building K	0		22-Feb-32																				
Ready to Hold Classes Building K (Fall 2033)	0		05-Jun-32																				
Building R - Primary Gymnasium																							
Pre-Design Building R	145	08-Jul-29*	29-Nov-29																				

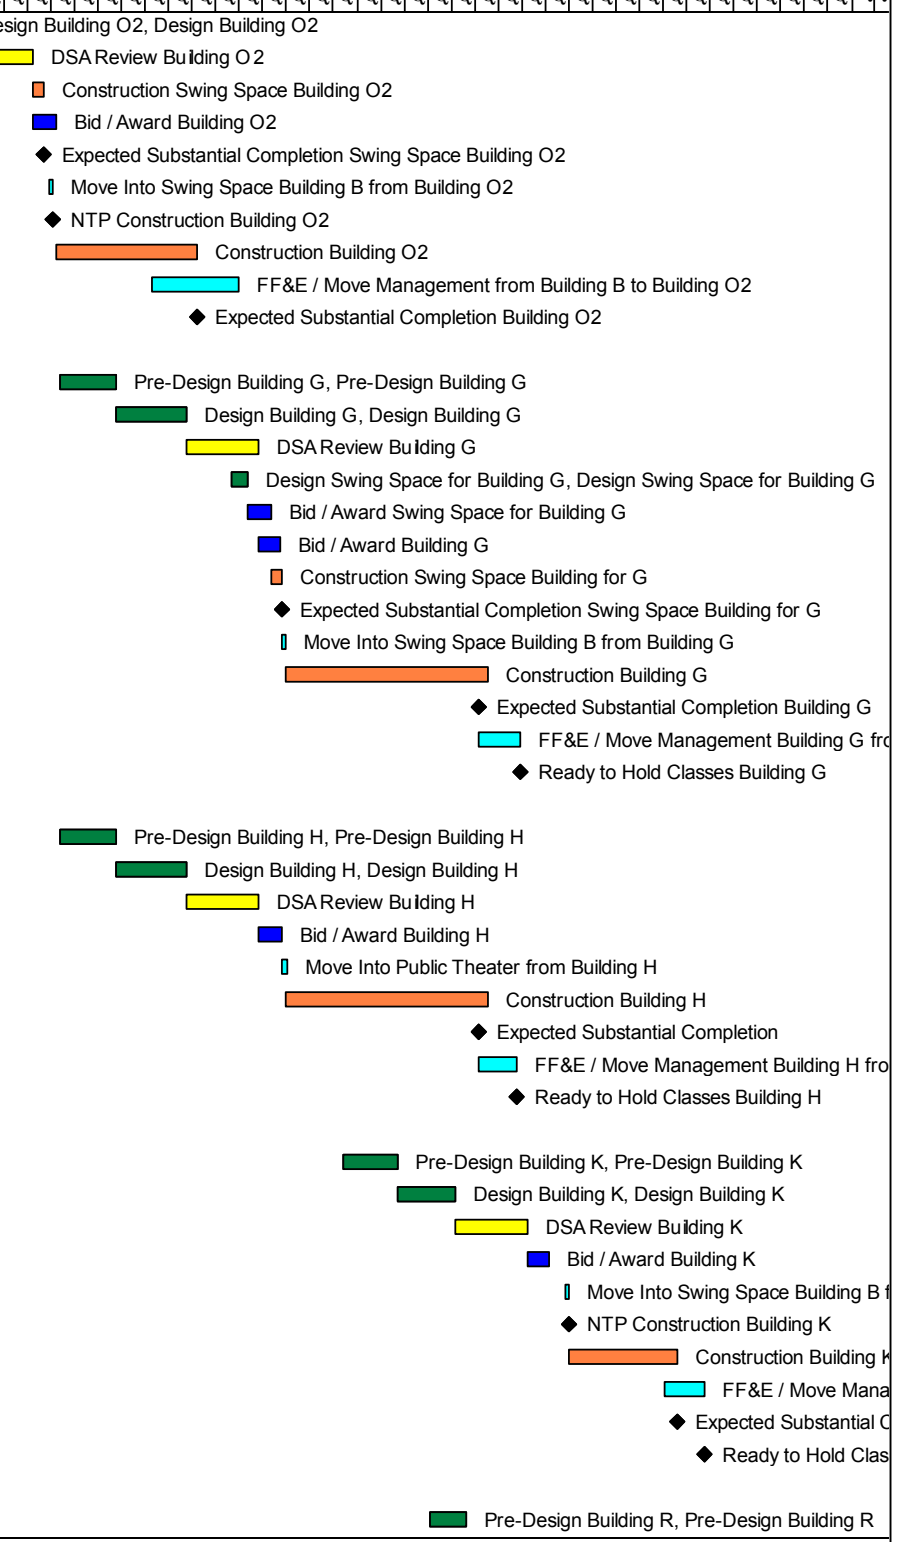

█ PRE █ Bid / Award █ CONST █ Actual
█ DESIGN █ DSA █ FF&E ◆ ◆ Milestone



LBCC Bond Program Master Schedule

Status as of March 1, 2017

Activity Name	At Completion Duration	Start	Finish	16	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Design Building R	363	30-Nov-29	27-Nov-30																				
DSA Review Building R	280	28-Nov-30	03-Sep-31																				
Bid / Award Building R	90	04-Sep-31	02-Dec-31																				
NTP Construction Building R	0	03-Dec-31																					
Construction Building R	760	03-Dec-31	31-Dec-33																				
FF&E / Move Management Building R	180	05-Jul-33	31-Dec-33																				
Expected Substantial Completion Building R	0		31-Dec-33																				
Ready to Hold Classes Building R (Spring 2034)	0		31-Dec-33																				
Building Q - Secondary Gymnasium																							
Pre-Design Building	320	16-Jun-31*	30-Apr-32																				
Design Building	246	01-May-32	01-Jan-33																				
DSA Review Building	280	02-Jan-33	08-Oct-33																				
Bid / Award Building	90	09-Oct-33	06-Jan-34																				
NTP Construction Building	0	07-Jan-34																					
Construction Building	640	07-Jan-34	08-Oct-35																				
FF&E / Move Management Building Q	202	11-Jun-35	29-Dec-35																				
Expected Substantial Completion Building	0		08-Oct-35																				
Ready to Hold Classes Building (Spring 2036)	0		29-Dec-35																				
Building B - Tech Studies																							
Pre-Design Building	200	18-Aug-32*	05-Mar-33																				
Design Building	276	06-Mar-33	06-Dec-33																				
DSA Review Building	280	07-Dec-33	12-Sep-34																				
Bid / Award Building	95	13-Sep-34	16-Dec-34																				
NTP Construction Building	0	17-Dec-34																					
Construction Building	730	30-Dec-34	28-Dec-36																				
Expected Substantial Completion Building	0		28-Dec-36																				
Building F - Demo Family/Consumer Education/New Courtyard																							
Design Building F	245	03-Mar-35*	02-Nov-35																				
DSA Review Building F	160	03-Nov-35	10-Apr-36																				
Bid / Award Building F	55	11-Apr-36	04-Jun-36																				
Move Into Building B from Building F	180	29-Dec-36	26-Jun-37																				
Demo & Courtyard Building F	365	27-Jun-37	26-Jun-38																				
Building O1 - ITS/ Warehouse																							
Pre-Design Building	183	02-May-35*	31-Oct-35																				
Design Building	244	01-Nov-35	01-Jul-36																				
DSA Review Building	280	02-Jul-36	07-Apr-37																				
Bid / Award Building	90	08-Apr-37	06-Jul-37																				
NTP Construction Building	0	07-Jul-37																					
Construction Building O1	450	07-Jul-37	29-Sep-38																				
FF&E / Move Management Building O1 from Building O2	213	02-Jun-38	31-Dec-38																				
Expected Substantial Completion Building O1	0		29-Sep-38																				
Building S - Stadium																							
Pre-Design Building	200	01-May-35*	16-Nov-35																				
Design Building	365	22-Nov-35	20-Nov-36																				
DSA Review Building S	280	21-Nov-36	27-Aug-37																				
Bid / Award Building S	90	28-Aug-37	25-Nov-37																				
Construction Swing Space Building for S	90	28-Aug-37	25-Nov-37																				

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone



LBCC Bond Program Master Schedule

Status as of March 1, 2017

Activity Name	At Completion Duration	Start	Finish	16	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	034	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Expected Substantial Completion Swing Space Building for S	0		25-Nov-37																				
Move Into Swing Space Building TBD from Building S	15	06-Dec-37	20-Dec-37																				
NTP Construction Building S	0	21-Dec-37																					
Construction Building S	729	21-Dec-37	19-Dec-39																				
Expected Substantial Completion Building S	0		19-Dec-39																				
FF&E / Move Management Building from Building TBD to Building S	193	20-Dec-39	29-Jun-40																				
Ready to Hold Classes Building S	0		29-Jun-40																				
Building CDC - Child Development Center																							
Pre-Design Building	49	01-Jun-37*	19-Jul-37																				
Design Building	154	20-Jul-37	20-Dec-37																				
DSA Review Building	280	21-Dec-37	26-Sep-38																				
Bid / Award Building	90	27-Sep-38	25-Dec-38																				
NTP Construction Building	0	26-Dec-38																					
Construction Building	290	26-Dec-38	11-Oct-39																				
FF&E / Move Management	260	15-Apr-39	30-Dec-39																				
Expected Substantial Completion Building	0		11-Oct-39																				
Pacific Coast Campus																							
Building QQ/RR - Electrical Program																							
DSA Review Building QQ/RR	113	01-Jul-15 A	22-Oct-15 A																				
Bid / Award Building QQ/RR	128	01-Nov-15 A	07-Mar-16 A																				
NTP Construction Building QQ/RR	0	21-Mar-16 A																					
Construction Building QQ/RR (Spring 2016 - Summer 2017)	412	21-Mar-16 A	06-May-17																				
FF&E / Move Management Building QQ/RR (Summer 2017)	234	13-Nov-16 A	04-Jul-17																				
Expected Substantial Completion	0		06-Apr-17																				
Punchlist Building QQ/RR	30	07-Apr-17	06-May-17																				
Ready to Hold Classes Building QQ/RR (Fall 2017)	0		04-Jul-17																				
ADA Campus Improvements																							
Design Campus Improvements	285	13-Oct-16 A	24-Jul-17																				
DSA Review ADA	210	25-Jul-17	19-Feb-18																				
Bid / Award Building ADA	90	20-Feb-18	20-May-18																				
Construction Building	504	29-May-18	14-Oct-19																				
Expected Substantial Completion	0		15-Sep-19																				
Building P2 - PCC Parking Structure																							
Pre-Design Building P2 Parking Structure	320	11-Jan-17 A	26-Nov-17																				
Award DBE Parking Structure	86	27-Nov-17	20-Feb-18																				
Design Parking Structure	174	21-Feb-18	13-Aug-18																				
DSA Review Parking Structure	280	15-Aug-18	21-May-19																				
Construct Swing Space Building FF	21	08-Jul-19*	28-Jul-19																				
Move FF from Foster Kinship (Summer 2019)	14	29-Jul-19	11-Aug-19																				
NTP Construction Parking Structure	0	12-Aug-19																					
Construction Parking Structure	365	12-Aug-19	10-Aug-20																				
Expected Substantial Completion Parking Structure	0		10-Aug-20																				
Closeout Parking Structure	90	11-Aug-20	08-Nov-20																				
Building MM - Construction Trades Ph 1																							
Design Building MM	424	01-Jun-17	29-Jul-18																				
Design Swing Space for Building MM	98	04-Feb-18	12-May-18																				
Construction Swing Space Building for MM	40	13-May-18	21-Jun-18																				

■ NTP Construction Building QQ/RR
■ Construction Building QQ/RR (Spring 2016 - Summer 2017)
■ FF&E / Move Management Building QQ/RR (Summer 2017)
◆ Expected Substantial Completion
■ Punchlist Building QQ/RR
◆ Ready to Hold Classes Building QQ/RR (Fall 2017)

■ Design Campus Improvements, Design Campus Improvements
■ DSA Review ADA
■ Bid / Award Building ADA
■ Construction Building
◆ Expected Substantial Completion

■ Pre-Design Building P2 Parking Structure, Pre-Design Building P2 Parking Structure
■ Award DBE Parking Structure
■ Design Parking Structure, Design Parking Structure
■ DSA Review Parking Structure
■ Construct Swing Space Building FF
■ Move FF from Foster Kinship (Summer 2019)
◆ NTP Construction Parking Structure
■ Construction Parking Structure
◆ Expected Substantial Completion Parking Structure
■ Closeout Parking Structure

■ Design Building MM, Design Building MM
■ Design Swing Space for Building MM, Design Swing Space for Building MM
■ Construction Swing Space Building for MM


■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone



LBCC Bond Program Master Schedule

Status as of March 1, 2017

Activity Name	At Completion Duration	Start	Finish	16	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	034	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Expected Substantial Completion Swing Space Building for MM	0		21-Jun-18																				
DSA Review Building MM	280	30-Jul-18	05-May-19																				
Bid / Award Building	90	06-May-19	03-Aug-19																				
Move Into Swing Space Building MM from Building MM	15	17-Jun-19*	01-Jul-19																				
Construction Building MM	450	04-Aug-19	26-Oct-20																				
FF&E / Move Management Building MM from Building MM	194	29-Jun-20	08-Jan-21																				
Expected Substantial Completion Building MM	0		27-Sep-20																				
Ready to Hold Classes Building MM	0		08-Jan-21																				
Building MM - Construction Trades Ph 2																							
Design Building MM	309	01-Sep-18	06-Jul-19																				
Design Swing Space for Building MM	86	06-Aug-19	30-Oct-19																				
Construction Swing Space Building for MM	40	31-Oct-19	09-Dec-19																				
DSA Review Building MM	280	29-Nov-19	03-Sep-20																				
Expected Substantial Completion Swing Space Building for MM	0		09-Dec-19																				
Bid / Award Building	90	04-Sep-20	02-Dec-20																				
Move Into Swing Space Building MM from Building MM	15	09-Jan-21	23-Jan-21																				
Construction Building MM	452	24-Jan-21	20-Apr-22																				
FF&E / Move Management Building MM from Building MM	199	22-Dec-21	08-Jul-22																				
Expected Substantial Completion Building MM	0		22-Mar-22																				
Ready to Hold Classes Building MM	0		08-Jul-22																				
Building OO - Humanities																							
Design Building Humanities	608	01-Oct-19*	30-May-21																				
DSA Review Building Humanities	280	31-May-21	06-Mar-22																				
Bid / Award Building Humanities	90	07-Mar-22	04-Jun-22																				
NTP Construction Building Humanities	0		04-Jun-22																				
Construction Building Humanities	800	05-Jun-22	12-Aug-24																				
FF&E / Move Management Building Humanities from Building Humanities	270	05-Apr-24	30-Dec-24																				
Expected Substantial Completion Building Humanities	0		14-Jul-24																				
Ready to Hold Classes Building Humanities (Spring 2025)	0		30-Dec-24																				
Building FF - Demo Fine Arts & Senior Center/Turnabout																							
Design Building FF Demo & Turnabout	189	01-Sep-22	08-Mar-23																				
DSA Review Building FF	280	09-Mar-23	13-Dec-23																				
Bid / Award Building FF Demo & Turnabout	90	14-Dec-23	12-Mar-24																				
Construction Building FF Demo	155	13-Mar-24	14-Aug-24																				
PCC Walkways & Wayfinding																							
Pre-Design Building	49	01-Sep-16 A	19-Oct-16 A																				
Design Building	256	20-Oct-16 A	02-Jul-17																				
DSA Review Building	280	03-Jul-17	08-Apr-18																				
Bid / Award	90	09-Apr-18	07-Jul-18																				
NTP Construction	0	08-Jul-18																					
Construction	8271	08-Jul-18	28-Feb-41																				
Expected Substantial Completion	0		28-Feb-41																				
District Wide																							
District Wide Security Monitoring System (Cameras)																							
Design Security Monitoring System	161	01-Oct-15 A	09-Mar-16 A																				
DSA Security Monitoring System	140	12-Apr-16 A	30-Aug-16 A																				
Bid Security Monitoring System	57	28-Jul-16 A	22-Sep-16 A																				

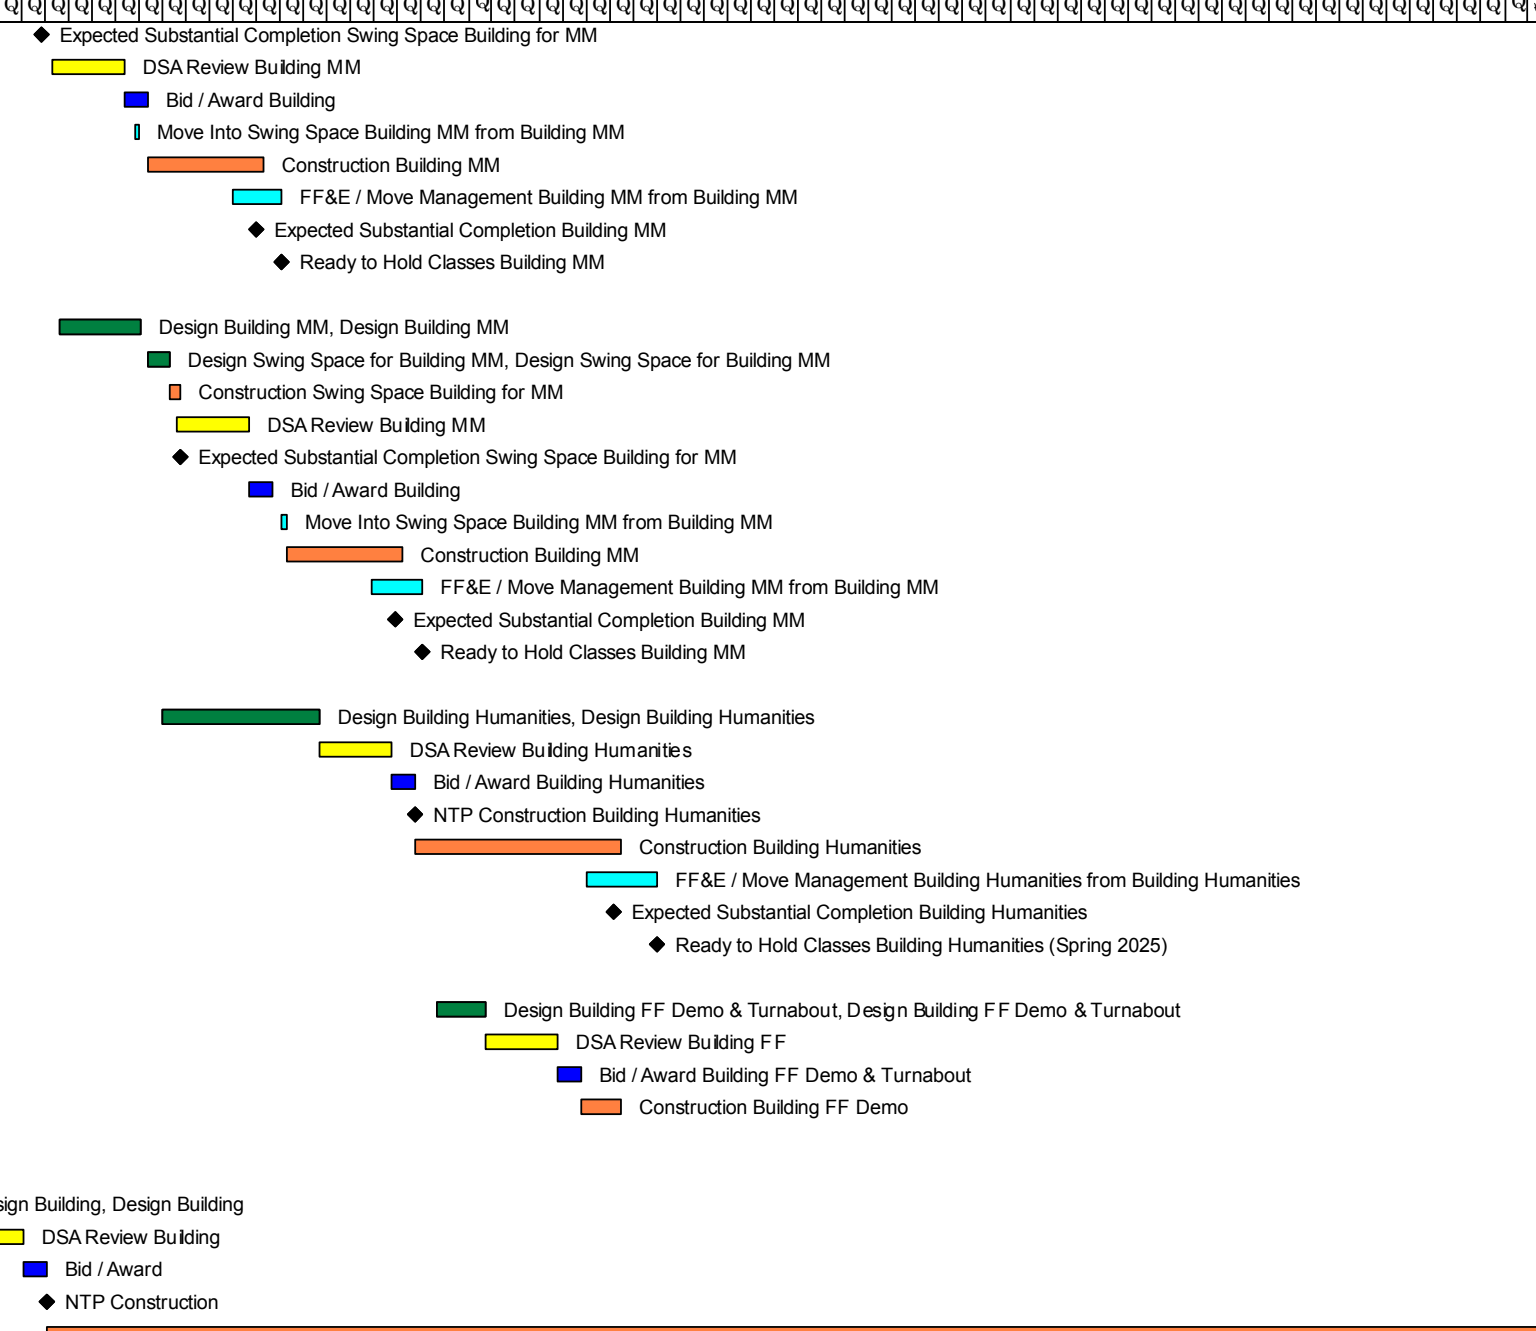

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone



LBCC Bond Program Master Schedule

Status as of March 1, 2017

Activity Name	At Completion Duration	Start	Finish	16	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	034
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Construction Security Monitoring System	366	11-Oct-16 A	12-Oct-17	■	■																	
Joint Use Facility w/ LBUSD & CSULB #12																						
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17*	14-Feb-21		■																	
Technology Refresh/Replacement																						
Technology Refresh/Replacement	8923	01-Feb-17*	07-Jul-41																			
Enterprise Wide Computer System																						
Enterprise Wide Computer System	8923	01-Feb-17*	07-Jul-41																			
Landscaping																						
Landscaping	8923	01-Feb-17*	07-Jul-41																			
Infrastructure Projectss																						
Infrastructure Projects	8923	01-Feb-17*	07-Jul-41																			
Energy/Water Conservation Projects																						
Energy Water Conservation Projects	9146	01-Jul-16 A	15-Jul-41																			
Minor Campus Improvements																						
Minor Campus Improvements	8923	01-Feb-17*	07-Jul-41																			
Surface Parking Improvements																						
Surface Parking Improvements	8923	01-Feb-17*	07-Jul-41																			

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone
