



LBCC Bond Program Master Schedule

Status as of July 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q

Long Beach Community College Bond Program Schedule - July 1, 2018 (KLAC, Bldg N)

Liberal Arts Campus

Building D - Science

FF&E / Move Management Building D	758	30-Dec-16 A	26-Jan-19
Construction Phase 1	212	04-Dec-17 A	03-Jul-18
Construction Phase 2	212	04-Dec-17 A	03-Jul-18
Construction Phase 3	60	08-Jun-18 A	06-Aug-18
Expected Substantial Completion Phase 2	0		03-Jul-18
Expected Substantial Completion Phase 1	0		03-Jul-18
Expected Substantial Completion Phase 3	0		06-Aug-18
Ready to Hold Classes Building D 1st Floor (Fall 2018)	0		15-Aug-18
Construction Phase 4	80	16-Aug-18	03-Nov-18
Expected Substantial Completion Phase 4	0		03-Nov-18
Ready to Hold Classes Building D 2nd Floor (Spring 2019)	0		26-Jan-19

Building P - Language Arts

Design Building P	239	22-Apr-15 A	17-Dec-15 A
Design Swing Space for Building P	67	01-Aug-15 A	06-Oct-15 A
DSA Building P	280	12-Jan-16 A	17-Oct-16 A
Award Swing Space Building P	65	05-May-16 A	08-Jul-16 A
Bid / Award Building P	112	26-Oct-16 A	14-Feb-17 A
Move Into Swing Space Building M/N from Building P	3	27-Dec-16 A	29-Dec-16 A
Construction Building P (Spring 2017 - Fall 2018)	559	14-Feb-17 A	26-Aug-18
FF&E / Move Management Building P from M/N (Winter 2019)	259	29-Apr-18 A	12-Jan-19
Expected Substantial Completion Building P	0		26-Aug-18
Ready to Hold Classes Building P (Spring 2019)	0		12-Jan-19

Building J - Auditorium


Design Building J	176	01-Oct-15 A	24-Mar-16 A
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A
DSA Building J	398	03-Sep-16 A	06-Oct-17 A
Bid / Award Swing Space for Building J	91	01-Mar-17 A	31-May-17 A
Construction Swing Space for Building J	56	01-Jun-17 A	26-Jul-17 A
Shelving Install Building O2 & Building FF (AlleyCat)	4	10-Jul-17 A	13-Jul-17 A
Move Into Swing Space Building FF & O2 from Building J (Summer 2017)	5	20-Jul-17 A	24-Jul-17 A
Bid / Award Building J	77	07-Oct-17 A	22-Dec-17 A
Construction Building J (Spring 2018 - Summer 2019)	520	16-Jan-18 A	19-Jun-19
FF&E / Move Management Building J from Public Theater & Building FF	250	21-May-19	25-Jan-20
Expected Substantial Completion Building J	0		19-Jun-19
Ready to Hold Classes Building J (Spring 2020)	0		25-Jan-20

Building O1 - Data Center MEP Upgrade

Bid / Award Building O1 - Data Center MEP Upgrade	132	30-Nov-17 A	11-Apr-18 A
Construction	109	30-Apr-18 A	16-Aug-18
Expected Substantial Completion	0		16-Aug-18

Building T - Emergency Generator

Bid / Award Building T - Emergency Generator	173	30-Nov-17 A	22-May-18 A
Construction Bldg T- Emergency Generator	80	29-May-18 A	16-Aug-18
Expected Substantial Completion	0		16-Aug-18

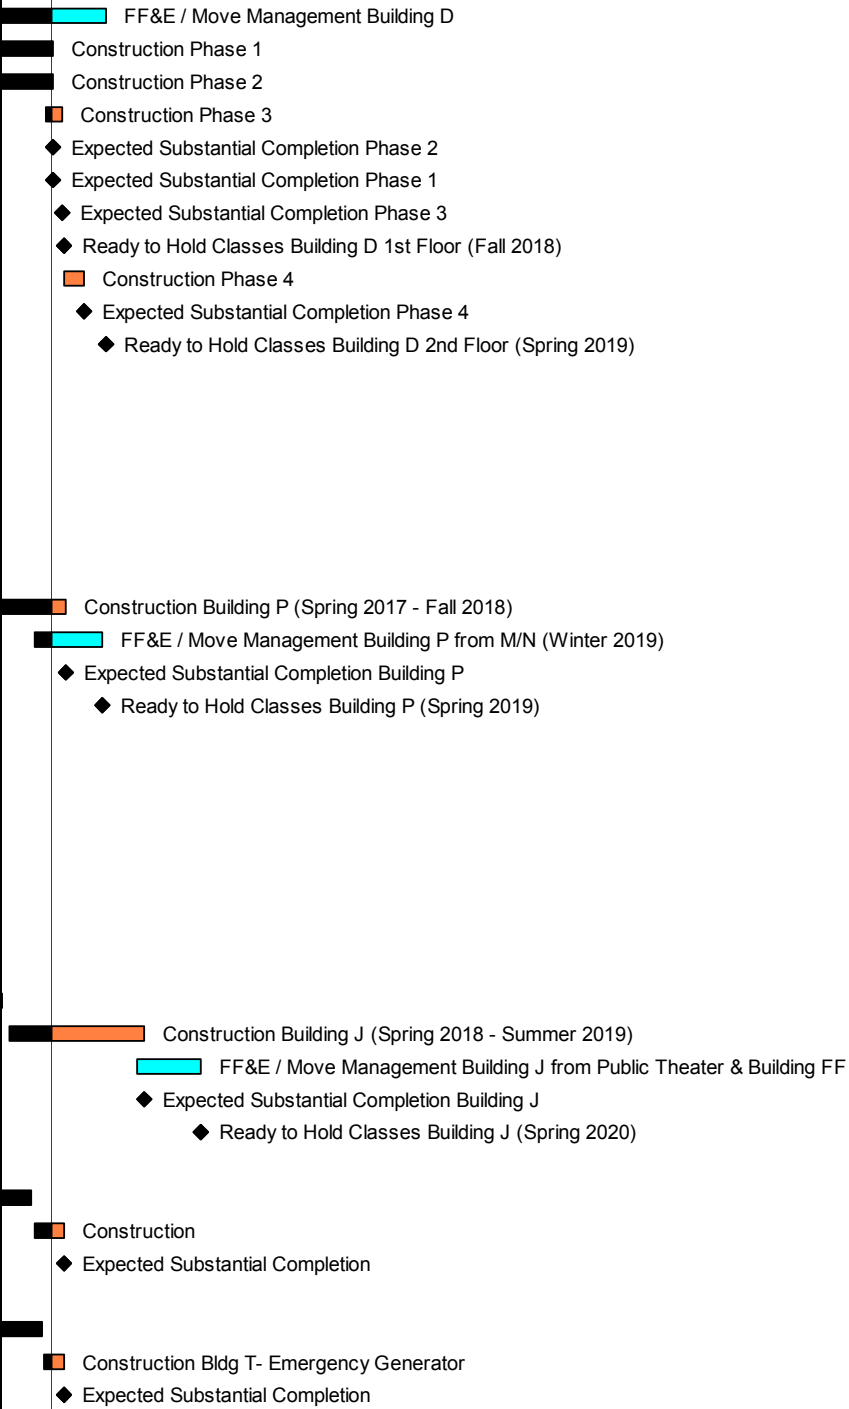

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone



LONG BEACH
CITY COLLEGE

LBCC Bond Program Master Schedule

Status as of July 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
LAC Accessibility Campus Improvements																						
Design Campus Improvements -TBD Phasing Plan	390	06-Oct-17 A	30-Oct-18	Design Campus Improvements -TBD Phasing Plan																		
DSA Review ADA	210	14-Nov-18	11-Jun-19	DSA Review ADA																		
Bid / Award ADA	90	12-Jun-19	09-Sep-19	Bid / Award ADA																		
Construction	474	17-Sep-19	02-Jan-21	Construction																		
Expected Substantial Completion	0		02-Jan-21	Expected Substantial Completion																		
Building X - Central Plant Expansion																						
Design	258	23-Jan-18 A	07-Oct-18	Design																		
DSA	208	10-Oct-18	05-May-19	DSA																		
Bid / Award	98	06-May-19	11-Aug-19	Bid / Award																		
Submittals and Approvals	42	12-Aug-19	23-Sep-19	Submittals and Approvals																		
Procurement	42	23-Sep-19	04-Nov-19	Procurement																		
Construction LAC Central Plant	127	04-Nov-19	09-Mar-20	Construction LAC Central Plant																		
Expected Substantial Completion	0		09-Mar-20	Expected Substantial Completion																		
Kinesiology Labs & Aquatics Center																						
Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A	Design Kinesiology Labs & Aquatic Center																		
Design Kinesiology Labs & Aquatic Center	592	01-Jun-17 A	13-Jan-19	Design Kinesiology Labs & Aquatic Center																		
DSA Kinesiology Labs & Aquatic Center	172	14-Jan-19	04-Jul-19	DSA Kinesiology Labs & Aquatic Center																		
Bid / Award Kinesiology Labs & Aquatic Center	106	05-Jul-19	18-Oct-19	Bid / Award Kinesiology Labs & Aquatic Center																		
NTP Kinesiology Labs & Aquatic Center	0	14-Nov-19		NTP Kinesiology Labs & Aquatic Center																		
Construction Kinesiology Labs & Aquatic Center	530	14-Nov-19	26-Apr-21	Construction Kinesiology Labs & Aquatic Center																		
FF&E / Move Management Kinesiology Labs & Aquatic Center	194	27-Jan-21	08-Aug-21	FF&E / Move Management Kinesiology Labs & Aquatic Center																		
Expected Substantial Completion Kinesiology Labs & Aquatic Center	0		26-Apr-21	Expected Substantial Completion Kinesiology Labs & Aquatic Center																		
Ready to Hold Classes Kinesiology Labs & Aquatic Center (F all 2021)	0		08-Aug-21	Ready to Hold Classes Kinesiology Labs & Aquatic Center (F all 2021)																		
Building M - Liberal Arts																						
Pre-Design Building M	0	30-Oct-17 A	30-Oct-17 A	Design Swing Space Building M																		
Design Swing Space Building M	241	02-Dec-17 A	30-Jul-18	Design Swing Space Building M																		
Award DBE Building M	39	27-Jun-18 A	04-Aug-18	Award DBE Building M																		
DSA Swing Space Building M	120	31-Jul-18	27-Nov-18	DSA Swing Space Building M																		
Design Building M	266	10-Sep-18	02-Jun-19	Design Building M																		
Bid Swing Space Building M	90	28-Nov-18	25-Feb-19	Bid Swing Space Building M																		
Construction Swing Space Building M	90	26-Feb-19	26-May-19	Construction Swing Space Building M																		
Expected Substantial Completion Swing Space Building M	0		26-May-19	Expected Substantial Completion Swing Space Building M																		
DSA Review Building M	280	03-Jun-19	08-Mar-20	DSA Review Building M																		
Move Into Swing Space Building B from Building M (Summer 2019)	20	26-Jun-19*	15-Jul-19	Move Into Swing Space Building B from Building M (Summer 2019)																		
Demolition Building M	60	04-Sep-19	02-Nov-19	Demolition Building M																		
NTP Construction Building M	0	16-Mar-20		NTP Construction Building M																		
Construction Building M	726	16-Mar-20	11-Mar-22	Construction Building M																		
FF&E / Move Management from Building B to Building M	201	12-Dec-21	30-Jun-22	FF&E / Move Management from Building B to Building M																		
Expected Substantial Completion Building M	0		11-Mar-22	Expected Substantial Completion Building M																		
Ready to Hold Classes Building J (Fall 2022)	0		30-Jun-22	Ready to Hold Classes Building J (Fall 2022)																		
Building E - College Center																						
Design Building E	432	03-Oct-20	08-Dec-21	Design Building E																		
DSA Review Swing Space for Building E	280	16-Sep-21	22-Jun-22	DSA Review Swing Space for Building E																		
DSA Review Building E	280	09-Dec-21	14-Sep-22	DSA Review Building E																		
Bid / Award Swing Space for Building E	93	23-Jun-22	23-Sep-22	Bid / Award Swing Space for Building E																		
Bid / Award Building E	91	15-Sep-22	14-Dec-22	Bid / Award Building E																		

█ PRE █ Bid / Award █ CONST █ Actual
█ DESIGN █ DSA █ FF&E ◆ ◆ Milestone




LBCC Bond Program Master Schedule

Status as of July 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Building E																							
Construction Swing Space for Building E	75	24-Sep-22	07-Dec-22																				
Expected Substantial Completion Swing Space for Building E	0		08-Nov-22																				
Move Into Swing Space Building B from Building E	30	08-Dec-22	06-Jan-23																				
NTP	0	12-Jan-23																					
Construction Building E	610	12-Jan-23	12-Sep-24																				
FF&E / Move Management Building E from Building B	206	15-Jun-24	06-Jan-25																				
Expected Substantial Completion	0		12-Sep-24																				
Ready to Hold Classes Building E (Spring 2025)	0		06-Jan-25																				
Building O2 - Economic & Workforce Development/Foundation																							
Pre-Design Building O2	180	14-Apr-23*	10-Oct-23																				
Design Building O2	280	11-Oct-23	16-Jul-24																				
DSA Review Building O2	280	17-Jul-24	22-Apr-25																				
Construction Swing Space Building O2	40	23-Apr-25	01-Jun-25																				
Bid / Award Building O2	90	23-Apr-25	21-Jul-25																				
Expected Substantial Completion Swing Space Building O2	0		01-Jun-25																				
Move Into Swing Space Building B from Building O2	20	22-Jun-25	11-Jul-25																				
NTP Construction Building O2	0	27-Jul-25																					
Construction Building O2	520	27-Jul-25	28-Dec-26																				
FF&E / Move Management from Building B to Building O2	209	09-Dec-26	05-Jul-27																				
Expected Substantial Completion Building O2	0		28-Dec-26																				
Building G - Music																							
Pre-Design Building G	216	04-Aug-25*	07-Mar-26																				
Design Building G	273	08-Mar-26	05-Dec-26																				
DSA Review Building G	280	06-Dec-26	11-Sep-27																				
Design Swing Space for Building G	67	01-Jun-27	06-Aug-27																				
Bid / Award Swing Space for Building G	89	07-Aug-27	03-Nov-27																				
Bid / Award Building G	90	12-Sep-27	10-Dec-27																				
Construction Swing Space Building for G	40	04-Nov-27	13-Dec-27																				
Expected Substantial Completion Swing Space Building for G	0		13-Dec-27																				
Move Into Swing Space Building B from Building G	15	14-Dec-27	28-Dec-27																				
Construction Building G	750	29-Dec-27	16-Jan-30																				
Expected Substantial Completion Building G	0		16-Jan-30																				
FF&E / Move Management Building G from Building B	162	17-Jan-30	27-Jun-30																				
Ready to Hold Classes Building G	0		27-Jun-30																				
Building H - Theater Arts																							
Pre-Design Building H	217	04-Aug-25*	08-Mar-26																				
Design Building H	273	09-Mar-26	06-Dec-26																				
DSA Review Building H	280	07-Dec-26	12-Sep-27																				
Bid / Award Building H	92	13-Sep-27	13-Dec-27																				
Move Into Public Theater from Building H	20	14-Dec-27	02-Jan-28																				
Construction Building H	750	29-Dec-27	16-Jan-30																				
Expected Substantial Completion	0		16-Jan-30																				
FF&E / Move Management Building H from Building Public Theater	146	17-Jan-30	11-Jun-30																				
Ready to Hold Classes Building H	0		11-Jun-30																				
Building K - Art																							
Pre-Design Building K	210	06-Aug-28*	03-Mar-29																				
Design Building K	224	04-Mar-29	13-Oct-29																				

	PRE		Bid / Award		CONST		Actual
	DESIGN		DSA		FF&E		Milestone

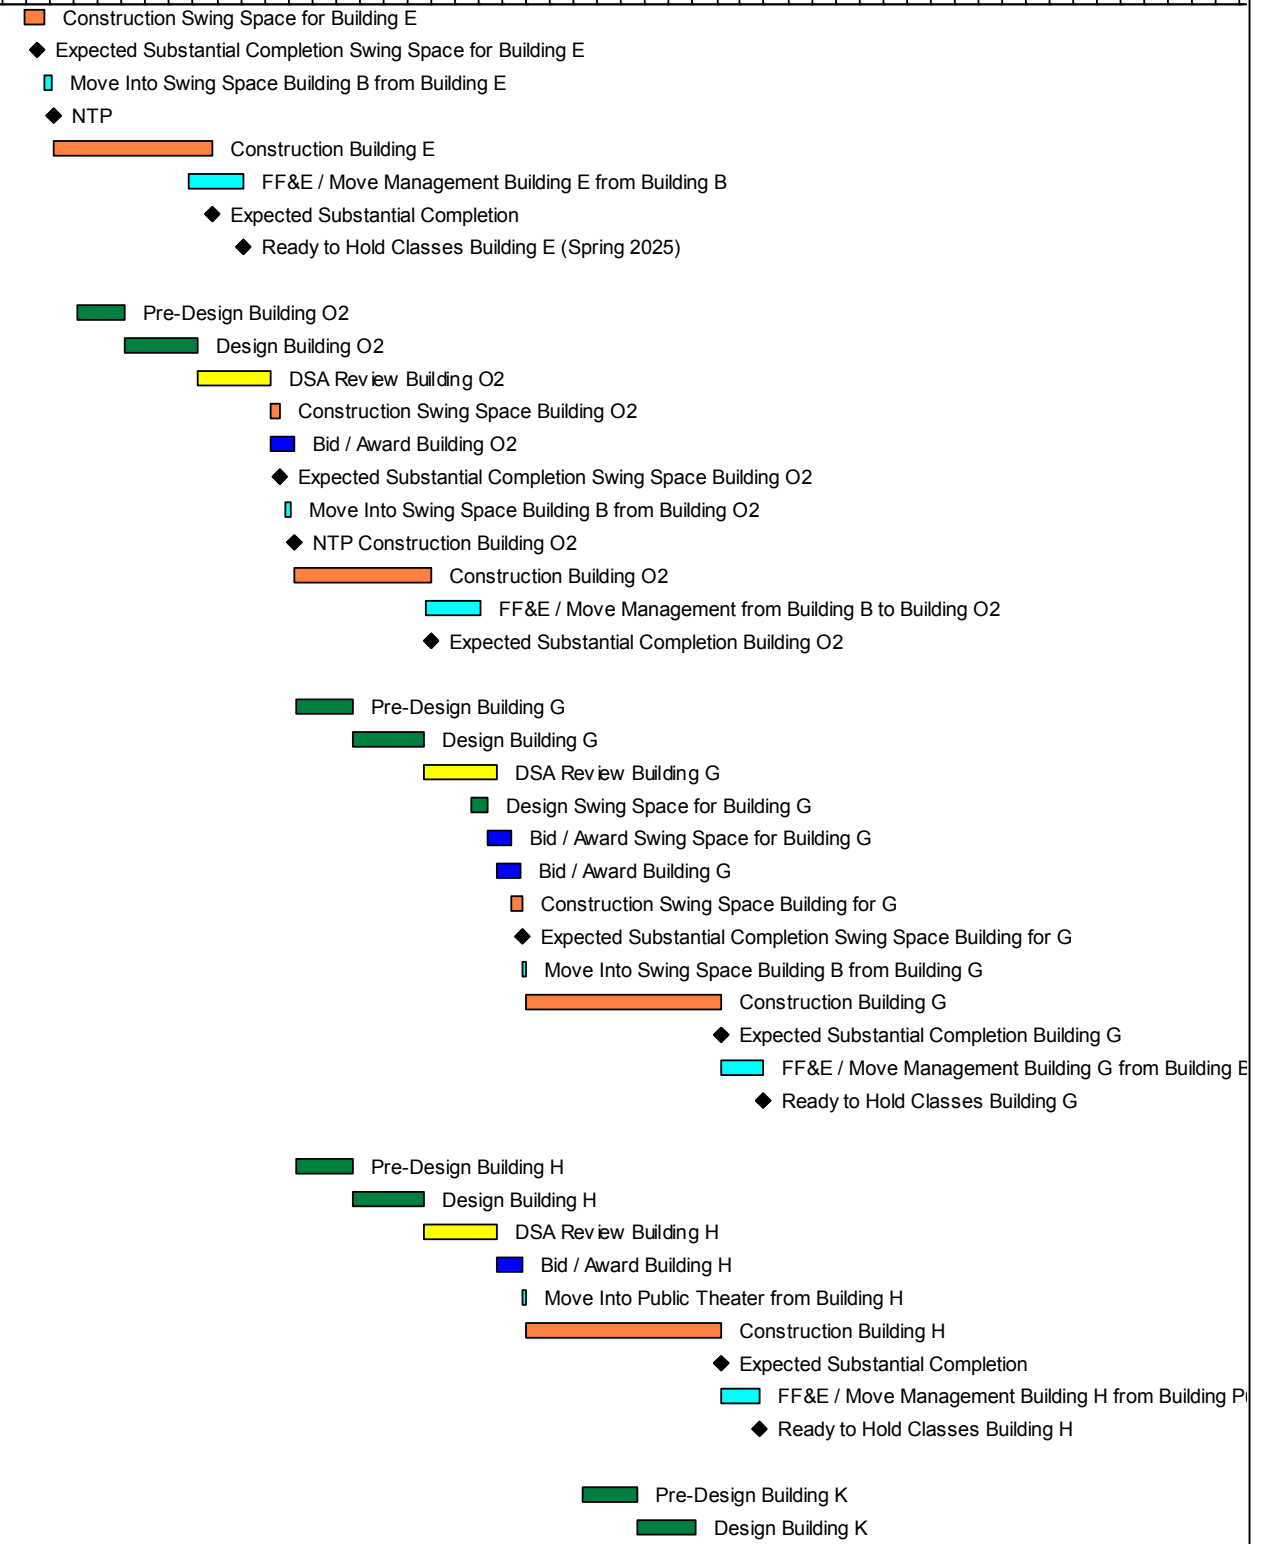




LBCC Bond Program Master Schedule

Status as of July 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
DSA Review Building K	280	14-Oct-29	20-Jul-30																				
Bid / Award Building K	90	21-Jul-30	18-Oct-30																				
Move Into Swing Space Building B from Building K	10	19-Dec-30	28-Dec-30																				
NTP Construction Building K	0	29-Dec-30																					
Construction Building K	390	29-Dec-30	22-Jan-32																				
FF&E / Move Management Building K from Building B	251	25-Oct-31	01-Jul-32																				
Expected Substantial Completion Building K	0		22-Jan-32																				
Ready to Hold Classes Building K (Fall 2032)	0		01-Jul-32																				
Building R - Primary Gymnasium																							
Pre-Design Building R	145	08-Jul-29*	29-Nov-29																				
Design Building R	363	30-Nov-29	27-Nov-30																				
DSA Review Building R	280	28-Nov-30	03-Sep-31																				
Bid / Award Building R	90	04-Sep-31	02-Dec-31																				
NTP Construction Building R	0	08-Dec-31																					
Construction Building R	730	08-Dec-31	06-Dec-33																				
FF&E / Move Management Building R	180	10-Jul-33	05-Jan-34																				
Expected Substantial Completion Building R	0		06-Dec-33																				
Ready to Hold Classes Building R (Spring 2034)	0		05-Jan-34																				
Building Q - Secondary Gymnasium																							
Pre-Design Building	320	16-Jun-31*	30-Apr-32																				
Design Building	246	01-May-32	01-Jan-33																				
DSA Review Building	280	02-Jan-33	08-Oct-33																				
Bid / Award Building	90	09-Oct-33	06-Jan-34																				
NTP Construction Building	0	12-Jan-34																					
Construction Building	640	12-Jan-34	13-Oct-35																				
FF&E / Move Management Building Q	202	16-Jun-35	03-Jan-36																				
Expected Substantial Completion Building	0		13-Oct-35																				
Ready to Hold Classes Building (Spring 2036)	0		03-Jan-36																				
Building B - Tech Studies																							
Pre-Design Building	200	18-Aug-32*	05-Mar-33																				
Design Building	276	06-Mar-33	06-Dec-33																				
DSA Review Building	280	07-Dec-33	12-Sep-34																				
Bid / Award Building	95	13-Sep-34	16-Dec-34																				
NTP Construction Building	0	17-Dec-34																					
Construction Building	730	04-Jan-35	02-Jan-37																				
Expected Substantial Completion Building	0		02-Jan-37																				
Building F - Demo Family/Consumer Education/New Courtyard																							
Design Building F	245	03-Mar-35*	02-Nov-35																				
DSA Review Building F	160	03-Nov-35	10-Apr-36																				
Bid / Award Building F	55	11-Apr-36	04-Jun-36																				
Move Into Building B from Building F	180	03-Jan-37	01-Jul-37																				
Demo & Courtyard Building F	365	02-Jul-37	01-Jul-38																				
Building O1 - IITS/ Warehouse																							
Pre-Design Building	183	02-May-35*	31-Oct-35																				
Design Building	244	01-Nov-35	01-Jul-36																				
DSA Review Building	280	02-Jul-36	07-Apr-37																				
Bid / Award Building	90	08-Apr-37	06-Jul-37																				

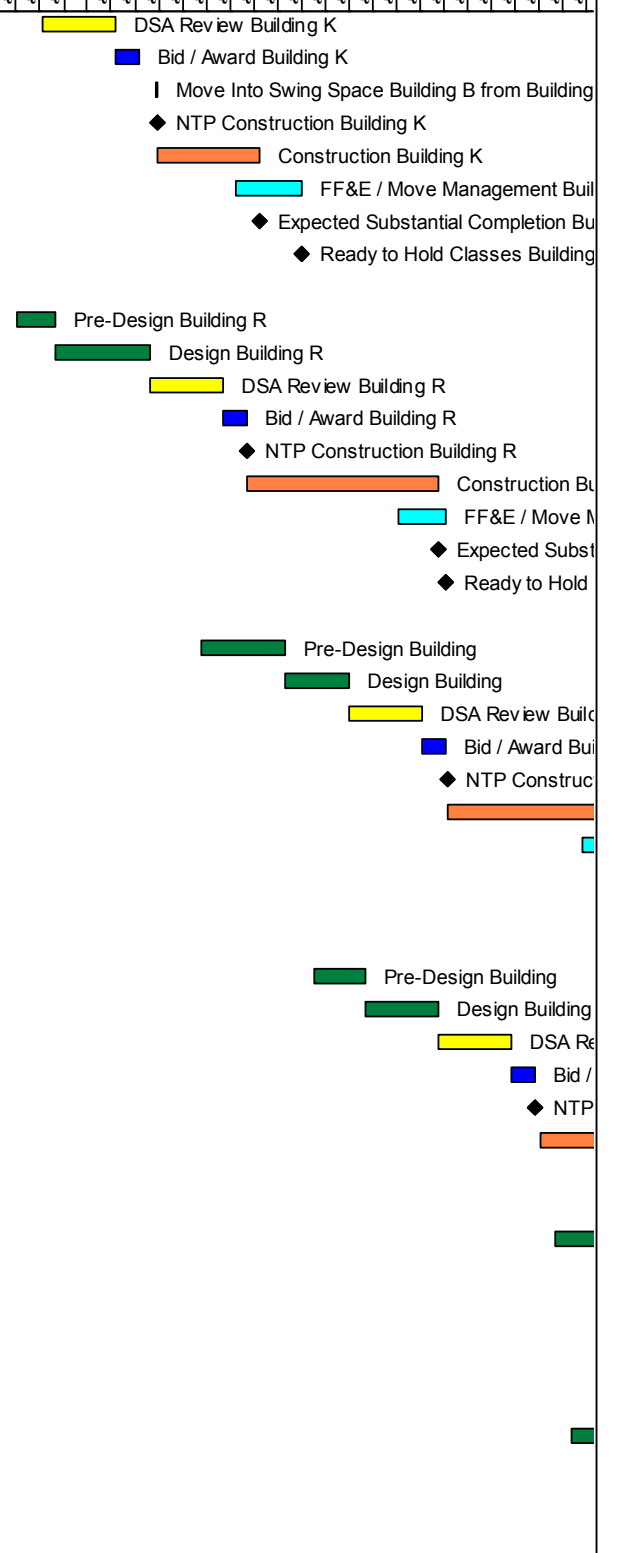


■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone



LBCC Bond Program Master Schedule

Status as of July 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
NTP Construction Building																					
Construction Building O1	420	12-Jul-37	04-Sep-38																		
FF&E / Move Management Building O1 from Building O2	213	08-May-38	06-Dec-38																		
Expected Substantial Completion Building O1	0		04-Sep-38																		
Building S - Stadium																					
Pre-Design Building	200	01-May-35*	16-Nov-35																		
Design Building	365	22-Nov-35	20-Nov-36																		
DSA Review Building S	280	21-Nov-36	27-Aug-37																		
Bid / Award Building S	90	28-Aug-37	25-Nov-37																		
Construction Swing Space Building for S	90	28-Aug-37	25-Nov-37																		
Expected Substantial Completion Swing Space Building for S	0		25-Nov-37																		
Move Into Swing Space Building TBD from Building S	15	06-Dec-37	20-Dec-37																		
NTP Construction Building S	0	21-Dec-37																			
Construction Building S	700	21-Dec-37	20-Nov-39																		
FF&E / Move Management Building from Building TBD to Building S	250	24-Jul-39	29-Mar-40																		
Expected Substantial Completion Building S	0		20-Nov-39																		
Punchlist Building S	30	21-Nov-39	20-Dec-39																		
Ready to Hold Classes Building S	0		29-Mar-40																		
Building CDC - Child Development Center																					
Pre-Design Building	49	01-Jun-37*	19-Jul-37																		
Design Building	154	20-Jul-37	20-Dec-37																		
DSA Review Building	280	21-Dec-37	26-Sep-38																		
Bid / Award Building	90	27-Sep-38	25-Dec-38																		
NTP Construction Building	0	26-Dec-38																			
Construction Building	290	26-Dec-38	11-Oct-39																		
FF&E / Move Management	201	13-Jun-39	30-Dec-39																		
Expected Substantial Completion Building	0		11-Sep-39																		
LAC Walkway and Wayfindings																					
Pre-Design	49	01-Feb-17 A	21-Mar-17 A																		
Design	154	22-Mar-17 A	22-Aug-17 A																		
DSA Review	280	23-Aug-17 A	29-May-18 A																		
Bid / Award	90	30-May-18 A	27-Aug-18																		
NTP Construction	0	28-Aug-18																			
Construction	2664	28-Aug-18	12-Dec-25																		
Expected Substantial Completion	0		12-Nov-25																		
Pacific Coast Campus																					
PCC Site Barrier Removal																					
Bid / Award ADA -Site Barrier Removal	99	30-Nov-17 A	09-Mar-18 A																		
Construction - Phase 0	38	26-Mar-18 A	03-May-18 A																		
Construction - Phase 1-A	56	04-May-18 A	29-Jun-18 A																		
Construction - Phase 1-B	61	04-May-18 A	03-Jul-18																		
Construction - Phase 2	70	08-Jun-18 A	16-Aug-18																		
Construction - Phase 3-A	33	17-Aug-18	18-Sep-18																		
Construction - Phase 3-B	16	19-Sep-18	04-Oct-18																		
Expected Substantial Completion All Phases	0		04-Oct-18																		
PCC Building Barrier Removal																					

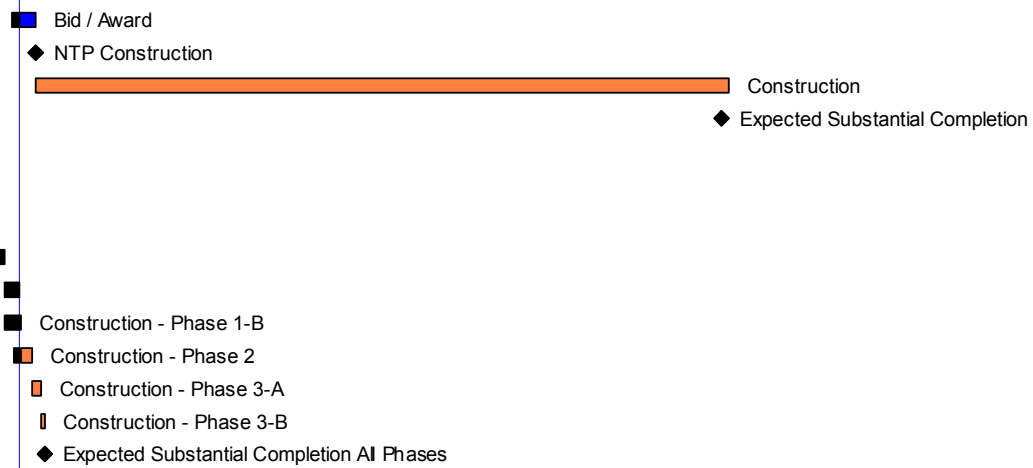

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone



LBCC Bond Program Master Schedule

Status as of July 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Bid / Award Building Barrier Removal	137	20-Feb-18 A	06-Jul-18	■ Bid / Award Building Barrier Removal																			
Construction - Phase 0	28	14-Jul-18	10-Aug-18	■ Construction - Phase 0																			
Construction - Phase 1-A	130	11-Aug-18	18-Dec-18	■ Construction - Phase 1-A																			
Construction - Phase 1-B	242	11-Aug-18	09-Apr-19	■ Construction - Phase 1-B																			
Construction - Phase 2	112	19-Dec-18	09-Apr-19	■ Construction - Phase 2																			
Construction - Phase 3	60	10-Apr-19	08-Jun-19	■ Construction - Phase 3																			
Construction - Phase 4	35	09-Jun-19	13-Jul-19	■ Construction - Phase 4																			
Expected Substantial Completion All Phases	0		13-Jul-19	◆ Expected Substantial Completion All Phases																			
Building P2 - PCC Parking Structure																							
Pre-Design Building P2 Parking Structure	456	11-Jan-17 A	11-Apr-18 A	■ Pre-Design Building P2 Parking Structure																			
Award DBE Parking Structure	96	12-Apr-18 A	16-Jul-18	■ Award DBE Parking Structure																			
Design Parking Structure	175	16-Jul-18	06-Jan-19	■ Design Parking Structure																			
DSA Review Parking Structure	254	07-Jan-19	17-Sep-19	■ DSA Review Parking Structure																			
Move into Swing Space Bldg F from Foster Kinship (Summer 2019)	14	17-Jun-19*	30-Jun-19	■ Move into Swing Space Bldg F from Foster Kinship (Summer 2019)																			
NTP Construction Parking Structure	0	02-Oct-19		◆ NTP Construction Parking Structure																			
Construction Parking Structure	367	02-Oct-19	02-Oct-20	■ Construction Parking Structure																			
Expected Substantial Completion Parking Structure	0		02-Oct-20	◆ Expected Substantial Completion Parking Structure																			
Closeout Parking Structure	30	03-Oct-20	01-Nov-20	■ Closeout Parking Structure																			
Building MM - Construction Trades Ph 1																							
Design Building MM	481	12-Sep-17 A	05-Jan-19	■ Design Building MM																			
Design Swing Space for Building MM	154	25-Nov-18	27-Apr-19	■ Design Swing Space for Building MM																			
DSA Review Building MM	280	06-Jan-19	12-Oct-19	■ DSA Review Building MM																			
Bid/Award Swing Space Building for MM	90	27-Jul-19	24-Oct-19	■ Bid/Award Swing Space Building for MM																			
Bid / Award Building	146	13-Oct-19	06-Mar-20	■ Bid / Award Building																			
Construction Swing Space Building for MM	40	25-Oct-19	03-Dec-19	■ Construction Swing Space Building for MM																			
Expected Substantial Completion Swing Space Building for MM	0		03-Dec-19	◆ Expected Substantial Completion Swing Space Building for MM																			
Move Into Swing Space Building MM from Building MM	15	17-Dec-19*	31-Dec-19	■ Move Into Swing Space Building MM from Building MM																			
Construction Building MM	420	07-Mar-20	30-Apr-21	■ Construction Building MM																			
FF&E / Move Management Building MM from Building MM	194	31-Jan-21	12-Aug-21	■ FF&E / Move Management Building MM from Building MM																			
Expected Substantial Completion Building MM	0		30-Apr-21	◆ Expected Substantial Completion Building MM																			
Ready to Hold Classes Building MM (Fall 2021)	0		12-Aug-21	◆ Ready to Hold Classes Building MM (Fall 2021)																			
Building MM - Construction Trades Ph 2																							
Design Building MM	454	01-May-19	27-Jul-20	■ Design Building MM																			
DSA Review Building MM	280	28-Jul-20	03-May-21	■ DSA Review Building MM																			
Design Swing Space for Building MM	189	15-Aug-20	19-Feb-21	■ Design Swing Space for Building MM																			
Bid/Award Swing Space Building for MM	90	22-Mar-21	19-Jun-21	■ Bid/Award Swing Space Building for MM																			
Bid / Award Building	90	04-May-21	01-Aug-21	■ Bid / Award Building																			
Construction Swing Space Building for MM	30	13-Aug-21	11-Sep-21	■ Construction Swing Space Building for MM																			
Expected Substantial Completion Swing Space Building for MM	0		11-Sep-21	◆ Expected Substantial Completion Swing Space Building for MM																			
Move Into Swing Space Building MM from Building MM	10	12-Sep-21	21-Sep-21	■ Move Into Swing Space Building MM from Building MM																			
Construction Building MM	390	02-Oct-21	26-Oct-22	■ Construction Building MM																			
FF&E / Move Management Building MM from Building MM	199	29-Jul-22	12-Feb-23	■ FF&E / Move Management Building MM from Building MM																			
Expected Substantial Completion Building MM	0		26-Oct-22	◆ Expected Substantial Completion Building MM																			
Ready to Hold Classes Building MM Ph 2 (Spring 2023)	0		12-Feb-23	◆ Ready to Hold Classes Building MM Ph 2 (Spring 2023)																			
Building OO - Humanities																							
Design Building Humanities	608	01-Oct-19*	30-May-21	■ Design Building Humanities																			
DSA Review Building Humanities	280	31-May-21	06-Mar-22	■ DSA Review Building Humanities																			

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone



LBCC Bond Program Master Schedule

Status as of July 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<p>Legend:</p> <ul style="list-style-type: none"> Bid / Award Building Humanities NTP Construction Building Humanities Construction Building Humanities FF&E / Move Management Building Humanities from Building Humanities Expected Substantial Completion Building Humanities Ready to Hold Classes Building Humanities (Spring 2025) Design Building FF Demo & Turnabout DSA Review Building FF Bid / Award Building FF Demo & Turnabout Construction Building FF Demo Joint Use w/ LBUSD & CSULB #12 Deliverables 																					
Building FF - Demo Fine Arts & Senior Center/Turnabout																					
Bid / Award Building Humanities	90	07-Mar-22	04-Jun-22																		
NTP Construction Building Humanities	0		09-Jun-22																		
Construction Building Humanities	770	10-Jun-22	18-Jul-24																		
FF&E / Move Management Building Humanities from Building Humanities	270	10-Apr-24	04-Jan-25																		
Expected Substantial Completion Building Humanities	0		18-Jul-24																		
Ready to Hold Classes Building Humanities (Spring 2025)	0		04-Jan-25																		
Design Building FF Demo & Turnabout																					
Design Building FF Demo & Turnabout	189	01-Sep-22	08-Mar-23																		
DSA Review Building FF	280	09-Mar-23	13-Dec-23																		
Bid / Award Building FF Demo & Turnabout	86	14-Dec-23	08-Mar-24																		
Construction Building FF Demo	155	09-Mar-24	10-Aug-24																		
PCC Walkways & Wayfinding																					
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41																		
District Wide																					
LBCCD Energy Master Plan																					
Benchmarking	61	31-Jul-17 A	30-Sep-17 A																		
Performance Analysis	63	30-Sep-17 A	01-Dec-17 A																		
Design Recommendations	40	17-Jan-18 A	25-Feb-18 A																		
Deliverables	136	26-Feb-18 A	11-Jul-18																		
Joint Use Facility w/ LBUSD & CSULB #12																					
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21																		
Energy/Water Conservation Projects																					
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41																		
Technology Refresh/Replacement																					
Technology Refresh/Replacement	8923	01-Feb-17 A	07-Jul-41																		
Enterprise Wide Computer System																					
Enterprise Wide Computer System	8923	01-Feb-17 A	07-Jul-41																		
Landscaping																					
Landscaping	8923	01-Feb-17 A	07-Jul-41																		
Infrastructure Projectss																					
Infrastructure Projects	8923	01-Feb-17 A	07-Jul-41																		
Minor Campus Improvements																					
Minor Campus Improvements	8923	01-Feb-17 A	07-Jul-41																		
Surface Parking Improvements																					
Surface Parking Improvements	8923	01-Feb-17 A	07-Jul-41																		

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone
