



# LBCC Bond Program Master Schedule

Status as of October 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	5
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>Long Beach Community College Bond Program Schedule - October 1, 2018</b>																					
<b>Liberal Arts Campus</b>																					
<b>Building D - Science</b>																					
FF&E / Move Management Building D	366	30-Dec-16 A	30-Dec-17 A																		
Construction Phase 1	262	04-Dec-17 A	23-Aug-18 A																		
Construction Phase 2	262	04-Dec-17 A	23-Aug-18 A																		
Construction Phase 3	116	08-Jun-18 A	01-Oct-18																		
Expected Substantial Completion Phase 2	0		23-Aug-18 A																		
Expected Substantial Completion Phase 1	0		23-Aug-18 A																		
Ready to Hold Classes Building D 1st Floor (Fall 2018)	0		27-Aug-18 A																		
Construction Phase 4	57	05-Sep-18 A	31-Oct-18																		
Expected Substantial Completion Phase 3	0		01-Oct-18																		
Expected Substantial Completion Phase 4	0		31-Oct-18																		
Ready to Hold Classes Building D 2nd Floor (Spring 2019)	0		11-Jan-19																		
<b>Building P - Language Arts</b>																					
Design Building P	239	22-Apr-15 A	17-Dec-15 A																		
Design Swing Space for Building P	67	01-Aug-15 A	06-Oct-15 A																		
DSA Building P	280	12-Jan-16 A	17-Oct-16 A																		
Award Swing Space Building P	65	05-May-16 A	08-Jul-16 A																		
Bid / Award Building P	112	26-Oct-16 A	14-Feb-17 A																		
Move Into Swing Space Building M/N from Building P	3	27-Dec-16 A	29-Dec-16 A																		
Construction Building P (Spring 2017 - Fall 2018)	606	14-Feb-17 A	12-Oct-18																		
FF&E / Move Management Building P from M/N (Winter 2019)	265	29-Apr-18 A	18-Jan-19																		
Expected Substantial Completion Building P	0		12-Oct-18																		
Ready to Hold Classes Building P (Spring 2019)	0		25-Jan-19																		
<b>Building J - Auditorium</b>																					
Design Building J	176	01-Oct-15 A	24-Mar-16 A																		
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A																		
DSA Building J	398	03-Sep-16 A	06-Oct-17 A																		
Bid / Award Swing Space for Building J	91	01-Mar-17 A	31-May-17 A																		
Construction Swing Space for Building J	56	01-Jun-17 A	26-Jul-17 A																		
Shelving Install Building O2 & Building FF (AlleyCat)	4	10-Jul-17 A	13-Jul-17 A																		
Move Into Swing Space Building FF & O2 from Building J (Summer 2017)	5	20-Jul-17 A	24-Jul-17 A																		
Bid / Award Building J	77	07-Oct-17 A	22-Dec-17 A																		
Construction Building J (Spring 2018 - Summer 2019)	520	16-Jan-18 A	19-Jun-19																		
FF&E / Move Management Building J from Public Theater & Building FF	242	21-May-19	17-Jan-20																		
Expected Substantial Completion Building J	0		19-Jun-19																		
Ready to Hold Classes Building J (Spring 2020)	0		17-Jan-20																		
<b>Building O1 - Data Center MEP Upgrade</b>																					
Bid / Award Building O1 - Data Center MEP Upgrade	132	30-Nov-17 A	11-Apr-18 A																		
Construction	201	14-Apr-18 A	31-Oct-18																		
Expected Substantial Completion	0		31-Oct-18																		
<b>Building T - Emergency Generator</b>																					
Bid / Award Building T - Emergency Generator	173	30-Nov-17 A	22-May-18 A																		
Construction Bldg T- Emergency Generator	200	29-May-18 A	14-Dec-18																		
Expected Substantial Completion	0		14-Dec-18																		

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of October 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	5	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>LAC Site Barrier Removal</b>																						
Design Campus Improvements	557	06-Oct-17 A	15-Apr-19	Design Campus Improvements																		
DSA Review ADA	182	16-Apr-19	14-Oct-19	DSA Review ADA																		
Bid / Award ADA	90	15-Oct-19	12-Jan-20	Bid / Award ADA																		
Construction LAC Site Barrier Removal	365	21-Jan-20	19-Jan-21	Construction LAC Site Barrier Removal																		
Expected Substantial Completion	0		19-Jan-21	Expected Substantial Completion																		
<b>LAC Building Barrier Removal</b>																						
Design Campus Improvements	634	06-Oct-17 A	01-Jul-19	Design Campus Improvements																		
DSA Review ADA	189	02-Jul-19	06-Jan-20	DSA Review ADA																		
Bid / Award ADA	90	07-Jan-20	05-Apr-20	Bid / Award ADA																		
Construction LAC Building Barrier Removal	545	14-Apr-20	10-Oct-21	Construction LAC Building Barrier Removal																		
Expected Substantial Completion	0		10-Oct-21	Expected Substantial Completion																		
<b>Building X - Central Plant Expansion</b>																						
Design	324	23-Jan-18 A	12-Dec-18	Design																		
DSA	208	15-Dec-18	10-Jul-19	DSA																		
Bid / Award	85	11-Jul-19	03-Oct-19	Bid / Award																		
Submittals and Approvals	42	10-Oct-19	21-Nov-19	Submittals and Approvals																		
Procurement	42	21-Nov-19	02-Jan-20	Procurement																		
Construction LAC Central Plant	127	02-Jan-20	07-May-20	Construction LAC Central Plant																		
Expected Substantial Completion	0		07-May-20	Expected Substantial Completion																		
<b>Kinesiology Labs &amp; Aquatics Center</b>																						
Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A	Pre-Design Kinesiology Labs & Aquatic Center																		
Design Kinesiology Labs & Aquatic Center	620	01-Jun-17 A	10-Feb-19	Design Kinesiology Labs & Aquatic Center																		
DSA Kinesiology Labs & Aquatic Center	172	10-Feb-19	31-Jul-19	DSA Kinesiology Labs & Aquatic Center																		
Bid / Award Kinesiology Labs & Aquatic Center	98	01-Aug-19	06-Nov-19	Bid / Award Kinesiology Labs & Aquatic Center																		
Construction Kinesiology Labs & Aquatic Center	530	07-Nov-19	19-Apr-21	Construction Kinesiology Labs & Aquatic Center																		
NTP Kinesiology Labs & Aquatic Center	0	13-Nov-19		NTP Kinesiology Labs & Aquatic Center																		
FF&E / Move Management Kinesiology Labs & Aquatic Center	194	20-Jan-21	01-Aug-21	FF&E / Move Management Kinesiology Labs & Aquatic Center																		
Expected Substantial Completion Kinesiology Labs & Aquatic Center	0		19-Apr-21	Expected Substantial Completion Kinesiology Labs & Aquatic Center																		
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Fall 2021)	0		01-Aug-21	Ready to Hold Classes Kinesiology Labs & Aquatic Center (Fall 2021)																		
<b>Building M - Liberal Arts</b>																						
Pre-Design Building M	294	01-Aug-17 A	22-May-18 A	Pre-Design Building M																		
Award DBE Building M	99	27-Jun-18 A	03-Oct-18	Award DBE Building M																		
Design and DSA Review Building M	591	15-Oct-18	27-May-20	Design and DSA Review Building M																		
Construction Swing Space Building B Demo	60	12-Dec-18	09-Feb-19	Construction Swing Space Building B Demo																		
Construction Swing Space Building B Renovation 1st Floor & Non-Occupied Rooms	90	06-Apr-19	04-Jul-19	Construction Swing Space Building B Renovation 1st Floor & Non-Occupied Rooms																		
Construction Swing Space Portable Building Lot A	90	06-Apr-19	04-Jul-19	Construction Swing Space Portable Building Lot A																		
Construction Swing Space Building B Renovation 2nd Floor & 3rd Floor	30	08-Jun-19*	07-Jul-19	Construction Swing Space Building B Renovation 2nd Floor & 3rd Floor																		
Move Into Swing Spaces from Building M (Summer 2019)	20	25-Jul-19*	13-Aug-19	Move Into Swing Spaces from Building M (Summer 2019)																		
NTP Construction Building M	0	28-May-20		NTP Construction Building M																		
Construction Building M	596	28-May-20	13-Jan-22	Construction Building M																		
Expected Substantial Completion Building M	0		13-Jan-22	Expected Substantial Completion Building M																		
FF&E / Move Management from Building B to Building M	194	14-Jan-22	26-Jul-22	FF&E / Move Management from Building B to Building M																		
Ready to Hold Classes Building M (Fall 2022)	0		26-Jul-22	Ready to Hold Classes Building M (Fall 2022)																		
<b>Building E - College Center</b>																						
Design Building E	432	03-Oct-20	08-Dec-21	Design Building E																		
DSA Review Swing Space for Building E	280	16-Sep-21	22-Jun-22	DSA Review Swing Space for Building E																		

█ PRE    █ Bid / Award    █ CONST    █ Actual  
█ DESIGN    █ DSA    █ FF&E    ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of October 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	5	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
DSA Review Building E	280	09-Dec-21	14-Sep-22																			
Bid / Award Swing Space for Building E	93	23-Jun-22	23-Sep-22																			
Bid / Award Building E	91	15-Sep-22	14-Dec-22																			
Construction Swing Space for Building E	75	24-Sep-22	07-Dec-22																			
Expected Substantial Completion Swing Space for Building E	0		08-Nov-22																			
Move Into Swing Space Building B from Building E	30	08-Dec-22	06-Jan-23																			
NTP	0	12-Jan-23																				
Construction Building E	610	12-Jan-23	12-Sep-24																			
FF&E / Move Management Building E from Building B	206	15-Jun-24	06-Jan-25																			
Expected Substantial Completion	0		12-Sep-24																			
Ready to Hold Classes Building E (Spring 2025)	0		06-Jan-25																			
<b>Building O2 - Economic &amp; Workforce Development/Foundation</b>																						
Pre-Design Building O2	180	14-Apr-23*	10-Oct-23																			
Design Building O2	280	11-Oct-23	16-Jul-24																			
DSA Review Building O2	280	17-Jul-24	22-Apr-25																			
Construction Swing Space Building O2	40	23-Apr-25	01-Jun-25																			
Bid / Award Building O2	90	23-Apr-25	21-Jul-25																			
Expected Substantial Completion Swing Space Building O2	0		01-Jun-25																			
Move Into Swing Space Building B from Building O2	20	22-Jun-25	11-Jul-25																			
NTP Construction Building O2	0	27-Jul-25																				
Construction Building O2	520	27-Jul-25	28-Dec-26																			
FF&E / Move Management from Building B to Building O2	209	09-Dec-26	05-Jul-27																			
Expected Substantial Completion Building O2	0		28-Dec-26																			
<b>Building G - Music</b>																						
Pre-Design Building G	216	04-Aug-25*	07-Mar-26																			
Design Building G	273	08-Mar-26	05-Dec-26																			
DSA Review Building G	280	06-Dec-26	11-Sep-27																			
Design Swing Space for Building G	67	01-Jun-27	06-Aug-27																			
Bid / Award Swing Space for Building G	89	07-Aug-27	03-Nov-27																			
Bid / Award Building G	90	12-Sep-27	10-Dec-27																			
Construction Swing Space Building for G	40	04-Nov-27	13-Dec-27																			
Expected Substantial Completion Swing Space Building for G	0		13-Dec-27																			
Move Into Swing Space Building B from Building G	15	14-Dec-27	28-Dec-27																			
Construction Building G	750	29-Dec-27	16-Jan-30																			
Expected Substantial Completion Building G	0		16-Jan-30																			
FF&E / Move Management Building G from Building B	162	17-Jan-30	27-Jun-30																			
Ready to Hold Classes Building G	0		27-Jun-30																			
<b>Building H - Theater Arts</b>																						
Pre-Design Building H	217	04-Aug-25*	08-Mar-26																			
Design Building H	273	09-Mar-26	06-Dec-26																			
DSA Review Building H	280	07-Dec-26	12-Sep-27																			
Bid / Award Building H	92	13-Sep-27	13-Dec-27																			
Move Into Public Theater from Building H	20	14-Dec-27	02-Jan-28																			
Construction Building H	750	29-Dec-27	16-Jan-30																			
Expected Substantial Completion	0		16-Jan-30																			
FF&E / Move Management Building H from Building Public Theater	146	17-Jan-30	11-Jun-30																			
Ready to Hold Classes Building H	0		11-Jun-30																			




■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of October 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	?
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>Building K - Art</b>																					
Pre-Design Building K	210	06-Aug-28*	03-Mar-29																		
Design Building K	224	04-Mar-29	13-Oct-29																		
DSA Review Building K	280	14-Oct-29	20-Jul-30																		
Bid / Award Building K	90	21-Jul-30	18-Oct-30																		
Move Into Swing Space Building B from Building K	10	19-Dec-30	28-Dec-30																		
NTP Construction Building K	0	29-Dec-30																			
Construction Building K	390	29-Dec-30	22-Jan-32																		
FF&E / Move Management Building K from Building B	251	25-Oct-31	01-Jul-32																		
Expected Substantial Completion Building K	0		22-Jan-32																		
Ready to Hold Classes Building K (Fall 2032)	0		01-Jul-32																		
<b>Building R - Primary Gymnasium</b>																					
Pre-Design Building R	145	08-Jul-29*	29-Nov-29																		
Design Building R	363	30-Nov-29	27-Nov-30																		
DSA Review Building R	280	28-Nov-30	03-Sep-31																		
Bid / Award Building R	90	04-Sep-31	02-Dec-31																		
NTP Construction Building R	0	08-Dec-31																			
Construction Building R	730	08-Dec-31	06-Dec-33																		
FF&E / Move Management Building R	180	10-Jul-33	05-Jan-34																		
Expected Substantial Completion Building R	0		06-Dec-33																		
Ready to Hold Classes Building R (Spring 2034)	0		05-Jan-34																		
<b>Building Q - Secondary Gymnasium</b>																					
Pre-Design Building	320	16-Jun-31*	30-Apr-32																		
Design Building	246	01-May-32	01-Jan-33																		
DSA Review Building	280	02-Jan-33	08-Oct-33																		
Bid / Award Building	90	09-Oct-33	06-Jan-34																		
NTP Construction Building	0	12-Jan-34																			
Construction Building	640	12-Jan-34	13-Oct-35																		
FF&E / Move Management Building Q	202	16-Jun-35	03-Jan-36																		
Expected Substantial Completion Building	0		13-Oct-35																		
Ready to Hold Classes Building (Spring 2036)	0		03-Jan-36																		
<b>Building B - Tech Studies</b>																					
Pre-Design Building	200	18-Aug-32*	05-Mar-33																		
Design Building	276	06-Mar-33	06-Dec-33																		
DSA Review Building	280	07-Dec-33	12-Sep-34																		
Bid / Award Building	95	13-Sep-34	16-Dec-34																		
NTP Construction Building	0	17-Dec-34																			
Construction Building	730	04-Jan-35	02-Jan-37																		
Expected Substantial Completion Building	0		02-Jan-37																		
<b>Building F - Demo Family/Consumer Education/New Courtyard</b>																					
Design Building F	245	03-Mar-35*	02-Nov-35																		
DSA Review Building F	160	03-Nov-35	10-Apr-36																		
Bid / Award Building F	55	11-Apr-36	04-Jun-36																		
Move Into Building B from Building F	180	03-Jan-37	01-Jul-37																		
Demo & Courtyard Building F	365	02-Jul-37	01-Jul-38																		
<b>Building O1 - IITS/ Warehouse</b>																					
Pre-Design Building	183	02-May-35*	31-Oct-35																		

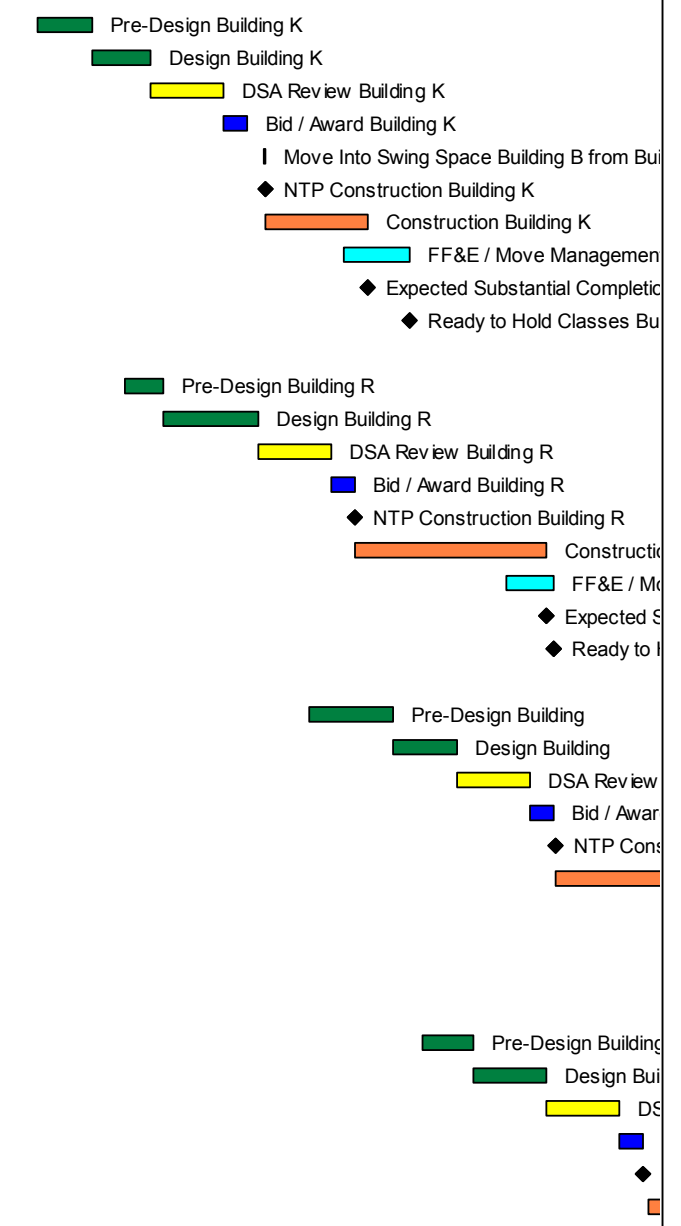

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of October 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	5
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>Design Building</b>	244	01-Nov-35	01-Jul-36																		
<b>DSA Review Building</b>	280	02-Jul-36	07-Apr-37																		
<b>Bid / Award Building</b>	90	08-Apr-37	06-Jul-37																		
<b>NTP Construction Building</b>	0	12-Jul-37																			
<b>Construction Building O1</b>	420	12-Jul-37	04-Sep-38																		
<b>FF&amp;E / Move Management Building O1 from Building O2</b>	213	08-May-38	06-Dec-38																		
<b>Expected Substantial Completion Building O1</b>	0		04-Sep-38																		
<b>Building S - Stadium</b>																					
<b>Pre-Design Building</b>	200	01-May-35*	16-Nov-35																		
<b>Design Building</b>	365	22-Nov-35	20-Nov-36																		
<b>DSA Review Building S</b>	280	21-Nov-36	27-Aug-37																		
<b>Bid / Award Building S</b>	90	28-Aug-37	25-Nov-37																		
<b>Construction Swing Space Building for S</b>	90	28-Aug-37	25-Nov-37																		
<b>Expected Substantial Completion Swing Space Building for S</b>	0		25-Nov-37																		
<b>Move Into Swing Space Building TBD from Building S</b>	15	06-Dec-37	20-Dec-37																		
<b>NTP Construction Building S</b>	0	21-Dec-37																			
<b>Construction Building S</b>	700	21-Dec-37	20-Nov-39																		
<b>FF&amp;E / Move Management Building from Building TBD to Building S</b>	250	24-Jul-39	29-Mar-40																		
<b>Expected Substantial Completion Building S</b>	0		20-Nov-39																		
<b>Punchlist Building S</b>	30	21-Nov-39	20-Dec-39																		
<b>Ready to Hold Classes Building S</b>	0		29-Mar-40																		
<b>Building CDC - Child Development Center</b>																					
<b>Pre-Design Building</b>	49	01-Jun-37*	19-Jul-37																		
<b>Design Building</b>	154	20-Jul-37	20-Dec-37																		
<b>DSA Review Building</b>	280	21-Dec-37	26-Sep-38																		
<b>Bid / Award Building</b>	90	27-Sep-38	25-Dec-38																		
<b>NTP Construction Building</b>	0	26-Dec-38																			
<b>Construction Building</b>	290	26-Dec-38	11-Oct-39																		
<b>FF&amp;E / Move Management</b>	201	13-Jun-39	30-Dec-39																		
<b>Expected Substantial Completion Building</b>	0		11-Sep-39																		
<b>LAC Walkway and Wayfindings</b>																					
<b>Pre-Design</b>	49	01-Feb-17 A	21-Mar-17 A																		
<b>Design</b>	154	22-Mar-17 A	22-Aug-17 A																		
<b>DSA Review</b>	280	23-Aug-17 A	29-May-18 A																		
<b>Bid / Award</b>	90	30-May-18 A	27-Aug-18 A																		
<b>NTP Construction</b>	0	28-Aug-18 A																			
<b>Construction</b>	2664	28-Aug-18 A	12-Dec-25																		
<b>Expected Substantial Completion</b>	0		12-Nov-25																		
<b>Pacific Coast Campus</b>																					
<b>PCC Site Barrier Removal</b>																					
<b>Bid / Award ADA -Site Barrier Removal</b>	99	30-Nov-17 A	09-Mar-18 A																		
<b>Construction - Phase 0</b>	38	26-Mar-18 A	03-May-18 A																		
<b>Construction - Phase 1-A</b>	57	04-May-18 A	30-Jun-18 A																		
<b>Construction - Phase 1-B</b>	65	08-May-18 A	12-Jul-18 A																		
<b>Construction - Phase 2</b>	146	08-Jun-18 A	31-Oct-18																		
<b>Construction - Phase 3-B</b>	16	07-Aug-18 A	23-Aug-18 A																		

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of October 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	5	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Construction - Phase 3-A	33	10-Sep-18 A	12-Oct-18	■ Construction - Phase 3-A																		
Expected Substantial Completion All Phases	0		12-Oct-18	◆ Expected Substantial Completion All Phases																		
<b>PCC Building Barrier Removal</b>																						
Bid / Award Building Barrier Removal	117	20-Feb-18 A	17-Jun-18 A	■																		
Construction - Phase 0	69	24-Jul-18 A	01-Oct-18 A	■																		
Construction - Phase 1-A	130	10-Sep-18 A	17-Jan-19	■ Construction - Phase 1-A																		
Construction - Phase 1-B	242	10-Sep-18 A	09-May-19	■ Construction - Phase 1-B																		
Construction - Phase 2	112	18-Jan-19	09-May-19	■ Construction - Phase 2																		
Construction - Phase 3	60	10-May-19	08-Jul-19	■ Construction - Phase 3																		
Construction - Phase 4	35	09-Jul-19	12-Aug-19	■ Construction - Phase 4																		
Expected Substantial Completion All Phases	0		12-Aug-19	◆ Expected Substantial Completion All Phases																		
<b>Building P2 - PCC Parking Structure</b>																						
Pre-Design Building P2 Parking Structure	456	11-Jan-17 A	11-Apr-18 A	■																		
Award DBE Parking Structure	61	12-Apr-18 A	11-Jun-18 A	■																		
Design Parking Structure	175	16-Jul-18 A	06-Jan-19	■ Design Parking Structure																		
Move into Swing Space from Foster Kinship	21	17-Dec-18*	06-Jan-19	■ Move into Swing Space from Foster Kinship																		
DSA Review Parking Structure	140	17-Jan-19	05-Jun-19	■ DSA Review Parking Structure																		
NTP Construction Parking Structure	0	08-Jul-19		◆ NTP Construction Parking Structure																		
Construction Parking Structure	400	08-Jul-19	10-Aug-20	■ Construction Parking Structure																		
Expected Substantial Completion Parking Structure	0		10-Aug-20	◆ Expected Substantial Completion Parking Structure																		
Closeout Parking Structure	30	11-Aug-20	09-Sep-20	■ Closeout Parking Structure																		
<b>Building MM - Construction Trades Ph 1</b>																						
Design Building MM Ph 1	499	12-Sep-17 A	23-Jan-19	■ Design Building MM Ph 1																		
Design Swing Space for Building MM Ph 1	154	01-Nov-18	03-Apr-19	■ Design Swing Space for Building MM Ph 1																		
DSA Review Building MM Ph 1	260	07-Jan-19	23-Sep-19	■ DSA Review Building MM Ph 1																		
Bid/Award Swing Space Building for MM Ph 1	90	03-Jul-19	30-Sep-19	■ Bid/Award Swing Space Building for MM Ph 1																		
Bid / Award Building MM Ph 1	142	24-Sep-19	12-Feb-20	■ Bid / Award Building MM Ph 1																		
Construction Swing Space Building for MM Ph 1	40	01-Oct-19	09-Nov-19	■ Construction Swing Space Building for MM Ph 1																		
Expected Substantial Completion Swing Space Building for MM Ph 1	0		09-Nov-19	◆ Expected Substantial Completion Swing Space Building for MM Ph 1																		
Move Into Swing Space Building MM from Building MM Ph 1	15	17-Dec-19*	31-Dec-19	■ Move Into Swing Space Building MM from Building MM Ph 1																		
Construction Building MM Ph 1	420	13-Feb-20	07-Apr-21	■ Construction Building MM Ph 1																		
FF&E / Move Management Building MM from Building MM Ph 1	194	13-Jan-21	25-Jul-21	■ FF&E / Move Management Building MM from Building MM Ph 1																		
Expected Substantial Completion Building MM Ph 1	0		07-Apr-21	◆ Expected Substantial Completion Building MM Ph 1																		
Ready to Hold Classes Building MM Ph 1 (Fall 2021)	0		25-Jul-21	◆ Ready to Hold Classes Building MM Ph 1 (Fall 2021)																		
<b>Building MM - Construction Trades Ph 2</b>																						
Design Building MM Ph 2	454	01-Sep-19	27-Nov-20	■ Design Building MM Ph 2																		
DSA Review Building MM Ph 2	280	28-Nov-20	03-Sep-21	■ DSA Review Building MM Ph 2																		
Design Swing Space for Building MM Ph 2	189	16-Dec-20	22-Jun-21	■ Design Swing Space for Building MM Ph 2																		
Bid/Award Swing Space Building for MM Ph 2	90	23-Jun-21	20-Sep-21	■ Bid/Award Swing Space Building for MM Ph 2																		
Bid / Award Building Building MM Ph 2	90	04-Sep-21	02-Dec-21	■ Bid / Award Building Building MM Ph 2																		
Construction Swing Space Building for MM Ph 2	21	21-Sep-21	11-Oct-21	■ Construction Swing Space Building for MM Ph 2																		
Expected Substantial Completion Swing Space Building for MM Ph 2	0		11-Oct-21	◆ Expected Substantial Completion Swing Space Building for MM Ph 2																		
Move Into Swing Space Building MM from Building MM Ph 2	10	20-Dec-21*	29-Dec-21	■ Move Into Swing Space Building MM from Building MM Ph 2																		
Construction Building MM Ph 2	390	09-Jan-22	02-Feb-23	■ Construction Building MM Ph 2																		
FF&E / Move Management Building MM from Building MM Ph 2	199	05-Nov-22	22-May-23	■ FF&E / Move Management Building MM from Building MM Ph 2																		
Expected Substantial Completion Building MM Ph 2	0		02-Feb-23	◆ Expected Substantial Completion Building MM Ph 2																		
Ready to Hold Classes Building MM Ph 2 (Fall 2023)	0		30-Jun-23	◆ Ready to Hold Classes Building MM Ph 2 (Fall 2023)																		

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of October 1, 2018

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	5	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>Building OO - Humanities</b>																						
Design Building Humanities	608	01-Oct-19*	30-May-21																			
DSA Review Building Humanities	280	31-May-21	06-Mar-22																			
Bid / Award Building Humanities	90	07-Mar-22	04-Jun-22																			
NTP Construction Building Humanities	0		09-Jun-22																			
Construction Building Humanities	770	10-Jun-22	18-Jul-24																			
FF&E / Move Management Building Humanities from Building Humanities	270	10-Apr-24	04-Jan-25																			
Expected Substantial Completion Building Humanities	0		18-Jul-24																			
Ready to Hold Classes Building Humanities (Spring 2025)	0		04-Jan-25																			
<b>Building FF - Demo Fine Arts &amp; Senior Center/Turnabout</b>																						
Design Building FF Demo & Turnabout	189	01-Sep-22	08-Mar-23																			
DSA Review Building FF	280	09-Mar-23	13-Dec-23																			
Bid / Award Building FF Demo & Turnabout	86	14-Dec-23	08-Mar-24																			
Construction Building FF Demo	155	09-Mar-24	10-Aug-24																			
<b>PCC Walkways &amp; Wayfinding</b>																						
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41																			
<b>District Wide</b>																						
<b>Joint Use Facility w/ LBUSD &amp; CSULB #12</b>																						
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21																			
<b>Energy/Water Conservation Projects</b>																						
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41																			
<b>Technology Refresh/Replacement</b>																						
Technology Refresh/Replacement	8923	01-Feb-17 A	07-Jul-41																			
<b>Enterprise Wide Computer System</b>																						
Enterprise Wide Computer System	8923	01-Feb-17 A	07-Jul-41																			
<b>Landscaping</b>																						
Landscaping	8923	01-Feb-17 A	07-Jul-41																			
<b>Infrastructure Projectss</b>																						
Infrastructure Projects	8923	01-Feb-17 A	07-Jul-41																			
<b>Minor Campus Improvements</b>																						
Minor Campus Improvements	8923	01-Feb-17 A	07-Jul-41																			
<b>Surface Parking Improvements</b>																						
Surface Parking Improvements	8923	01-Feb-17 A	07-Jul-41																			

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone
