



# LBCC Bond Program Master Schedule

Status as of December 1, 2017

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q

## Long Beach Community College Bond Program Schedule - December 1, 2017

### Liberal Arts Campus

#### Building D - Science

FF&E / Move Management Building D	762	30-Dec-16 A	30-Jan-19
Construction Building D (Fall 2016 - Fall 2018)	353	01-Dec-17	18-Nov-18
Expected Substantial Completion Phase 2	0		10-May-18
Expected Substantial Completion Phase 1	0		10-May-18
Expected Substantial Completion Phase 3	0		03-Aug-18
Ready to Hold Classes Building D 1st Floor (Fall 2018)	0		13-Aug-18
Expected Substantial Completion Phase 4	0		28-Oct-18
Ready to Hold Classes Building D 2nd Floor (Spring 2019)	0		31-Jan-19

- FF&E / Move Management Building D
- Construction Building D (Fall 2016 - Fall 2018)
- ◆ Expected Substantial Completion Phase 2
- ◆ Expected Substantial Completion Phase 1
- ◆ Expected Substantial Completion Phase 3
- ◆ Ready to Hold Classes Building D 1st Floor (Fall 2018)
- ◆ Expected Substantial Completion Phase 4
- ◆ Ready to Hold Classes Building D 2nd Floor (Spring 2019)

#### Building P - Language Arts

Design Building P	239	22-Apr-15 A	17-Dec-15 A
Design Swing Space for Building P	67	01-Aug-15 A	06-Oct-15 A
DSA Building P	280	12-Jan-16 A	17-Oct-16 A
Award Swing Space Building P	65	05-May-16 A	08-Jul-16 A
Bid / Award Building P	112	26-Oct-16 A	14-Feb-17 A
Move Into Swing Space Building M/N from Building P	3	27-Dec-16 A	29-Dec-16 A
Construction Building P (Spring 2017 - Summer 2018)	436	14-Feb-17 A	25-Apr-18
FF&E / Move Management Building P from M/N (Summer 2018)	220	27-Dec-17	03-Aug-18
Expected Contractual Substantial Completion Building P	0		25-Apr-18
Ready to Hold Classes Building P (Fall 2018)	0		03-Aug-18

- Construction Building P (Spring 2017 - Summer 2018)
- FF&E / Move Management Building P from M/N (Summer 2018)
- ◆ Expected Contractual Substantial Completion Building P
- ◆ Ready to Hold Classes Building P (Fall 2018)

#### Building J - Auditorium

Design Building J	176	01-Oct-15 A	24-Mar-16 A
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A
DSA Building J	398	03-Sep-16 A	06-Oct-17 A
Bid / Award Swing Space for Building J	91	01-Mar-17 A	31-May-17 A
Construction Swing Space for Building J	56	01-Jun-17 A	26-Jul-17 A
Shelving Install Building O2 & Building FF (AlleyCat)	4	10-Jul-17 A	13-Jul-17 A
Move Into Swing Space Building FF & O2 from Building J (Summer 2017)	5	20-Jul-17 A	24-Jul-17 A
Bid / Award Building J	94	07-Oct-17 A	08-Jan-18
Construction Building J (Spring 2018 - Summer 2019)	550	17-Jan-18	20-Jul-19
FF&E / Move Management Building J from Public Theater & Building FF	250	22-May-19	26-Jan-20
Expected Substantial Completion Building J	0		21-Jun-19
Ready to Hold Classes Building J (Spring 2020)	0		26-Jan-20

- Bid / Award Building J
- Construction Building J (Spring 2018 - Summer 2019)
- FF&E / Move Management Building J from Public Theater & Building FF
- ◆ Expected Substantial Completion Building J
- ◆ Ready to Hold Classes Building J (Spring 2020)

#### Kinesiology Labs & Aquatics Center

Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A
Design Kinesiology Labs & Aquatic Center	482	01-Jun-17 A	25-Sep-18
DSA Kinesiology Labs & Aquatic Center	266	29-Sep-18	21-Jun-19
Bid / Award Kinesiology Labs & Aquatic Center	106	22-Jun-19	05-Oct-19
Construction Kinesiology Labs & Aquatic Center	560	08-Oct-19	19-Apr-21
FF&E / Move Management Kinesiology Labs & Aquatic Center	215	21-Dec-20	23-Jul-21
Expected Substantial Completion Kinesiology Labs & Aquatic Center	0		21-Mar-21
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Fall 2021)	0		23-Jul-21

- Design Kinesiology Labs & Aquatic Center
- DSA Kinesiology Labs & Aquatic Center
- Bid / Award Kinesiology Labs & Aquatic Center
- Construction Kinesiology Labs & Aquatic Center
- FF&E / Move Management Kinesiology Labs & Aquatic Center
- ◆ Expected Substantial Completion Kinesiology Labs & Aquatic Center
- ◆ Ready to Hold Classes Kinesiology Labs & Aquatic Center (Fall 2021)

#### Building M - Liberal Arts

Pre-Design Building M	201	30-Oct-17 A	18-May-18
Design Swing Space Building M	120	15-Dec-17	13-Apr-18

- Pre-Design Building M
- Design Swing Space Building M

PRE	Bid / Award	CONST	Actual
DESIGN	DSA	FF&E	◆ Milestone



# LBCC Bond Program Master Schedule

Status as of December 1, 2017

Activity Name	At Completion Duration	Start	Finish	Timeline																														
				2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035													
DSA Swing Space Building M	240	14-Apr-18	09-Dec-18	[Gantt chart for DSA Swing Space Building M]																														
Award DBE Building M	95	19-May-18	21-Aug-18	[Gantt chart for Award DBE Building M]																														
Design Building M	266	22-Aug-18	14-May-19	[Gantt chart for Design Building M]																														
Bid Swing Space Building M	90	10-Dec-18	09-Mar-19	[Gantt chart for Bid Swing Space Building M]																														
Construction Swing Space Building M	90	10-Mar-19	07-Jun-19	[Gantt chart for Construction Swing Space Building M]																														
DSA Review Building M	280	15-May-19	18-Feb-20	[Gantt chart for DSA Review Building M]																														
Expected Substantial Completion Swing Space Building M	0		07-Jun-19	[Milestone for Expected Substantial Completion Swing Space Building M]																														
Move Into Swing Space Building B from Building M (Summer 2019)	20	08-Jul-19*	27-Jul-19	[Gantt chart for Move Into Swing Space Building B from Building M (Summer 2019)]																														
NTP Construction Building M	0	19-Feb-20		[Milestone for NTP Construction Building M]																														
Construction Building M	775	19-Feb-20	03-Apr-22	[Gantt chart for Construction Building M]																														
FF&E / Move Management from Building B to Building M	216	05-Dec-21	08-Jul-22	[Gantt chart for FF&E / Move Management from Building B to Building M]																														
Expected Substantial Completion Building M	0		05-Mar-22	[Milestone for Expected Substantial Completion Building M]																														
Move-In (Summer 2022)	10	17-Jun-22	30-Jun-22	[Gantt chart for Move-In (Summer 2022)]																														
Ready to Hold Classes Building J (Fall 2022)	0		30-Jun-22	[Milestone for Ready to Hold Classes Building J (Fall 2022)]																														
<b>LAC Accessibility Campus Improvements</b>																																		
Design Campus Improvements -TBD Phasing Plan	225	06-Oct-17 A	18-May-18	[Gantt chart for Design Campus Improvements -TBD Phasing Plan]																														
DSA Review ADA	210	19-May-18	14-Dec-18	[Gantt chart for DSA Review ADA]																														
Bid / Award ADA	90	15-Dec-18	14-Mar-19	[Gantt chart for Bid / Award ADA]																														
Construction	504	21-Mar-19	05-Aug-20	[Gantt chart for Construction]																														
Expected Substantial Completion	0		07-Jul-20	[Milestone for Expected Substantial Completion]																														
<b>Building E - College Center</b>																																		
Design Building E	429	03-Oct-20	05-Dec-21	[Gantt chart for Design Building E]																														
DSA Review Swing Space for Building E	280	16-Sep-21	22-Jun-22	[Gantt chart for DSA Review Swing Space for Building E]																														
DSA Review Building E	280	09-Dec-21	14-Sep-22	[Gantt chart for DSA Review Building E]																														
Bid / Award Swing Space for Building E	93	23-Jun-22	23-Sep-22	[Gantt chart for Bid / Award Swing Space for Building E]																														
Bid / Award Building E	92	15-Sep-22	15-Dec-22	[Gantt chart for Bid / Award Building E]																														
Construction Swing Space for Building E	75	24-Sep-22	07-Dec-22	[Gantt chart for Construction Swing Space for Building E]																														
Expected Substantial Completion Swing Space for Building E	0		08-Nov-22	[Milestone for Expected Substantial Completion Swing Space for Building E]																														
Move Into Swing Space Building B from Building E	30	08-Dec-22	06-Jan-23	[Gantt chart for Move Into Swing Space Building B from Building E]																														
Construction Building E	640	12-Jan-23	12-Oct-24	[Gantt chart for Construction Building E]																														
FF&E / Move Management Building E from Building B	206	15-Jun-24	06-Jan-25	[Gantt chart for FF&E / Move Management Building E from Building B]																														
Expected Substantial Completion	0		13-Sep-24	[Milestone for Expected Substantial Completion]																														
Ready to Hold Classes Building E (Spring 2025)	0		06-Jan-25	[Milestone for Ready to Hold Classes Building E (Spring 2025)]																														
<b>Building O2 - Economic &amp; Workforce Development/Foundation</b>																																		
Pre-Design Building O2	180	14-Apr-23*	10-Oct-23	[Gantt chart for Pre-Design Building O2]																														
Design Building O2	280	11-Oct-23	16-Jul-24	[Gantt chart for Design Building O2]																														
DSA Review Building O2	280	17-Jul-24	22-Apr-25	[Gantt chart for DSA Review Building O2]																														
Construction Swing Space Building O2	40	23-Apr-25	01-Jun-25	[Gantt chart for Construction Swing Space Building O2]																														
Bid / Award Building O2	90	23-Apr-25	21-Jul-25	[Gantt chart for Bid / Award Building O2]																														
Expected Substantial Completion Swing Space Building O2	0		01-Jun-25	[Milestone for Expected Substantial Completion Swing Space Building O2]																														
Move Into Swing Space Building B from Building O2	20	22-Jun-25	11-Jul-25	[Gantt chart for Move Into Swing Space Building B from Building O2]																														
NTP Construction Building O2	0	12-Jul-25		[Milestone for NTP Construction Building O2]																														
Construction Building O2	550	22-Jul-25	22-Jan-27	[Gantt chart for Construction Building O2]																														
FF&E / Move Management from Building B to Building O2	209	03-Jan-27	30-Jul-27	[Gantt chart for FF&E / Move Management from Building B to Building O2]																														
Expected Substantial Completion Building O2	0		22-Jan-27	[Milestone for Expected Substantial Completion Building O2]																														
<b>Building G - Music</b>																																		
Pre-Design Building G	216	04-Aug-25*	07-Mar-26	[Gantt chart for Pre-Design Building G]																														


■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of December 1, 2017

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>Building G</b>																					
Design Building G	273	08-Mar-26	05-Dec-26																		
DSA Review Building G	280	06-Dec-26	11-Sep-27																		
Design Swing Space for Building G	67	01-Jun-27	06-Aug-27																		
Bid / Award Swing Space for Building G	90	07-Aug-27	04-Nov-27																		
Bid / Award Building G	90	12-Sep-27	10-Dec-27																		
Construction Swing Space Building for G	40	05-Nov-27	14-Dec-27																		
Expected Substantial Completion Swing Space Building for G	0		14-Dec-27																		
Move Into Swing Space Building B from Building G	15	15-Dec-27	29-Dec-27																		
Construction Building G	780	30-Dec-27	16-Feb-30																		
Expected Substantial Completion Building G	0		18-Jan-30																		
FF&E / Move Management Building G from Building B	162	18-Jan-30	28-Jun-30																		
Ready to Hold Classes Building G	0		28-Jun-30																		
<b>Building H - Theater Arts</b>																					
Pre-Design Building H	217	04-Aug-25*	08-Mar-26																		
Design Building H	273	09-Mar-26	06-Dec-26																		
DSA Review Building H	280	07-Dec-26	12-Sep-27																		
Bid / Award Building H	92	13-Sep-27	13-Dec-27																		
Move Into Public Theater from Building H	20	15-Dec-27	03-Jan-28																		
Construction Building H	780	30-Dec-27	16-Feb-30																		
Expected Substantial Completion	0		18-Jan-30																		
FF&E / Move Management Building H from Building Public Theater	146	18-Jan-30	12-Jun-30																		
Ready to Hold Classes Building H	0		12-Jun-30																		
<b>Building K - Art</b>																					
Pre-Design Building K	210	06-Aug-28*	03-Mar-29																		
Design Building K	224	04-Mar-29	13-Oct-29																		
DSA Review Building K	280	14-Oct-29	20-Jul-30																		
Bid / Award Building K	90	21-Jul-30	18-Oct-30																		
Move Into Swing Space Building B from Building K	10	20-Dec-30	29-Dec-30																		
NTP Construction Building K	0	30-Dec-30																			
Construction Building K	420	30-Dec-30	22-Feb-32																		
FF&E / Move Management Building K from Building B	174	09-Jan-32	30-Jun-32																		
Expected Substantial Completion Building K	0		22-Feb-32																		
Ready to Hold Classes Building K (Fall 2033)	0		30-Jun-32																		
<b>Building R - Primary Gymnasium</b>																					
Pre-Design Building R	145	08-Jul-29*	29-Nov-29																		
Design Building R	363	30-Nov-29	27-Nov-30																		
DSA Review Building R	280	28-Nov-30	03-Sep-31																		
Bid / Award Building R	90	04-Sep-31	02-Dec-31																		
NTP Construction Building R	0	03-Dec-31																			
Construction Building R	760	03-Dec-31	31-Dec-33																		
FF&E / Move Management Building R	180	05-Jul-33	31-Dec-33																		
Expected Substantial Completion Building R	0		31-Dec-33																		
Ready to Hold Classes Building R (Spring 2034)	0		31-Dec-33																		
<b>Building Q - Secondary Gymnasium</b>																					
Pre-Design Building	320	16-Jun-31*	30-Apr-32																		
Design Building	246	01-May-32	01-Jan-33																		
DSA Review Building	280	02-Jan-33	08-Oct-33																		

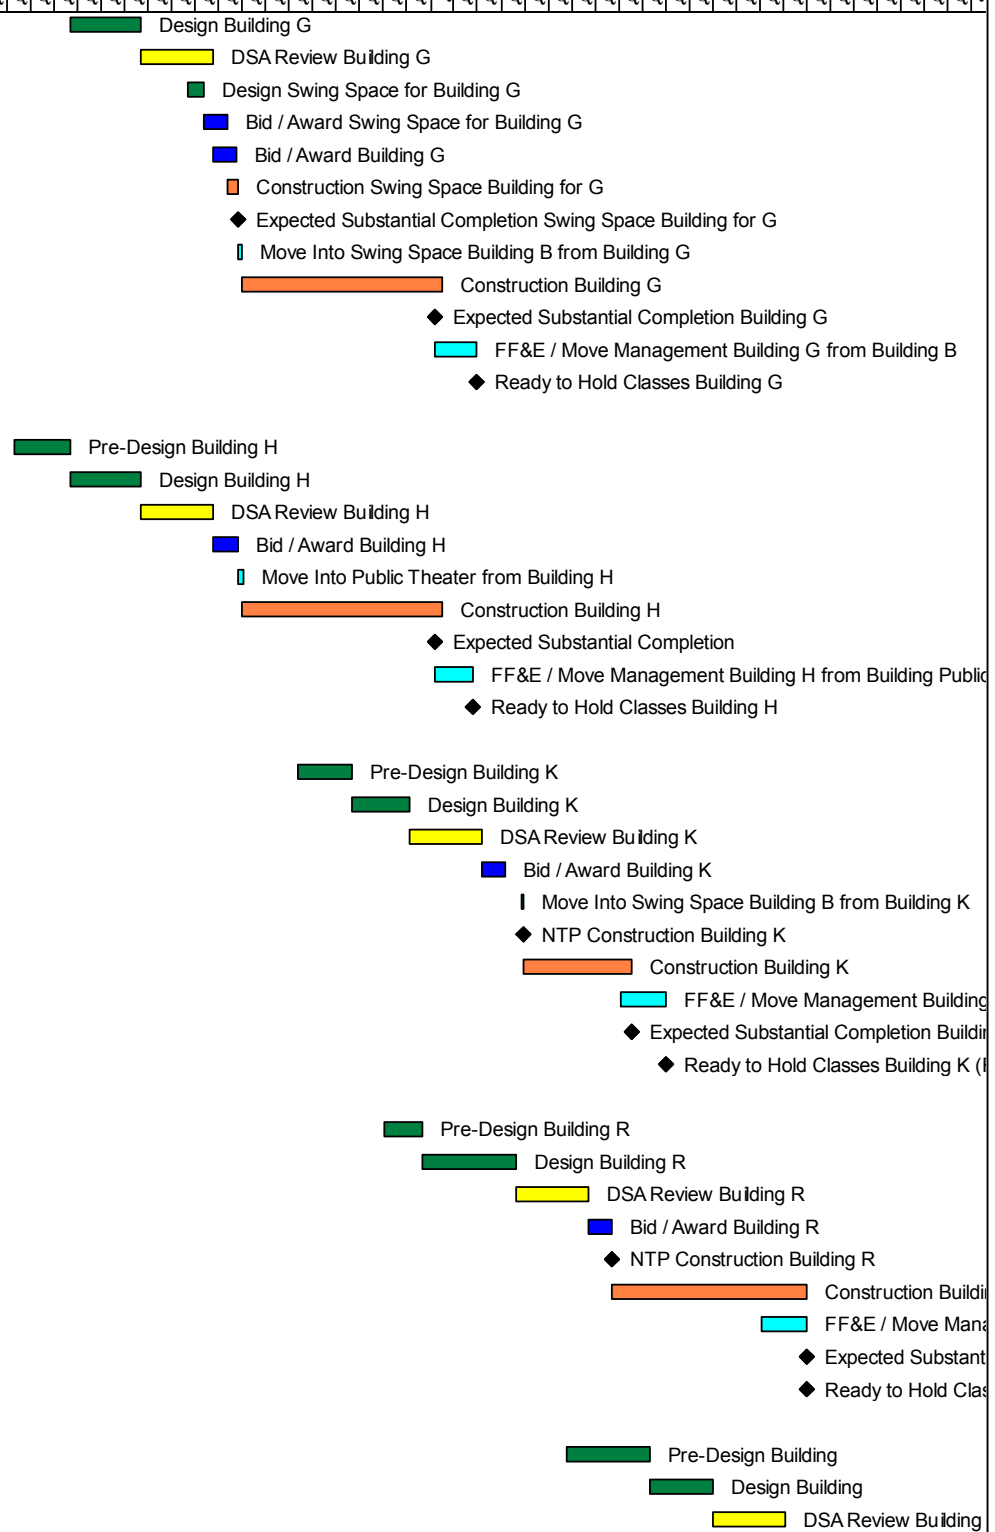

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of December 1, 2017

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Bid / Award Building	90	09-Oct-33	06-Jan-34																				
NTP Construction Building	0	07-Jan-34																					
Construction Building	640	07-Jan-34	08-Oct-35																				
FF&E / Move Management Building Q	202	11-Jun-35	29-Dec-35																				
Expected Substantial Completion Building	0		08-Oct-35																				
Ready to Hold Classes Building (Spring 2036)	0		29-Dec-35																				
<b>Building B - Tech Studies</b>																							
Pre-Design Building	200	18-Aug-32*	05-Mar-33																				
Design Building	276	06-Mar-33	06-Dec-33																				
DSA Review Building	280	07-Dec-33	12-Sep-34																				
Bid / Award Building	95	13-Sep-34	16-Dec-34																				
NTP Construction Building	0	17-Dec-34																					
Construction Building	730	30-Dec-34	28-Dec-36																				
Expected Substantial Completion Building	0		28-Dec-36																				
<b>Building F - Demo Family/Consumer Education/New Courtyard</b>																							
Design Building F	245	03-Mar-35*	02-Nov-35																				
DSA Review Building F	160	03-Nov-35	10-Apr-36																				
Bid / Award Building F	55	11-Apr-36	04-Jun-36																				
Move Into Building B from Building F	180	29-Dec-36	26-Jun-37																				
Demo & Courtyard Building F	365	27-Jun-37	26-Jun-38																				
<b>Building O1 - IITS/ Warehouse</b>																							
Pre-Design Building	183	02-May-35*	31-Oct-35																				
Design Building	244	01-Nov-35	01-Jul-36																				
DSA Review Building	280	02-Jul-36	07-Apr-37																				
Bid / Award Building	90	08-Apr-37	06-Jul-37																				
NTP Construction Building	0	07-Jul-37																					
Construction Building O1	450	07-Jul-37	29-Sep-38																				
FF&E / Move Management Building O1 from Building O2	213	02-Jun-38	31-Dec-38																				
Expected Substantial Completion Building O1	0		29-Sep-38																				
<b>Building S - Stadium</b>																							
Pre-Design Building	200	01-May-35*	16-Nov-35																				
Design Building	365	22-Nov-35	20-Nov-36																				
DSA Review Building S	280	21-Nov-36	27-Aug-37																				
Bid / Award Building S	90	28-Aug-37	25-Nov-37																				
Construction Swing Space Building for S	90	28-Aug-37	25-Nov-37																				
Expected Substantial Completion Swing Space Building for S	0		25-Nov-37																				
Move Into Swing Space Building TBD from Building S	15	06-Dec-37	20-Dec-37																				
NTP Construction Building S	0	21-Dec-37																					
Construction Building S	729	21-Dec-37	19-Dec-39																				
Expected Substantial Completion Building S	0		19-Dec-39																				
FF&E / Move Management Building from Building TBD to Building S	193	20-Dec-39	29-Jun-40																				
Ready to Hold Classes Building S	0		29-Jun-40																				
<b>Building CDC - Child Development Center</b>																							
Pre-Design Building	49	01-Jun-37*	19-Jul-37																				
Design Building	154	20-Jul-37	20-Dec-37																				
DSA Review Building	280	21-Dec-37	26-Sep-38																				
Bid / Award Building	90	27-Sep-38	25-Dec-38																				



■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of December 1, 2017

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
NTP Construction Building	0	26-Dec-38																					
Construction Building	290	26-Dec-38	11-Oct-39																				
FF&E / Move Management	170	14-Jul-39	30-Dec-39																				
Expected Substantial Completion Building	0		11-Oct-39																				
<b>LAC Walkway and Wayfindings</b>																							
Pre-Design	49	01-Feb-17 A	21-Mar-17 A																				
Design	154	22-Mar-17 A	22-Aug-17 A																				
DSA Review	280	23-Aug-17 A	29-May-18																				
Bid / Award	90	30-May-18	27-Aug-18																				
NTP Construction	0	28-Aug-18																					
Construction	2664	28-Aug-18	12-Dec-25																				
Expected Substantial Completion	0		12-Dec-25																				
<b>Pacific Coast Campus</b>																							
<b>PCC Accessibility Improvement</b>																							
Design Campus Improvements	361	01-Oct-16 A	27-Sep-17 A																				
DSA Review ADA - Site	46	28-Sep-17 A	13-Nov-17 A																				
DSA Review ADA - Building	54	12-Oct-17 A	04-Dec-17																				
Bid / Award ADA -Site	110	20-Nov-17 A	09-Mar-18																				
Bid / Award ADA -Building	123	05-Dec-17	06-Apr-18																				
Construction - Site	276	17-Mar-18	17-Dec-18																				
Construction - Building	276	14-Apr-18	14-Jan-19																				
Expected Substantial Completion	0		18-Nov-18																				
Expected Substantial Completion	0		16-Dec-18																				
<b>Building P2 - PCC Parking Structure</b>																							
Pre-Design Building P2 Parking Structure	360	01-Apr-17 A	26-Mar-18																				
Design Swing Space	175	10-Jan-18	03-Jul-18																				
Award DBE Parking Structure	72	27-Mar-18	06-Jun-18																				
Design Parking Structure	175	12-Jun-18	03-Dec-18																				
DSA Over-the-Counter Review PCC Foster Kinship Swing Space	60	20-Jun-18	18-Aug-18																				
Bid Foster Kinship Swing Space	90	19-Aug-18	16-Nov-18																				
Construction Foster Kinship Swing Space	180	17-Nov-18	15-May-19																				
DSA Review Parking Structure	250	04-Dec-18	10-Aug-19																				
Move into Swing Space from Foster Kinship (Summer 2019)	14	17-Jun-19*	30-Jun-19																				
NTP Construction Parking Structure	0	11-Aug-19																					
Construction Parking Structure	365	11-Aug-19	09-Aug-20																				
Expected Substantial Completion Parking Structure	0		09-Aug-20																				
Closeout Parking Structure	90	10-Aug-20	07-Nov-20																				
<b>Building MM - Construction Trades Ph 1</b>																							
Design Building MM	481	12-Sep-17 A	05-Jan-19																				
Design Swing Space for Building MM	98	25-Nov-18	02-Mar-19																				
DSA Review Building MM	280	06-Jan-19	12-Oct-19																				
Bid/Award Swing Space Building for MM	90	27-Jul-19	24-Oct-19																				
Bid / Award Building	90	13-Oct-19	10-Jan-20																				
Construction Swing Space Building for MM	40	25-Oct-19	03-Dec-19																				
Expected Substantial Completion Swing Space Building for MM	0		03-Dec-19																				
Move Into Swing Space Building MM from Building MM	15	17-Dec-19*	31-Dec-19																				
Construction Building MM	450	11-Jan-20	04-Apr-21																				

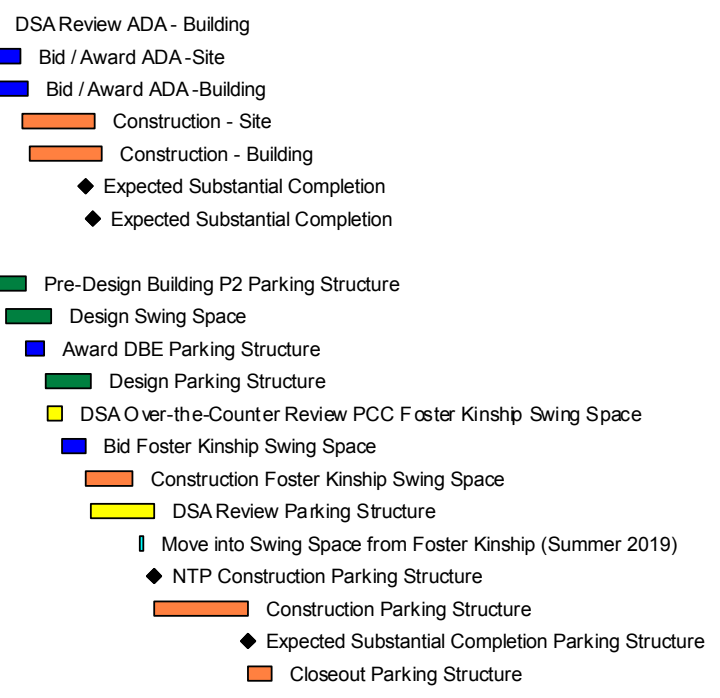



# LBCC Bond Program Master Schedule

Status as of December 1, 2017

Activity Name	At Completion Duration	Start	Finish	Timeline																											
				2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035										
FF&E / Move Management Building MM from Building MM	214	06-Dec-20	07-Jul-21	FF&E / Move Management Building MM from Building MM																											
Expected Substantial Completion Building MM	0		06-Mar-21	◆ Expected Substantial Completion Building MM																											
Ready to Hold Classes Building MM (Fall 2021)	0		07-Jul-21	◆ Ready to Hold Classes Building MM (Fall 2021)																											
<b>Building MM - Construction Trades Ph 2</b>																															
Design Building MM	454	01-May-19	27-Jul-20	Design Building MM																											
Design Swing Space for Building MM	189	16-Jun-20	21-Dec-20	Design Swing Space for Building MM																											
DSA Review Building MM	280	28-Jul-20	03-May-21	DSA Review Building MM																											
Bid/Award Swing Space Building for MM	90	22-Mar-21	19-Jun-21	Bid/Award Swing Space Building for MM																											
Bid / Award Building	90	04-May-21	01-Aug-21	Bid / Award Building																											
Construction Swing Space Building for MM	30	03-Jul-21	01-Aug-21	Construction Swing Space Building for MM																											
Expected Substantial Completion Swing Space Building for MM	0		01-Aug-21	◆ Expected Substantial Completion Swing Space Building for MM																											
Move Into Swing Space Building MM from Building MM	10	02-Aug-21	11-Aug-21	Move Into Swing Space Building MM from Building MM																											
Construction Building MM	422	22-Aug-21	17-Oct-22	Construction Building MM																											
FF&E / Move Management Building MM from Building MM	199	20-Jun-22	04-Jan-23	FF&E / Move Management Building MM from Building MM																											
Expected Substantial Completion Building MM	0		18-Sep-22	◆ Expected Substantial Completion Building MM																											
Ready to Hold Classes Building MM Ph 2 (Spring 2023)	0		04-Jan-23	◆ Ready to Hold Classes Building MM Ph 2 (Spring 2023)																											
<b>Building OO - Humanities</b>																															
Design Building Humanities	608	01-Oct-19*	30-May-21	Design Building Humanities																											
DSA Review Building Humanities	280	31-May-21	06-Mar-22	DSA Review Building Humanities																											
Bid / Award Building Humanities	90	07-Mar-22	04-Jun-22	Bid / Award Building Humanities																											
NTP Construction Building Humanities	0		04-Jun-22	◆ NTP Construction Building Humanities																											
Construction Building Humanities	800	05-Jun-22	12-Aug-24	Construction Building Humanities																											
FF&E / Move Management Building Humanities from Building Humanities	270	05-Apr-24	30-Dec-24	FF&E / Move Management Building Humanities from Building Humanities																											
Expected Substantial Completion Building Humanities	0		14-Jul-24	◆ Expected Substantial Completion Building Humanities																											
Ready to Hold Classes Building Humanities (Spring 2025)	0		30-Dec-24	◆ Ready to Hold Classes Building Humanities (Spring 2025)																											
<b>Building FF - Demo Fine Arts &amp; Senior Center/Turnabout</b>																															
Design Building FF Demo & Turnabout	189	01-Sep-22	08-Mar-23	Design Building FF Demo & Turnabout																											
DSA Review Building FF	280	09-Mar-23	13-Dec-23	DSA Review Building FF																											
Bid / Award Building FF Demo & Turnabout	90	14-Dec-23	12-Mar-24	Bid / Award Building FF Demo & Turnabout																											
Construction Building FF Demo	155	13-Mar-24	14-Aug-24	Construction Building FF Demo																											
<b>PCC Walkways &amp; Wayfinding</b>																															
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41	PCC Walkways and Wayfindings																											
<b>District Wide</b>																															
<b>District Wide Security Monitoring System (Cameras)</b>																															
Design Security Monitoring System	161	01-Oct-15 A	09-Mar-16 A	Design Security Monitoring System																											
DSA Security Monitoring System	140	12-Apr-16 A	30-Aug-16 A	DSA Security Monitoring System																											
Bid Security Monitoring System	57	28-Jul-16 A	22-Sep-16 A	Bid Security Monitoring System																											
Construction Security Monitoring System	462	11-Oct-16 A	15-Jan-18	Construction Security Monitoring System																											
<b>LBCCD Energy Master Plan</b>																															
Benchmarking	61	31-Jul-17 A	30-Sep-17 A	Benchmarking																											
Performance Analysis	63	30-Sep-17 A	01-Dec-17	Performance Analysis																											
Design Recommendations	63	02-Dec-17	02-Feb-18	Design Recommendations																											
Deliverables	63	03-Feb-18	06-Apr-18	Deliverables																											
<b>LBCCD Central Plant Load Study</b>																															
Scope Document	60	31-Jul-17 A	29-Sep-17 A	Scope Document																											
<b>Joint Use Facility w/ LBUSD &amp; CSULB #12</b>																															
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21	Joint Use w/ LBUSD & CSULB #12																											

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ ◆ Milestone



# LBCC Bond Program Master Schedule

Status as of December 1, 2017

Activity Name	At Completion Duration	Start	Finish	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>Energy/Water Conservation Projects</b>																						
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41																			
<b>Technology Refresh/Replacement</b>																						
Technology Refresh/Replacement	8923	01-Feb-17 A	07-Jul-41																			
<b>Enterprise Wide Computer System</b>																						
Enterprise Wide Computer System	8923	01-Feb-17 A	07-Jul-41																			
<b>Landscaping</b>																						
Landscaping	8923	01-Feb-17 A	07-Jul-41																			
<b>Infrastructure Projectss</b>																						
Infrastructure Projects	8923	01-Feb-17 A	07-Jul-41																			
<b>Minor Campus Improvements</b>																						
Minor Campus Improvements	8923	01-Feb-17 A	07-Jul-41																			
<b>Surface Parking Improvements</b>																						
Surface Parking Improvements	8923	01-Feb-17 A	07-Jul-41																			

■ PRE    ■ Bid / Award    ■ CONST    ■ Actual  
■ DESIGN    ■ DSA    ■ FF&E    ◆ Milestone
