


LBCC Bond Program Master Schedule

Status as of April 1, 2020

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Long Beach Community College Bond Program Schedule - April 1, 2020																					
Liberal Arts Campus																					
Building J - Auditorium																					
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A																		
Design Building J	145	01-Nov-15 A	24-Mar-16 A																		
DSA Building J	398	03-Sep-16 A	06-Oct-17 A																		
Bid / Award Building J	89	07-Oct-17 A	04-Jan-18 A																		
Construction Building J (Spring 2018 - Spring 2020)	840	12-Jan-18 A	30-Apr-20																		
FF&E / Move Management from Building J from Public Theater & Building FF	263	24-Nov-19 A	12-Aug-20																		
Expected Substantial Completion Building J	0		30-Apr-20																		
Ready to Hold Classes Building J (Fall 2020)	0		11-Aug-20																		
Kinesiology Labs & Aquatics Center																					
Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A																		
Design Kinesiology Labs & Aquatic Center	615	01-Jun-17 A	06-Feb-19 A																		
DSA Kinesiology Labs & Aquatic Center	241	29-Jan-19 A	26-Sep-19 A																		
Bid / Award Kinesiology Labs & Aquatic Center	138	19-Sep-19 A	03-Feb-20 A																		
NTP Kinesiology Labs & Aquatic Center	0	10-Feb-20 A																			
Phase 2 Softball Complex	360	10-Feb-20 A	03-Feb-21																		
Phase 1 Aquatic Complex & North Fields	530	10-Feb-20 A	23-Jul-21																		
Phase 3 Parking Lot etc.	45	04-Feb-21	20-Mar-21																		
FF&E / Move Management Kinesiology Labs & Aquatic Center	258	25-Apr-21	08-Jan-22																		
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Spring 2022)	0		08-Jan-22																		
Building X - Central Plant Expansion																					
Design	413	23-Jan-18 A	12-Mar-19 A																		
DSA LAC Central Plant	146	13-Apr-19 A	06-Sep-19 A																		
Bid / Award LAC Central Plant	107	19-Aug-19 A	03-Dec-19 A																		
Construction LAC Central Plant Phase 1	155	09-Dec-19 A	11-May-20																		
Construction LAC Central Plant Phase 2	250	09-Dec-19 A	14-Aug-20																		
Expected Substantial Completion Phase 1	0		11-May-20																		
Expected Substantial Completion Phase 2	0		14-Aug-20																		
LAC Site Barrier Removal																					
Design Campus Improvements	924	12-Sep-17 A	23-Mar-20 A																		
DSA Review LAC Site Barrier Removal	183	24-Mar-20 A	22-Sep-20																		
Bid / Award LAC Site Barrier Removal	90	23-Sep-20	21-Dec-20																		
Construction LAC Site Barrier Removal	518	29-Dec-20	30-May-22																		
Expected Substantial Completion	0		30-May-22																		
LAC Building Barrier Removal																					
Design Campus Improvements	952	12-Sep-17 A	20-Apr-20																		
DSA Review LAC Building Barrier Removal	182	21-Apr-20	19-Oct-20																		
Bid / Award LAC Building Barrier Removal	90	20-Oct-20	17-Jan-21																		
Construction LAC Building Barrier Removal	518	04-Feb-21	06-Jul-22																		
Expected Substantial Completion	0		06-Jul-22																		
Building M - Liberal Arts																					
Pre-Design Building M	329	01-Aug-17 A	26-Jun-18 A																		
Award DBE Building M	120	27-Jun-18 A	25-Oct-18 A																		
Design and DSA Review Building M	517	05-Nov-18 A	04-Apr-20																		

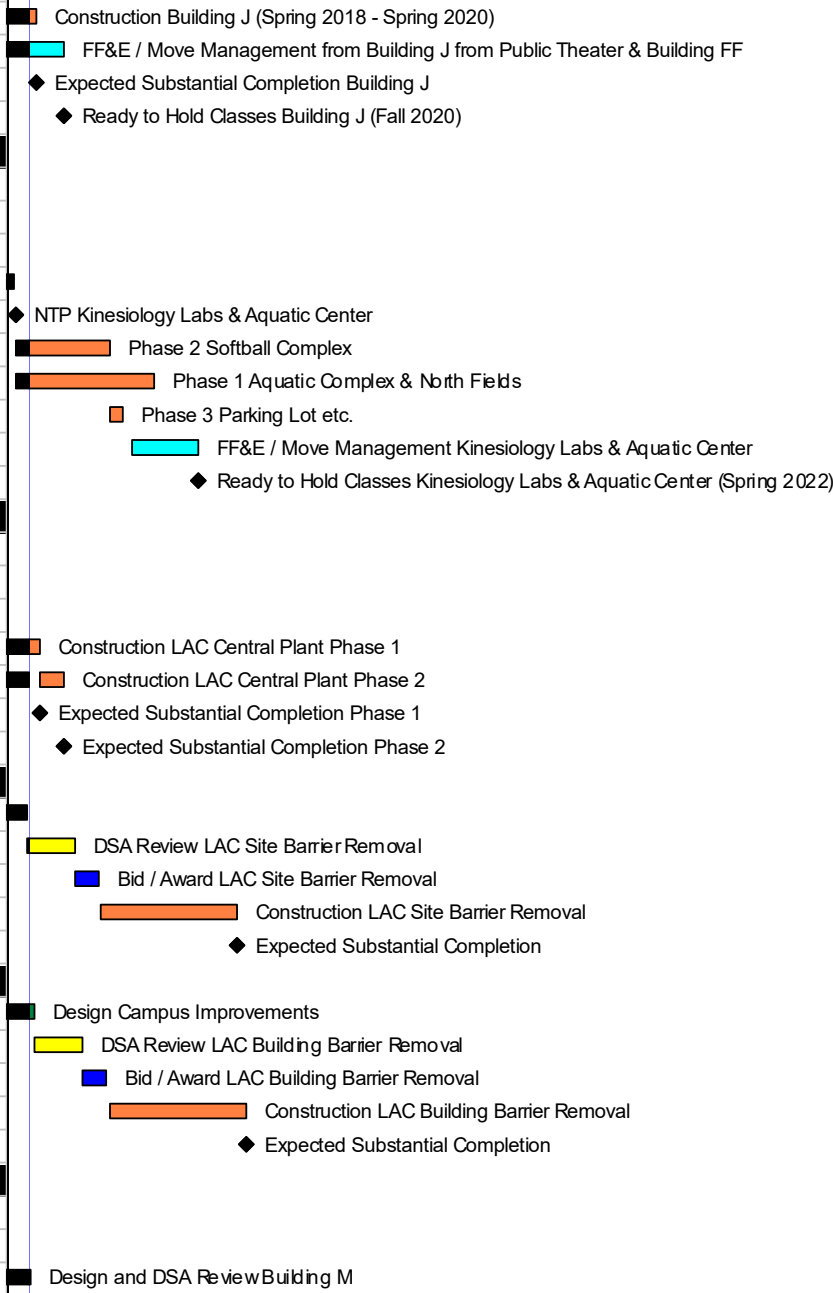

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of April 1, 2020

Activity Name	At Completion Duration	Start	Finish	Timeline (2020-2037)																																	
				2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037																
FF&E / Move Management Swing Spaces Building B for Building M	245	06-Jun-19 A	05-Feb-20 A																																		
Move Into Swing Spaces Bldg B for Building M (Jan 2020)	1	17-Jan-20 A	17-Jan-20 A																																		
Move Into Swing Spaces Portables for Building M (Jan 2020)	1	26-Jan-20 A	26-Jan-20 A																																		
NTP Construction Building M	0	13-Feb-20 A																																			
Construction Building M	625	13-Feb-20 A	29-Oct-21																																		
FF&E / Move Management Building M	274	30-Sep-21	01-Jul-22																																		
Expected Substantial Completion Building M	0		29-Oct-21																																		
Ready to Hold Classes Building M (Fall 2022)	0		01-Jul-22																																		
Building G - Music & Theater Arts																																					
Design Building G/H	354	11-Sep-19 A	29-Aug-20																																		
Design Swing Space for Building G/H	210	07-Nov-19 A	03-Jun-20																																		
DSA Review Building G/H	243	19-Jul-20	18-Mar-21																																		
Approve Working Documents and Proceed to Bid	182	19-Mar-21	16-Sep-21																																		
Bid / Award Swing Space for Building G/H	90	09-Jun-21	06-Sep-21																																		
Construction Swing Space Building for G/H	40	07-Sep-21	16-Oct-21																																		
Bid / Award Building G/H	124	17-Sep-21	18-Jan-22																																		
Expected Substantial Completion Swing Space Building for G/H	0		16-Oct-21																																		
Move Into Swing Space (TBD) for Building G/H (Dec 2021/Jan 2022)	15	20-Dec-21	03-Jan-22																																		
Construction Building G	750	19-Jan-22	07-Feb-24																																		
Expected Substantial Completion Building G	0		07-Feb-24																																		
FF&E / Move Management Building G from Swing Space (TBD)	158	08-Feb-24	14-Jul-24																																		
Ready to Hold Classes Building G (Fall 2024)	0		29-Jun-24																																		
EEM-2A - Energy and Portable Water Reductions - LAC (TBD)																																					
Design EEM-2A	180	01-Apr-21 A	27-Sep-21 A																																		
DSA EEM-2A	260	01-Apr-21*	16-Dec-21																																		
Bid / Award EEM-2A	90	17-Dec-21	16-Mar-22																																		
Construction EEM-2A	365	17-Mar-22	16-Mar-23																																		
EEM-2C - Thermal Storage Strategy - Bldg P Attic (TBD)																																					
Design EEM-2C	180	01-Apr-21 A	27-Sep-21 A																																		
DSA EEM-2C	180	01-Apr-21*	27-Sep-21																																		
Bid / Award EEM-2C	90	28-Sep-21	26-Dec-21																																		
Construction EEM-2C	160	27-Dec-21	04-Jun-22																																		
Building E - College Center																																					
Design Building E	432	03-Aug-20	08-Oct-21																																		
DSA Review Swing Space for Building E	280	17-Jul-21	22-Apr-22																																		
DSA Review Building E	280	09-Oct-21	15-Jul-22																																		
Bid / Award Swing Space for Building E	93	23-Apr-22	24-Jul-22																																		
Bid / Award Building E	91	16-Jul-22	14-Oct-22																																		
Construction Swing Space for Building E	75	25-Jul-22	07-Oct-22																																		
FF&E / Move Management Building B Swing Space for Building E	180	09-Aug-22	04-Feb-23																																		
Expected Substantial Completion Swing Space for Building E	0		07-Oct-22																																		
NTP	0	20-Jan-23																																			
Construction Building E	610	20-Jan-23	20-Sep-24																																		
FF&E / Move Management Building E	200	23-Jun-24	08-Jan-25																																		
Expected Substantial Completion	0		20-Sep-24																																		
Ready to Hold Classes Building E (Spring 2025)	0		08-Jan-25																																		

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of April 1, 2020

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Building O2 - Economic & Workforce Development/Foundation																						
Pre-Design Building O2	180	14-Apr-23*	10-Oct-23																			
Design Building O2	280	11-Oct-23	16-Jul-24																			
DSA Review Building O2	280	17-Jul-24	22-Apr-25																			
Construction Swing Space Building O2	40	23-Apr-25	01-Jun-25																			
Bid / Award Building O2	90	23-Apr-25	21-Jul-25																			
Expected Substantial Completion Swing Space Building O2	0		01-Jun-25																			
Move Into Swing Space Building B for Building O2	20	22-Jun-25	11-Jul-25																			
NTP Construction Building O2	0	27-Jul-25																				
Construction Building O2	520	27-Jul-25	28-Dec-26																			
FF&E / Move Management from Building B to Building O2	209	09-Dec-26	05-Jul-27																			
Expected Substantial Completion Building O2	0		28-Dec-26																			
Building K - Art																						
Pre-Design Building K	210	06-Aug-25*	03-Mar-26																			
Design Building K	224	04-Mar-26	13-Oct-26																			
DSA Review Building K	280	14-Oct-26	20-Jul-27																			
Bid / Award Building K	90	21-Jul-27	18-Oct-27																			
Move Into Swing Space Building B for Building K	10	19-Dec-27	28-Dec-27																			
NTP Construction Building K	0	29-Dec-27																				
Construction Building K	390	29-Dec-27	21-Jan-29																			
FF&E / Move Management Building K from Building B	251	24-Oct-28	01-Jul-29																			
Expected Substantial Completion Building K	0		21-Jan-29																			
Ready to Hold Classes Building K	0		01-Jul-29																			
Building R - Primary Gymnasium																						
Pre-Design Building R	145	18-Feb-27*	12-Jul-27																			
Design Building R	363	13-Jul-27	09-Jul-28																			
DSA Review Building R	280	10-Jul-28	15-Apr-29																			
Bid / Award Building R	90	16-Apr-29	14-Jul-29																			
Move Into Swing Space Building Q & Aquatic	30	15-Jul-29	13-Aug-29																			
NTP Construction Building R	0	14-Aug-29																				
Construction Building R	730	14-Aug-29	13-Aug-31																			
FF&E / Move Management Building R	180	15-Jul-31	10-Jan-32																			
Expected Substantial Completion Building R	0		13-Aug-31																			
Ready to Hold Classes Building R	0		10-Jan-32																			
Building Q - Secondary Gymnasium																						
Pre-Design Building Q	320	07-Jan-30*	22-Nov-30																			
Design Building Q	246	23-Nov-30	26-Jul-31																			
DSA Review Building Q	280	27-Jul-31	01-May-32																			
Bid / Award Building Q	90	02-May-32	30-Jul-32																			
Move Into Swing Space Building R & Aquatic	30	01-Jun-32	30-Jun-32																			
NTP Construction Building Q	0	05-Aug-32																				
Construction Building Q	610	05-Aug-32	06-Apr-34																			
FF&E / Move Management Building Q	195	08-Dec-33	20-Jun-34																			
Expected Substantial Completion Building Q	0		06-Apr-34																			
Ready to Hold Classes Building Q	0		20-Jun-34																			
Building B - Tech Studies																						



■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of April 1, 2020


Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Pre-Design Building B	170	05-Jan-32*	22-Jun-32																			
Design Building B	276	23-Jun-32	25-Mar-33																			
DSA Review Building B	280	26-Mar-33	30-Dec-33																			
Bid / Award Building B	90	31-Dec-33	30-Mar-34																			
NTP Construction Building B	0	31-Mar-34																				
Construction Building B	730	31-Mar-34	29-Mar-36																			
Expected Substantial Completion Building B	0		29-Mar-36																			
Building F - Demo Family/Consumer Education/New Courtyard																						
Design Building F	245	08-Jan-35*	09-Sep-35																			
DSA Review Building F	160	10-Sep-35	16-Feb-36																			
Bid / Award Building F	55	17-Feb-36	11-Apr-36																			
Move Into Building B from Building F	60	29-Apr-36	27-Jun-36																			
Demo & Courtyard Building F	365	28-Jun-36	27-Jun-37																			
Building O1 - IITS/ Warehouse																						
Pre-Design Building O1	200	02-May-34*	17-Nov-34																			
Design Building O1	244	18-Nov-34	19-Jul-35																			
DSA Review Building O1	280	20-Jul-35	24-Apr-36																			
Bid / Award Building O1	90	25-Apr-36	23-Jul-36																			
Move Into Swing Space Building O2	30	24-Jun-36	23-Jul-36																			
NTP Construction Building O1	0	29-Jul-36																				
Construction Building O1	420	29-Jul-36	21-Sep-37																			
FF&E / Move Management Building O1 from Building O2	213	25-May-37	23-Dec-37																			
Expected Substantial Completion Building O1	0		21-Sep-37																			
Building S - Stadium																						
Pre-Design Building S	200	15-May-34*	30-Nov-34																			
Design Building S	365	06-Dec-34	05-Dec-35																			
DSA Review Building S	280	06-Dec-35	10-Sep-36																			
Bid / Award Building S	90	11-Sep-36	09-Dec-36																			
Construction Swing Space Building for S	90	11-Sep-36	09-Dec-36																			
Expected Substantial Completion Swing Space Building for S	0		09-Dec-36																			
Move Into Swing Space Building TBD from Building S	15	20-Dec-36	03-Jan-37																			
NTP Construction Building S	0	04-Jan-37																				
Construction Building S	700	04-Jan-37	04-Dec-38																			
Expected Substantial Completion Building S	0		04-Dec-38																			
Punchlist Building S	30	05-Dec-38	03-Jan-39																			
FF&E / Move Management Building from Building TBD to Building S	200	05-Dec-38	22-Jun-39																			
Ready to Hold Classes Building S	0		22-Jun-39																			
Building CDC - Child Development Center																						
Pre-Design Building	49	01-Jun-36*	19-Jul-36																			
Design Building	154	20-Jul-36	20-Dec-36																			
DSA Review Building	280	21-Dec-36	26-Sep-37																			
Move Into Swing Space TBD from CDC	60	20-May-37	18-Jul-37																			
Bid / Award Building	90	27-Sep-37	25-Dec-37																			
NTP Construction Building	0	26-Dec-37																				
Construction Building	290	26-Dec-37	11-Oct-38																			
FF&E / Move Management	201	13-Jun-38	30-Dec-38																			

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of April 1, 2020

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Expected Substantial Completion Building	0		11-Sep-38																				
Pacific Coast Campus																							
Building P2 - PCC Parking Structure																							
Design Parking Structure	224	16-Jul-18 A	25-Feb-19 A																				
DSA Review Parking Structure	290	16-Jan-19 A	01-Nov-19 A																				
NTP Construction Parking Structure	0	11-Oct-19 A																					
Construction Parking Structure	430	11-Oct-19 A	13-Dec-20																				
Expected Substantial Completion Parking Structure	0		13-Dec-20																				
Closeout Parking Structure	30	14-Dec-20	12-Jan-21																				
Building MM - Construction Trades Ph 1																							
DSA Review Building MM Ph 1	385	10-Jan-19 A	30-Jan-20 A																				
Approve Working Documents and Proceed to Bid Ph 1	88	01-Feb-20 A	28-Apr-20																				
Approval to Award Construction Contract	127	29-Apr-20	02-Sep-20																				
Construction Building MM Ph 1	420	03-Sep-20	27-Oct-21																				
FF&E / Move Management Building MM for Building MM Ph 1	192	30-Jun-21	08-Jan-22																				
Expected Substantial Completion Building MM Ph 1	0		27-Oct-21																				
Ready to Hold Classes Building MM Ph 1 (Spring 2022)	0		08-Jan-22																				
EEM-2A - Energy and Portable Water Reductions - PCC (TBD)																							
Design EEM-2A	180	01-Apr-21*	27-Sep-21																				
DSA EEM-2A	260	28-Sep-21	14-Jun-22																				
Bid / Award EEM-2A	90	15-Jun-22	12-Sep-22																				
Construction EEM-2A	365	13-Sep-22	12-Sep-23																				
Building MM - Construction Trades Ph 2																							
Design Building MM Ph 2	454	01-Oct-20	28-Dec-21																				
DSA Review Building MM Ph 2	280	29-Dec-21	04-Oct-22																				
Bid / Award Building Building MM Ph 2	90	05-Oct-22	02-Jan-23																				
Construction Building MM Ph 2	390	03-Jan-23	27-Jan-24																				
FF&E / Move Management Building MM from Building MM Ph 2	238	29-Nov-23	23-Jul-24																				
Expected Substantial Completion Building MM Ph 2	0		27-Jan-24																				
Ready to Hold Classes Building MM Ph 2 (Fall 2024)	0		23-Jul-24																				
Building OO - Humanities																							
Design Building Humanities	608	01-Oct-21*	31-May-23																				
DSA Review Building Humanities	280	01-Jun-23	06-Mar-24																				
Bid / Award Building Humanities	90	07-Mar-24	04-Jun-24																				
NTP Construction Building Humanities	0		09-Jun-24																				
Construction Building Humanities	770	10-Jun-24	19-Jul-26																				
FF&E / Move Management Building Humanities from Building Humanities	265	11-Apr-26	31-Dec-26																				
Expected Substantial Completion Building Humanities	0		19-Jul-26																				
Ready to Hold Classes Building Humanities (Spring 2026)	0		31-Dec-26																				
Building FF - Demo Fine Arts & Senior Center/Turnabout																							
Design Building FF Demo & Turnabout	189	01-Sep-22	08-Mar-23																				
DSA Review Building FF	280	09-Mar-23	13-Dec-23																				
Bid / Award Building FF Demo & Turnabout	86	14-Dec-23	08-Mar-24																				
Construction Building FF Demo	155	09-Mar-24	10-Aug-24																				
PCC Walkways & Wayfinding																							
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41																				

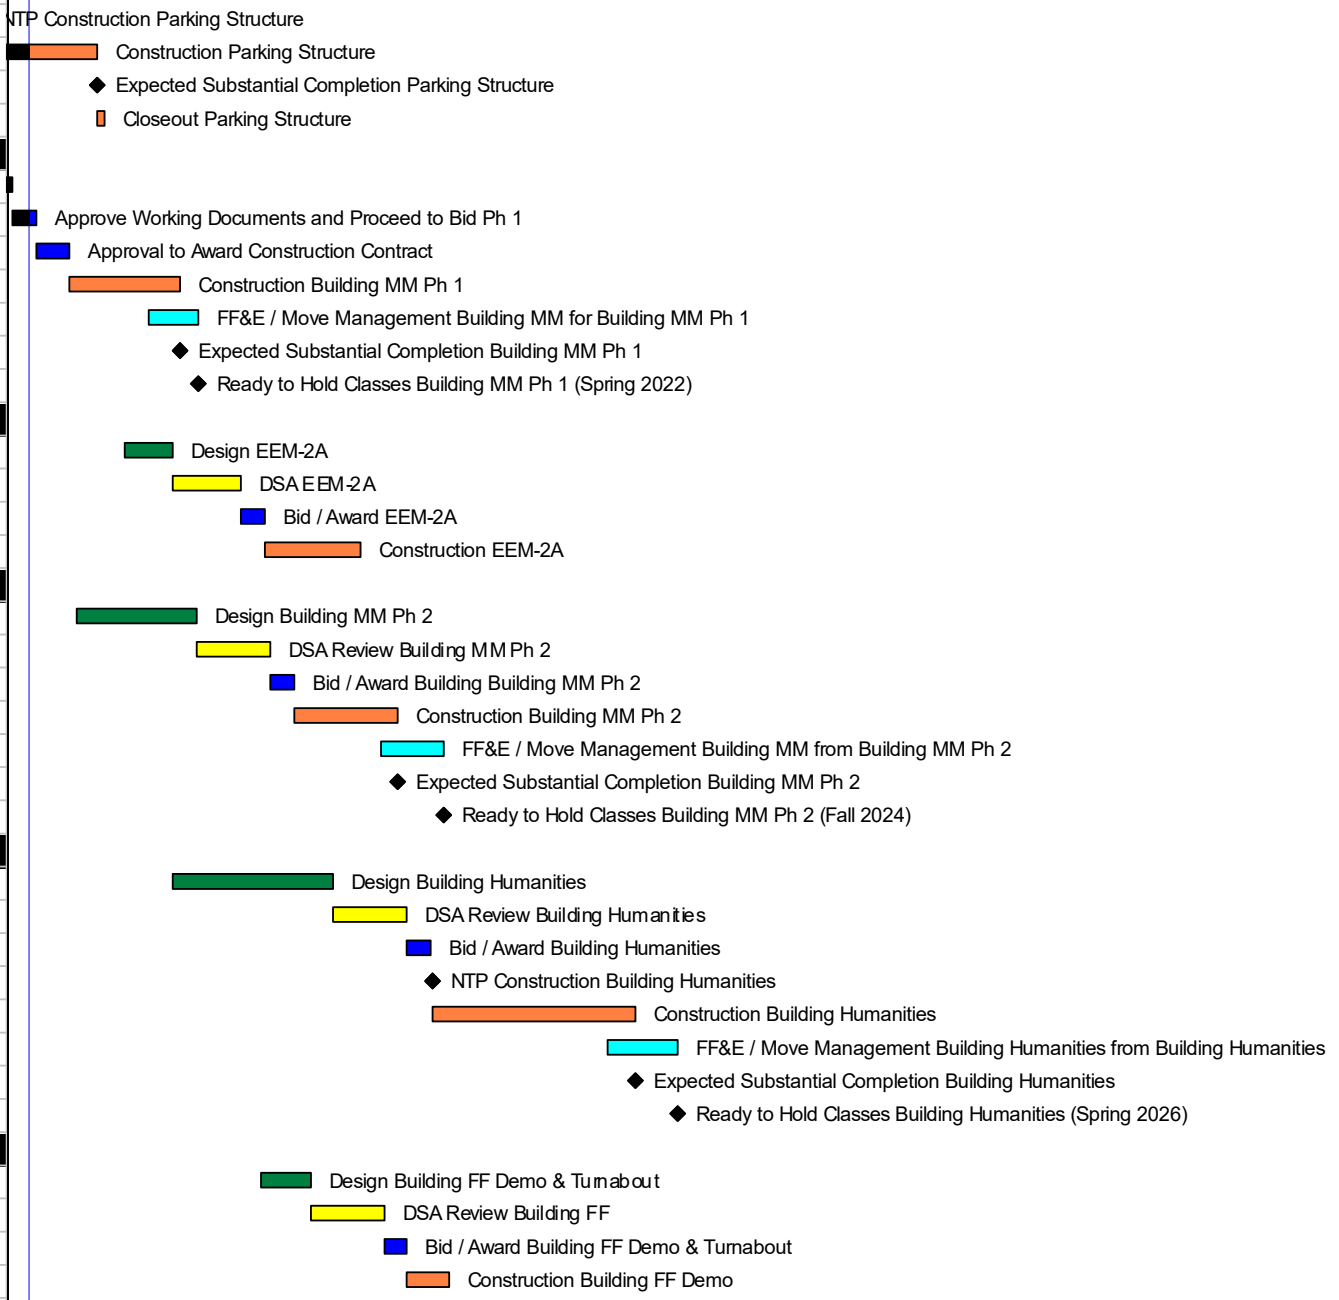

█ PRE █ Bid / Award █ CONST █ Actual
█ DESIGN █ DSA █ FF&E ◆ ◆ Milestone

LBCC Bond Program Master Schedule

Status as of April 1, 2020

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
District Wide																						
Joint Use Facility w/ LBUSD & CSULB #12																						
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21	Joint Use w/ LBUSD & CSULB #12																		
Energy/Water Conservation Projects																						
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41	Energy Water Conservation Projects																		
Districtwide Solar Projects																						
Pre-Design, Criteria Documents, RFP	476	21-Mar-19 A	08-Jul-20	Pre-Design, Criteria Documents, RFP																		
Award Districtwide Solar	40	09-Jul-20	17-Aug-20	Award Districtwide Solar																		
Design Districtwide Solar	119	18-Aug-20	14-Dec-20	Design Districtwide Solar																		
DSA Districtwide Solar	120	15-Dec-20	13-Apr-21	DSA Districtwide Solar																		
NTP PCC Construction Solar	0	14-Apr-21		NTP PCC Construction Solar																		
PCC Construction Solar	120	14-Apr-21	11-Aug-21	PCC Construction Solar																		
NTP LAC Construction Solar	0	08-Jun-21		NTP LAC Construction Solar																		
LAC Construction Solar	120	08-Jun-21	05-Oct-21	LAC Construction Solar																		
Expected Substantial Completion PCC Solar	0		11-Aug-21	Expected Substantial Completion PCC Solar																		
Expected Substantial Completion LAC Solar	0		05-Oct-21	Expected Substantial Completion LAC Solar																		
SCE Charge Ready																						
Design SCE Charge Ready	113	01-Apr-19 A	22-Jul-19 A	Design SCE Charge Ready																		
Permit and Easement SCE Charge Ready	147	23-Jul-19 A	17-Dec-19 A	Permit and Easement SCE Charge Ready																		
PCC Construction Infrastructure SCE Charge Ready	70	16-Jan-20 A	25-Mar-20 A	PCC Construction Infrastructure SCE Charge Ready																		
LAC Construction SCE Infrastructure SCE Charge Ready	72	20-Jan-20 A	31-Mar-20 A	LAC Construction SCE Infrastructure SCE Charge Ready																		
PCC Construction Install ChargePoint SCE Charge Ready	60	26-Mar-20 A	24-May-20	PCC Construction Install ChargePoint SCE Charge Ready																		
LAC Construction Install ChargePoint SCE Charge Ready	60	01-Apr-20	30-May-20	LAC Construction Install ChargePoint SCE Charge Ready																		
Technology Refresh/Replacement																						
Technology Refresh/Replacement	8923	01-Feb-17 A	07-Jul-41	Technology Refresh/Replacement																		
Enterprise Wide Computer System																						
Enterprise Wide Computer System	8923	01-Feb-17 A	07-Jul-41	Enterprise Wide Computer System																		
Landscaping																						
Landscaping	8923	01-Feb-17 A	07-Jul-41	Landscaping																		
Infrastructure Projectss																						
Infrastructure Projects	8923	01-Feb-17 A	07-Jul-41	Infrastructure Projects																		
Minor Campus Improvements																						
Minor Campus Improvements	8923	01-Feb-17 A	07-Jul-41	Minor Campus Improvements																		
Surface Parking Improvements																						
Surface Parking Improvements	8923	01-Feb-17 A	07-Jul-41	Surface Parking Improvements																		

■ PRE ■ Bid /Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone
