

LBCC Bond Program Master Schedule

Status as of March 1, 2021

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Long Beach Community College Bond Program Schedule - March 1, 2021																					
Liberal Arts Campus																					
Building J - Auditorium																					
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A																		
Design Building J	145	01-Nov-15 A	24-Mar-16 A																		
DSA Building J	398	03-Sep-16 A	06-Oct-17 A																		
Bid / Award Building J	89	07-Oct-17 A	04-Jan-18 A																		
Construction Building J (Spring 2018 - Summer 2020)	914	12-Jan-18 A	14-Jul-20 A																		
FF&E / Move Management from Building J from Public Theater & Building FF	493	24-Nov-19 A	30-Mar-21																		
Expected Substantial Completion Building J	0		14-Jul-20 A																		
Ready to Hold Classes Building J (Spring 2021)	0		03-Dec-20 A																		
Kinesiology Labs & Aquatics Center																					
Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A																		
Design Kinesiology Labs & Aquatic Center	615	01-Jun-17 A	06-Feb-19 A																		
DSA Kinesiology Labs & Aquatic Center	241	29-Jan-19 A	26-Sep-19 A																		
Bid / Award Kinesiology Labs & Aquatic Center	138	19-Sep-19 A	03-Feb-20 A																		
NTP Kinesiology Labs & Aquatic Center	0	10-Feb-20 A																			
Phase 2 Softball Complex	429	10-Feb-20 A	13-Apr-21																		
Phase 1 Aquatic Complex & North Fields	530	10-Feb-20 A	23-Jul-21																		
Phase 3 Parking Lot etc.	45	14-Apr-21	28-May-21																		
FF&E / Move Management Kinesiology Labs & Aquatic Center	258	25-Apr-21	08-Jan-22																		
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Spring 2022)	0		08-Jan-22																		
Building X - Central Plant Expansion																					
Design	413	23-Jan-18 A	12-Mar-19 A																		
DSA LAC Central Plant	146	13-Apr-19 A	06-Sep-19 A																		
Bid / Award LAC Central Plant	107	19-Aug-19 A	03-Dec-19 A																		
Construction LAC Central Plant Phase 1	130	09-Dec-19 A	16-Apr-20 A																		
Construction LAC Central Plant Phase 2	130	09-Dec-19 A	16-Apr-20 A																		
Expected Substantial Completion Phase 1	0		12-Jan-21 A																		
Expected Substantial Completion Phase 2	0		12-Jan-21 A																		
LAC Site Barrier Removal																					
Design Campus Improvements	924	12-Sep-17 A	23-Mar-20 A																		
DSA Review LAC Site Barrier Removal	166	24-Mar-20 A	05-Sep-20 A																		
Bid / Award LAC Site Barrier Removal	156	06-Sep-20 A	08-Feb-21 A																		
Construction LAC Site Barrier Removal	270	22-Feb-21 A	18-Nov-21																		
Expected Substantial Completion	0		18-Nov-21																		
LAC Building Barrier Removal																					
Design Campus Improvements	952	12-Sep-17 A	20-Apr-20 A																		
DSA Review LAC Building Barrier Removal	155	12-Jun-20 A	13-Nov-20 A																		
Bid / Award LAC Building Barrier Removal	100	26-Feb-21 A	05-Jun-21																		
Construction LAC Building Barrier Removal	518	17-Jul-21	16-Dec-22																		
Expected Substantial Completion	0		16-Dec-22																		
Building M - Liberal Arts																					
Pre-Design Building M	329	01-Aug-17 A	26-Jun-18 A																		
Award DBE Building M	120	27-Jun-18 A	25-Oct-18 A																		
Design and DSA Review Building M	517	05-Nov-18 A	04-Apr-20 A																		

PRE
 Bid / Award
 CONST
 Actual
 DESIGN
 DSA
 FF&E
◆ Milestone

LBCC Bond Program Master Schedule

Status as of March 1, 2021


Activity Name	At Completion Duration	Start	Finish	Year																							
				2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037						
FF&E / Move Management Swing Spaces Building B for Building M	245	06-Jun-19 A	05-Feb-20 A	█																							
Move Into Swing Spaces Bldg B for Building M (Jan 2020)	1	17-Jan-20 A	17-Jan-20 A	█																							
Move Into Swing Spaces Portables for Building M (Jan 2020)	1	26-Jan-20 A	26-Jan-20 A	█																							
NTP Construction Building M	0	13-Feb-20 A		◆ NTP Construction Building M																							
Construction Building M	610	08-Apr-20 A	08-Dec-21	█ Construction Building M																							
FF&E / Move Management Building M	234	09-Nov-21	01-Jul-22	█ FF&E / Move Management Building M																							
Expected Substantial Completion Building M	0		08-Dec-21	◆ Expected Substantial Completion Building M																							
Ready to Hold Classes Building M (Fall 2022)	0		01-Jul-22	◆ Ready to Hold Classes Building M (Fall 2022)																							
Building G - Music & Theater Arts																											
Design Building G/H	434	11-Sep-19 A	17-Nov-20 A	█																							
Design Swing Space for Building G/H	300	01-May-20 A	25-Feb-21 A	█																							
DSA Review Building G/H	316	18-Nov-20 A	29-Sep-21	█ DSA Review Building G/H																							
DSA Review Swing Space for Building G/H	60	25-Feb-21 A	25-Apr-21	█ DSA Review Swing Space for Building G/H																							
Bid / Award Swing Space for Building G/H	90	26-Apr-21	24-Jul-21	█ Bid / Award Swing Space for Building G/H																							
Construction Swing Space Building for G/H	150	27-Jul-21	23-Dec-21	█ Construction Swing Space Building for G/H																							
Approve Working Documents and Proceed to Bid	52	30-Sep-21	21-Nov-21	█ Approve Working Documents and Proceed to Bid																							
Bid / Award Building G/H	123	21-Nov-21	23-Mar-22	█ Bid / Award Building G/H																							
Expected Substantial Completion Swing Space Building for G/H	0		23-Dec-21	◆ Expected Substantial Completion Swing Space Building for G/H																							
Move Into Swing Space (TBD) for Building G/H (Dec 2021/Jan 2022)	15	24-Dec-21	07-Jan-22	█ Move Into Swing Space (TBD) for Building G/H (Dec 2021/Jan 2022)																							
Construction Building G	750	24-Mar-22	11-Apr-24	█ Construction Building G																							
Expected Substantial Completion Building G	0		11-Apr-24	◆ Expected Substantial Completion Building G																							
Ready to Hold Classes Building G (Fall 2024)	0		24-Jul-24	◆ Ready to Hold Classes Building G (Fall 2024)																							
EEM-2C - Thermal Storage Strategy - Bldg P Attic (TBD)																											
Design EEM-2C	180	01-Apr-21*	27-Sep-21	█ Design EEM-2C																							
DSA EEM-2C	180	28-Sep-21*	26-Mar-22	█ DSA EEM-2C																							
Bid / Award EEM-2C	90	27-Mar-22	24-Jun-22	█ Bid / Award EEM-2C																							
Construction EEM-2C	160	25-Jun-22	01-Dec-22	█ Construction EEM-2C																							
EEM-2A - Energy and Portable Water Reductions - LAC (TBD)																											
Design EEM-2A	180	01-Apr-21*	27-Sep-21	█ Design EEM-2A																							
DSA EEM-2A	260	28-Sep-21*	14-Jun-22	█ DSA EEM-2A																							
Bid / Award EEM-2A	90	15-Jun-22	12-Sep-22	█ Bid / Award EEM-2A																							
Construction EEM-2A	365	13-Sep-22	12-Sep-23	█ Construction EEM-2A																							
Building E - College Center																											
Design Building E	443	18-Jan-21 A	05-Apr-22	█ Design Building E																							
Design Swing Space for Building E	180	05-Jun-21	01-Dec-21	█ Design Swing Space for Building E																							
DSA Review Swing Space for Building E	90	02-Dec-21	01-Mar-22	█ DSA Review Swing Space for Building E																							
Bid / Award Swing Space for Building E	93	02-Mar-22	02-Jun-22	█ Bid / Award Swing Space for Building E																							
DSA Review Building E	280	06-Apr-22	10-Jan-23	█ DSA Review Building E																							
Construction Swing Space for Building E	120	03-Jun-22	30-Sep-22	█ Construction Swing Space for Building E																							
FF&E / Move Management Swing Space for Building E	176	02-Aug-22	24-Jan-23	█ FF&E / Move Management Swing Space for Building E																							
Expected Substantial Completion Swing Space for Building E	0		30-Sep-22	◆ Expected Substantial Completion Swing Space for Building E																							
Bid / Award Building E	91	11-Jan-23	11-Apr-23	█ Bid / Award Building E																							
NTP	0	13-Apr-23		◆ NTP																							
Construction Building E	610	13-Apr-23	12-Dec-24	█ Construction Building E																							
FF&E / Move Management Building E	195	14-Sep-24	27-Mar-25	█ FF&E / Move Management Building E																							
Expected Substantial Completion	0		12-Dec-24	◆ Expected Substantial Completion																							

█ PRE █ Bid / Award █ CONST █ Actual
█ DESIGN █ DSA █ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of March 1, 2021

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Ready to Hold Classes Building E (Fall 2025)	0		27-Mar-25																				
Building S - Stadium																							
Feasibility Study Building S	91	01-Apr-21*	30-Jun-21																				
Town Hall Meetings Building S	150	01-Jul-21	27-Nov-21																				
Supplemental EIR Building S	365	28-Nov-21	27-Nov-22																				
Design Building S	560	28-Nov-21	10-Jun-23																				
Design Swing Space for Building S	180	28-Nov-22	26-May-23																				
DSA Review Swing Space for Building S	180	27-May-23	22-Nov-23																				
DSA Review Building S	320	11-Jun-23	25-Apr-24																				
Bid/Award Swing Space for Building S	90	23-Nov-23	20-Feb-24																				
Construction Swing Space for Building S	270	21-Feb-24	16-Nov-24																				
Bid / Award Building S	180	26-Apr-24	22-Oct-24																				
Expected Substantial Completion Swing Space Building for S	0		16-Nov-24																				
Move Into Swing Space Building TBD from Building S	50	16-Dec-24*	03-Feb-25																				
NTP Construction Building S	0	22-Feb-25																					
Construction Building S	700	22-Feb-25	22-Jan-27																				
Expected Substantial Completion Building S	0		22-Jan-27																				
Punchlist Building S	30	23-Jan-27	21-Feb-27																				
FF&E / Move Management Building from Building TBD to Building S	200	23-Jan-27	10-Aug-27																				
Ready to Hold Classes Building S (Fall 2027)	0		10-Aug-27																				
Building O2 - Economic & Workforce Development/Foundation																							
Pre-Design Building O2	180	14-Apr-25*	10-Oct-25																				
Design Building O2	280	11-Oct-25	17-Jul-26																				
DSA Review Building O2	280	18-Jul-26	23-Apr-27																				
Construction Swing Space Building O2	40	24-Apr-27	02-Jun-27																				
Bid / Award Building O2	90	24-Apr-27	22-Jul-27																				
Expected Substantial Completion Swing Space Building O2	0		02-Jun-27																				
Move Into Swing Space Building B for Building O2	20	23-Jun-27	12-Jul-27																				
NTP Construction Building O2	0	28-Jul-27																					
Construction Building O2	520	28-Jul-27	28-Dec-28																				
FF&E / Move Management from Building B to Building O2	209	09-Dec-28	05-Jul-29																				
Expected Substantial Completion Building O2	0		28-Dec-28																				
Building K - Art																							
Pre-Design Building K	210	06-Aug-27*	02-Mar-28																				
Design Building K	224	03-Mar-28	12-Oct-28																				
DSA Review Building K	280	13-Oct-28	19-Jul-29																				
Bid / Award Building K	90	20-Jul-29	17-Oct-29																				
Move Into Swing Space Building B for Building K	10	19-Dec-29	28-Dec-29																				
NTP Construction Building K	0	29-Dec-29																					
Construction Building K	390	29-Dec-29	22-Jan-31																				
FF&E / Move Management Building K from Building B	251	25-Oct-30	02-Jul-31																				
Expected Substantial Completion Building K	0		22-Jan-31																				
Ready to Hold Classes Building K	0		02-Jul-31																				
Building R - Primary Gymnasium																							
Pre-Design Building R	145	18-Feb-29*	12-Jul-29																				
Design Building R	363	13-Jul-29	10-Jul-30																				

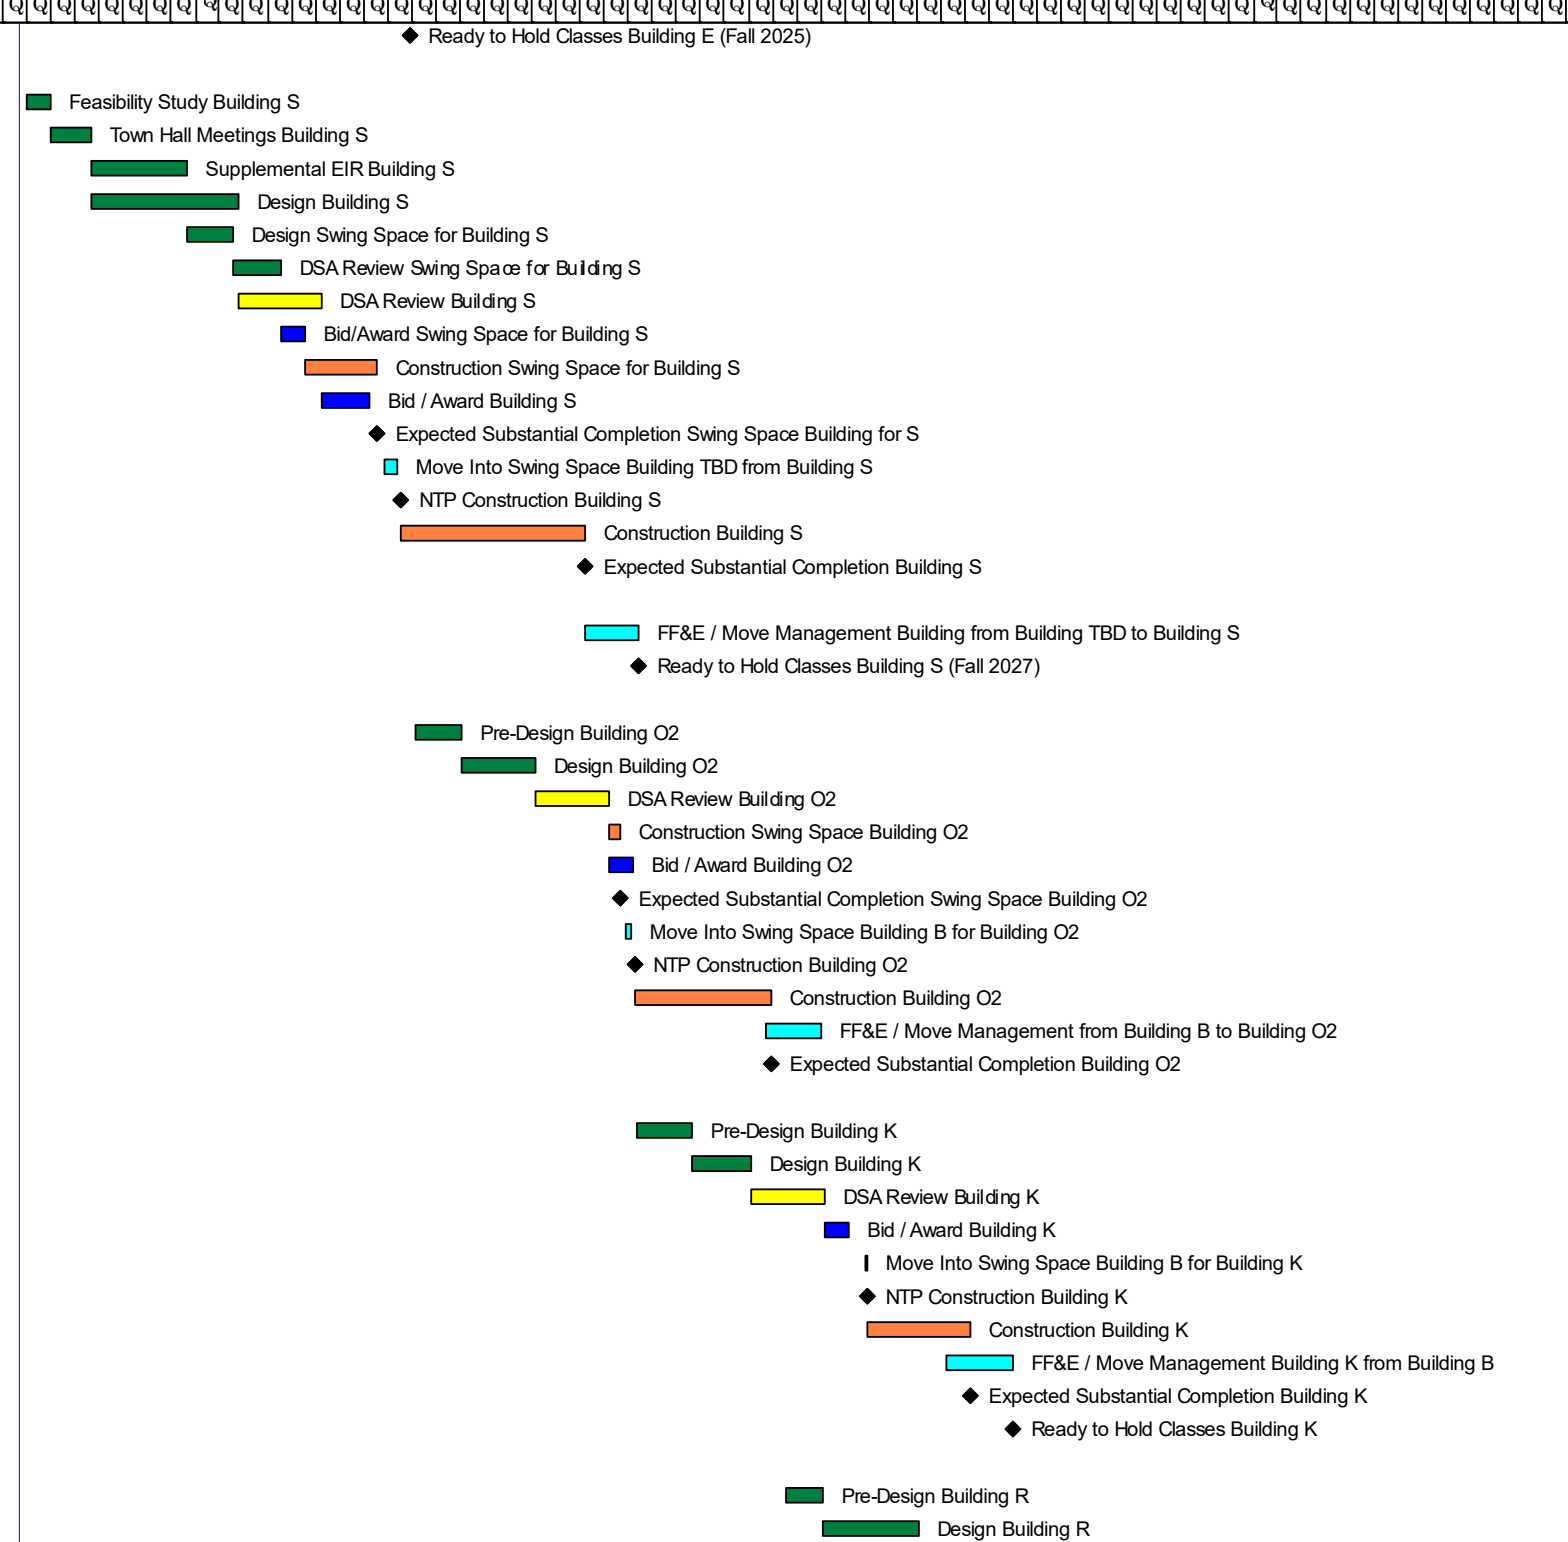

■ PRE ■ Bid/Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone

LBCC Bond Program Master Schedule

Status as of March 1, 2021

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
DSA Review Building R	280	11-Jul-30	16-Apr-31																			
Bid / Award Building R	90	17-Apr-31	15-Jul-31																			
Move Into Swing Space Building Q & Aquatic	30	16-Jul-31	14-Aug-31																			
NTP Construction Building R	0	15-Aug-31																				
Construction Building R	730	15-Aug-31	13-Aug-33																			
FF&E / Move Management Building R	180	15-Jul-33	10-Jan-34																			
Expected Substantial Completion Building R	0		13-Aug-33																			
Ready to Hold Classes Building R	0		10-Jan-34																			
Building Q - Secondary Gymnasium																						
Pre-Design Building Q	320	07-Jan-32*	21-Nov-32																			
Design Building Q	246	22-Nov-32	25-Jul-33																			
DSA Review Building Q	280	26-Jul-33	01-May-34																			
Bid / Award Building Q	90	02-May-34	30-Jul-34																			
Move Into Swing Space Building R & Aquatic	30	01-Jun-34	30-Jun-34																			
NTP Construction Building Q	0	05-Aug-34																				
Construction Building Q	610	05-Aug-34	05-Apr-36																			
FF&E / Move Management Building Q	195	08-Dec-35	19-Jun-36																			
Expected Substantial Completion Building Q	0		05-Apr-36																			
Ready to Hold Classes Building Q	0		19-Jun-36																			
Building B - Tech Studies																						
Pre-Design Building B	170	20-Mar-34*	05-Sep-34																			
Design Building B	276	06-Sep-34	08-Jun-35																			
DSA Review Building B	280	09-Jun-35	14-Mar-36																			
Bid / Award Building B	90	15-Mar-36	12-Jun-36																			
NTP Construction Building B	0	13-Jun-36																				
Construction Building B	730	13-Jun-36	12-Jun-38																			
Expected Substantial Completion Building B	0		12-Jun-38																			
Building F - Demo Family/Consumer Education/New Courtyard																						
Design Building F	245	08-Jan-37*	09-Sep-37																			
DSA Review Building F	160	10-Sep-37	16-Feb-38																			
Bid / Award Building F	55	17-Feb-38	12-Apr-38																			
Move Into Building B from Building F	60	13-Jul-38	10-Sep-38																			
Demo & Courtyard Building F	365	11-Sep-38	10-Sep-39																			
Building O1 - IITS/ Warehouse																						
Pre-Design Building O1	200	02-May-36*	17-Nov-36																			
Design Building O1	244	18-Nov-36	19-Jul-37																			
DSA Review Building O1	280	20-Jul-37	25-Apr-38																			
Bid / Award Building O1	90	26-Apr-38	24-Jul-38																			
Move Into Swing Space Building O2	30	25-Jun-38	24-Jul-38																			
NTP Construction Building O1	0	30-Jul-38																				
Construction Building O1	420	30-Jul-38	22-Sep-39																			
FF&E / Move Management Building O1 from Building O2	213	26-May-39	24-Dec-39																			
Expected Substantial Completion Building O1	0		22-Sep-39																			
Building CDC - Child Development Center																						
Pre-Design Building	49	01-Jun-38*	19-Jul-38																			
Design Building	154	20-Jul-38	20-Dec-38																			

- DSA Review Building R
- Bid / Award Building R
- Move Into Swing Space Building Q & Aquatic
- ◆ NTP Construction Building R
- Construction Building R
- FF&E / Move Management Building R
- ◆ Expected Substantial Completion Building R
- ◆ Ready to Hold Classes Building R

- Pre-Design Building Q
- Design Building Q
- DSA Review Building Q
- Bid / Award Building Q
- Move Into Swing Space Building R & Aquatic
- ◆ NTP Construction Building Q
- Construction Building Q
- FF&E / Move Management Building Q
- ◆ Expected Substantial Completion Building Q
- ◆ Ready to Hold Classes Building Q

- Pre-Design Building B
- Design Building B
- DSA Review Building B
- Bid / Award Building B
- ◆ NTP Construction Building B
- Construction Building B

- Pre-Design Building F
- Design Building F
- DSA Review Building F
- Bid / Award Building F
- ◆ NTP Construction Building F
- Construction Building F

- Pre-Design Building O1
- Design Building O1
- DSA Review Building O1
- Bid / Award Building O1
- ◆ NTP Construction Building O1
- Construction Building O1

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of March 1, 2021

Activity Name	At Completion Duration	Start	Finish	Schedule																							
				2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037						
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q				
DSA Review Building	280	21-Dec-38	26-Sep-39																								
Move Into Swing Space TBD from CDC	60	20-May-39	18-Jul-39																								
Bid / Award Building	90	27-Sep-39	25-Dec-39																								
NTP Construction Building	0	26-Dec-39																									
Construction Building	290	26-Dec-39	10-Oct-40																								
FF&E / Move Management	201	12-Jun-40	29-Dec-40																								
Expected Substantial Completion Building	0		10-Sep-40																								
Pacific Coast Campus																											
Building P2 - PCC Parking Structure																											
Design Parking Structure	224	16-Jul-18 A	25-Feb-19 A																								
DSA Review Parking Structure	290	16-Jan-19 A	01-Nov-19 A																								
NTP Construction Parking Structure	0	11-Oct-19 A																									
Construction Parking Structure	381	11-Oct-19 A	26-Oct-20 A																								
Expected Substantial Completion Parking Structure	0		26-Oct-20 A																								
Closeout Parking Structure	91	01-Nov-20 A	30-Jan-21 A																								
Building MM - Construction Trades Ph 1																											
DSA Review Building MM Ph 1	385	10-Jan-19 A	30-Jan-20 A																								
Approve Working Documents and Proceed to Bid Ph 1	128	01-Feb-20 A	08-Jun-20 A																								
Approval to Award Construction Contract	123	09-May-20 A	08-Sep-20 A																								
Construction Building MM Ph 1	420	01-Dec-20 A	24-Jan-22																								
FF&E / Move Management Building MM for Building MM Ph 1	282	27-Sep-21	06-Jul-22																								
Expected Substantial Completion Building MM Ph 1	0		24-Jan-22																								
Ready to Hold Classes Building MM Ph 1 (Fall 2022)	0		06-Jul-22																								
EEM-2A - Energy and Portable Water Reductions - PCC (TBD)																											
Design EEM-2A	180	01-Apr-21*	27-Sep-21																								
DSA EEM-2A	260	28-Sep-21	14-Jun-22																								
Bid / Award EEM-2A	90	15-Jun-22	12-Sep-22																								
Construction EEM-2A	365	13-Sep-22	12-Sep-23																								
Building MM - Construction Trades Ph 2																											
Design Building MM Ph 2	419	01-Oct-20 A	23-Nov-21																								
DSA Review Building MM Ph 2	280	24-Nov-21	30-Aug-22																								
Chancellor's Office Review DSA Permit & Bid	56	31-Aug-22	25-Oct-22																								
Bid Process for Building Building MM Ph 2	91	26-Oct-22	24-Jan-23																								
Chancellor's Office Review & Approve Award of Contract	28	25-Jan-23	21-Feb-23																								
Construction Building MM Ph 2	488	22-Feb-23	23-Jun-24																								
FF&E / Move Management Building MM from Building MM Ph 2	195	25-Apr-24	05-Nov-24																								
Expected Substantial Completion Building MM Ph 2	0		23-Jun-24																								
Ready to Hold Classes Building MM Ph 2 (Spring 2025)	0		27-Dec-24																								
Building OO - Humanities																											
Design Building Humanities	608	03-Oct-22*	01-Jun-24																								
DSA Review Building Humanities	280	02-Jun-24	08-Mar-25																								
Bid / Award Building Humanities	90	09-Mar-25	06-Jun-25																								
NTP Construction Building Humanities	0		11-Jun-25																								
Construction Building Humanities	770	12-Jun-25	21-Jul-27																								
FF&E / Move Management Building Humanities from Building Humanities	265	13-Apr-27	02-Jan-28																								
Expected Substantial Completion Building Humanities	0		21-Jul-27																								

NTP Construction Parking Structure

Expected Substantial Completion Parking Structure

Construction Building MM Ph 1
 FF&E / Move Management Building MM for Building MM Ph 1
 Expected Substantial Completion Building MM Ph 1
 Ready to Hold Classes Building MM Ph 1 (Fall 2022)

Design EEM-2A
 DSA EEM-2A
 Bid / Award EEM-2A
 Construction EEM-2A

Design Building MM Ph 2
 DSA Review Building MM Ph 2
 Chancellor's Office Review DSA Permit & Bid
 Bid Process for Building Building MM Ph 2
 Chancellor's Office Review & Approve Award of Contract
 Construction Building MM Ph 2
 FF&E / Move Management Building MM from Building MM Ph 2
 Expected Substantial Completion Building MM Ph 2
 Ready to Hold Classes Building MM Ph 2 (Spring 2025)

Design Building Humanities
 DSA Review Building Humanities
 Bid / Award Building Humanities
 NTP Construction Building Humanities
 Construction Building Humanities
 FF&E / Move Management Building Humanities from Building Humanities
 Expected Substantial Completion Building Humanities

PRE	Bid / Award	CONST	Actual
DESIGN	DSA	FF&E	Milestone

LBCC Bond Program Master Schedule

Status as of March 1, 2021

Activity Name	At Completion Duration	Start	Finish	Year																							
				2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037						
Ready to Hold Classes Building Humanities (Spring 2028)	0		02-Jan-28	◆ Ready to Hold Classes Building Humanities (Spring 2028)																							
Building FF - Demo Fine Arts & Senior Center/Turnabout																											
Design Building FF Demo & Turnabout	189	01-Sep-23	07-Mar-24	<div style="display: flex; justify-content: space-between;"> <div style="width: 45%;"> <p>■ Design Building FF Demo & Turnabout</p> <p>■ DSA Review Building FF</p> <p>■ Bid / Award Building FF Demo & Turnabout</p> <p>■ Construction Building FF Demo</p> </div> <div style="width: 45%;"> <p>■ Pre-Design, Criteria Documents, RFP</p> <p>■ Award Districtwide Solar</p> <p>■ Design Districtwide Solar</p> <p>■ DSA Districtwide Solar</p> <p>◆ NTP PCC Construction Solar</p> <p>■ PCC Construction Solar</p> <p>◆ Expected Substantial Completion PCC Solar</p> </div> </div>																							
DSA Review Building FF	280	08-Mar-24	12-Dec-24																								
Bid / Award Building FF Demo & Turnabout	86	13-Dec-24	08-Mar-25																								
Construction Building FF Demo	155	09-Mar-25	10-Aug-25																								
PCC Walkways & Wayfinding																											
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41	■																							
District Wide																											
Joint Use Facility w/ LBUSD & CSULB #12																											
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21 A	■																							
Energy/Water Conservation Projects																											
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41	■																							
Districtwide Solar Projects																											
Pre-Design, Criteria Documents, RFP	826	21-Mar-19 A	23-Jun-21	■																							
Award Districtwide Solar	40	24-Jun-21	02-Aug-21	■																							
Design Districtwide Solar	119	03-Aug-21	29-Nov-21	■																							
DSA Districtwide Solar	120	30-Nov-21	29-Mar-22	■																							
NTP PCC Construction Solar	0	30-Mar-22		◆																							
PCC Construction Solar	120	30-Mar-22	27-Jul-22	■																							
Expected Substantial Completion PCC Solar	0		27-Jul-22	◆																							
SCE Charge Ready																											
Design SCE Charge Ready	113	01-Apr-19 A	22-Jul-19 A	■																							
Permit and Easement SCE Charge Ready	147	23-Jul-19 A	17-Dec-19 A	■																							
PCC Construction Infrastructure SCE Charge Ready	70	16-Jan-20 A	25-Mar-20 A	■																							
LAC Construction SCE Infrastructure SCE Charge Ready	72	20-Jan-20 A	31-Mar-20 A	■																							
PCC Construction Install ChargePoint SCE Charge Ready	60	26-Mar-20 A	24-May-20 A	■																							
LAC Construction Install ChargePoint SCE Charge Ready	60	01-Apr-20 A	30-May-20 A	■																							
Technology Refresh/Replacement																											
Technology Refresh/Replacement	8923	01-Feb-17 A	07-Jul-41	■																							
Enterprise Wide Computer System																											
Enterprise Wide Computer System	8923	01-Feb-17 A	07-Jul-41	■																							
Landscaping																											
Landscaping	8923	01-Feb-17 A	07-Jul-41	■																							
Infrastructure Projectss																											
Infrastructure Projects	8923	01-Feb-17 A	07-Jul-41	■																							
Minor Campus Improvements																											
Minor Campus Improvements	8923	01-Feb-17 A	07-Jul-41	■																							
Surface Parking Improvements																											
Surface Parking Improvements	8923	01-Feb-17 A	07-Jul-41	■																							

■ PRE ■ Bid /Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone
