

LBCC Bond Program Master Schedule

Status as of May 1, 2021

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Long Beach Community College Bond Program Schedule - May 1, 2021																					
Liberal Arts Campus																					
Building J - Auditorium																					
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A																		
Design Building J	145	01-Nov-15 A	24-Mar-16 A																		
DSA Building J	398	03-Sep-16 A	06-Oct-17 A																		
Bid / Award Building J	89	07-Oct-17 A	04-Jan-18 A																		
Construction Building J (Spring 2018 - Summer 2020)	914	12-Jan-18 A	14-Jul-20 A																		
FF&E / Move Management from Building J from Public Theater & Building FF	554	24-Nov-19 A	30-May-21																		
Expected Substantial Completion Building J	0		14-Jul-20 A																		
Ready to Hold Classes Building J (Spring 2021)	0		03-Dec-20 A																		
Kinesiology Labs & Aquatics Center																					
Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A																		
Design Kinesiology Labs & Aquatic Center	615	01-Jun-17 A	06-Feb-19 A																		
DSA Kinesiology Labs & Aquatic Center	241	29-Jan-19 A	26-Sep-19 A																		
Bid / Award Kinesiology Labs & Aquatic Center	138	19-Sep-19 A	03-Feb-20 A																		
NTP Kinesiology Labs & Aquatic Center	0	10-Feb-20 A																			
Phase 2 Softball Complex	476	10-Feb-20 A	30-May-21																		
Phase 1 Aquatic Complex & North Fields	530	10-Feb-20 A	23-Jul-21																		
FF&E / Move Management Kinesiology Labs & Aquatic Center	258	25-Apr-21 A	08-Jan-22																		
Phase 3 Parking Lot etc.	45	31-May-21 A	14-Jul-21																		
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Spring 2022)	0		08-Jan-22																		
Building X - Central Plant Expansion																					
Design	413	23-Jan-18 A	12-Mar-19 A																		
DSA LAC Central Plant	146	13-Apr-19 A	06-Sep-19 A																		
Bid / Award LAC Central Plant	107	19-Aug-19 A	03-Dec-19 A																		
Construction LAC Central Plant Phase 1	130	09-Dec-19 A	16-Apr-20 A																		
Construction LAC Central Plant Phase 2	130	09-Dec-19 A	16-Apr-20 A																		
Expected Substantial Completion Phase 1	0		12-Jan-21 A																		
Expected Substantial Completion Phase 2	0		12-Jan-21 A																		
LAC Site Barrier Removal																					
Design Campus Improvements	924	12-Sep-17 A	23-Mar-20 A																		
DSA Review LAC Site Barrier Removal	166	24-Mar-20 A	05-Sep-20 A																		
Bid / Award LAC Site Barrier Removal	156	06-Sep-20 A	08-Feb-21 A																		
Construction LAC Site Barrier Removal	282	22-Feb-21 A	30-Nov-21																		
Expected Substantial Completion	0		30-Nov-21																		
LAC Building Barrier Removal																					
Design Campus Improvements	952	12-Sep-17 A	20-Apr-20 A																		
DSA Review LAC Building Barrier Removal	155	12-Jun-20 A	13-Nov-20 A																		
Bid / Award LAC Building Barrier Removal	119	31-May-21 A	26-Sep-21																		
Construction LAC Building Barrier Removal	518	16-Oct-21	17-Mar-23																		
Expected Substantial Completion	0		17-Mar-23																		
Building M - Liberal Arts																					
Pre-Design Building M	329	01-Aug-17 A	26-Jun-18 A																		
Award DBE Building M	120	27-Jun-18 A	25-Oct-18 A																		
Design and DSA Review Building M	517	05-Nov-18 A	04-Apr-20 A																		

 PRE	 Bid / Award	 CONST	 Actual
 DESIGN	 DSA	 FF&E	◆ Milestone

LBCC Bond Program Master Schedule

Status as of May 1, 2021


Activity Name	At Completion Duration	Start	Finish	Timeline																																				
				2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037																			
FF&E / Move Management Swing Spaces Building B for Building M	245	06-Jun-19 A	05-Feb-20 A	█																																				
Move Into Swing Spaces Bldg B for Building M (Jan 2020)	1	17-Jan-20 A	17-Jan-20 A	█																																				
Move Into Swing Spaces Portables for Building M (Jan 2020)	1	26-Jan-20 A	26-Jan-20 A	█																																				
NTP Construction Building M	0	13-Feb-20 A		◆																																				
Construction Building M	610	08-Apr-20 A	08-Dec-21	█																																				
FF&E / Move Management Building M	234	09-Nov-21	01-Jul-22	█																																				
Expected Substantial Completion Building M	0		08-Dec-21	◆																																				
Ready to Hold Classes Building M (Fall 2022)	0		01-Jul-22	◆																																				
Building G - Music & Theater Arts																																								
Design Building G/H	434	11-Sep-19 A	17-Nov-20 A	█																																				
Design Swing Space for Building G/H	300	01-May-20 A	25-Feb-21 A	█																																				
DSA Review Building G/H	316	18-Nov-20 A	29-Sep-21	█																																				
DSA Review Swing Space for Building G/H	60	31-Jan-21 A	31-Mar-21 A	█																																				
Bid / Award Swing Space for Building G/H	106	26-Apr-21 A	09-Aug-21	█																																				
Construction Swing Space Building for G/H	150	10-Aug-21	06-Jan-22	█																																				
Approve Working Documents and Proceed to Bid	52	30-Sep-21	21-Nov-21	█																																				
Bid / Award Building G/H	123	21-Nov-21	23-Mar-22	█																																				
Expected Substantial Completion Swing Space Building for G/H	0		06-Jan-22	◆																																				
Move Into Swing Space (TBD) for Building G/H (Dec 2021/Jan 2022)	15	07-Jan-22	21-Jan-22	█																																				
Construction Building G	750	24-Mar-22	11-Apr-24	█																																				
Expected Substantial Completion Building G	0		11-Apr-24	◆																																				
Ready to Hold Classes Building G (Fall 2024)	0		24-Jul-24	◆																																				
EEM-2C - Thermal Storage Strategy - Bldg P Attic (TBD)																																								
Design EEM-2C	180	01-Apr-22*	27-Sep-22	█																																				
DSA EEM-2C	180	28-Sep-22*	26-Mar-23	█																																				
Bid / Award EEM-2C	90	27-Mar-23	24-Jun-23	█																																				
Construction EEM-2C	160	25-Jun-23	01-Dec-23	█																																				
EEM-2A - Energy and Portable Water Reductions - LAC (TBD)																																								
Design EEM-2A	180	01-Apr-22*	27-Sep-22	█																																				
DSA EEM-2A	260	28-Sep-22*	14-Jun-23	█																																				
Bid / Award EEM-2A	90	15-Jun-23	12-Sep-23	█																																				
Construction EEM-2A	365	13-Sep-23	11-Sep-24	█																																				
Building E - College Center																																								
Design Building E	443	18-Jan-21 A	05-Apr-22	█																																				
Design Swing Space for Building E	180	05-Jun-21	01-Dec-21	█																																				
DSA Review Swing Space for Building E	90	02-Dec-21	01-Mar-22	█																																				
Bid / Award Swing Space for Building E	93	02-Mar-22	02-Jun-22	█																																				
DSA Review Building E	280	06-Apr-22	10-Jan-23	█																																				
Construction Swing Space for Building E	120	03-Jun-22	30-Sep-22	█																																				
FF&E / Move Management Swing Space for Building E	176	02-Aug-22	24-Jan-23	█																																				
Expected Substantial Completion Swing Space for Building E	0		30-Sep-22	◆																																				
Bid / Award Building E	91	11-Jan-23	11-Apr-23	█																																				
NTP	0	13-Apr-23		◆																																				
Construction Building E	610	13-Apr-23	12-Dec-24	█																																				
FF&E / Move Management Building E	195	14-Sep-24	27-Mar-25	█																																				
Expected Substantial Completion	0		12-Dec-24	◆																																				

█ PRE █ Bid / Award █ CONST █ Actual
█ DESIGN █ DSA █ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of May 1, 2021

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Ready to Hold Classes Building E (Fall 2025)	0		27-Mar-25																				
Building S - Stadium																							
Feasibility Study Building S	91	01-May-21*	30-Jul-21																				
Town Hall Meetings Building S	120	31-Jul-21	27-Nov-21																				
Supplemental EIR Building S	365	28-Nov-21	27-Nov-22																				
Design Building S	560	28-Nov-21	10-Jun-23																				
Design Swing Space for Building S	180	28-Nov-22	26-May-23																				
DSA Review Swing Space for Building S	180	27-May-23	22-Nov-23																				
DSA Review Building S	320	11-Jun-23	25-Apr-24																				
Bid/Award Swing Space for Building S	90	23-Nov-23	20-Feb-24																				
Construction Swing Space for Building S	270	21-Feb-24	16-Nov-24																				
Bid / Award Building S	180	26-Apr-24	22-Oct-24																				
Expected Substantial Completion Swing Space Building for S	0		16-Nov-24																				
Move Into Swing Space Building TBD from Building S	50	16-Dec-24*	03-Feb-25																				
NTP Construction Building S	0	22-Feb-25																					
Construction Building S	700	22-Feb-25	22-Jan-27																				
Expected Substantial Completion Building S	0		22-Jan-27																				
Punchlist Building S	30	23-Jan-27	21-Feb-27																				
FF&E / Move Management Building from Building TBD to Building S	200	23-Jan-27	10-Aug-27																				
Ready to Hold Classes Building S (Fall 2027)	0		10-Aug-27																				
Building O2 - Economic & Workforce Development/Foundation																							
Pre-Design Building O2	180	14-Apr-25*	10-Oct-25																				
Design Building O2	280	11-Oct-25	17-Jul-26																				
DSA Review Building O2	280	18-Jul-26	23-Apr-27																				
Construction Swing Space Building O2	40	24-Apr-27	02-Jun-27																				
Bid / Award Building O2	90	24-Apr-27	22-Jul-27																				
Expected Substantial Completion Swing Space Building O2	0		02-Jun-27																				
Move Into Swing Space Building B for Building O2	20	23-Jun-27	12-Jul-27																				
NTP Construction Building O2	0	28-Jul-27																					
Construction Building O2	520	28-Jul-27	28-Dec-28																				
FF&E / Move Management from Building B to Building O2	209	09-Dec-28	05-Jul-29																				
Expected Substantial Completion Building O2	0		28-Dec-28																				
Building K - Art																							
Pre-Design Building K	210	06-Aug-27*	02-Mar-28																				
Design Building K	224	03-Mar-28	12-Oct-28																				
DSA Review Building K	280	13-Oct-28	19-Jul-29																				
Bid / Award Building K	90	20-Jul-29	17-Oct-29																				
Move Into Swing Space Building B for Building K	10	19-Dec-29	28-Dec-29																				
NTP Construction Building K	0	29-Dec-29																					
Construction Building K	390	29-Dec-29	22-Jan-31																				
FF&E / Move Management Building K from Building B	251	25-Oct-30	02-Jul-31																				
Expected Substantial Completion Building K	0		22-Jan-31																				
Ready to Hold Classes Building K	0		02-Jul-31																				
Building R - Primary Gymnasium																							
Pre-Design Building R	145	18-Feb-29*	12-Jul-29																				
Design Building R	363	13-Jul-29	10-Jul-30																				

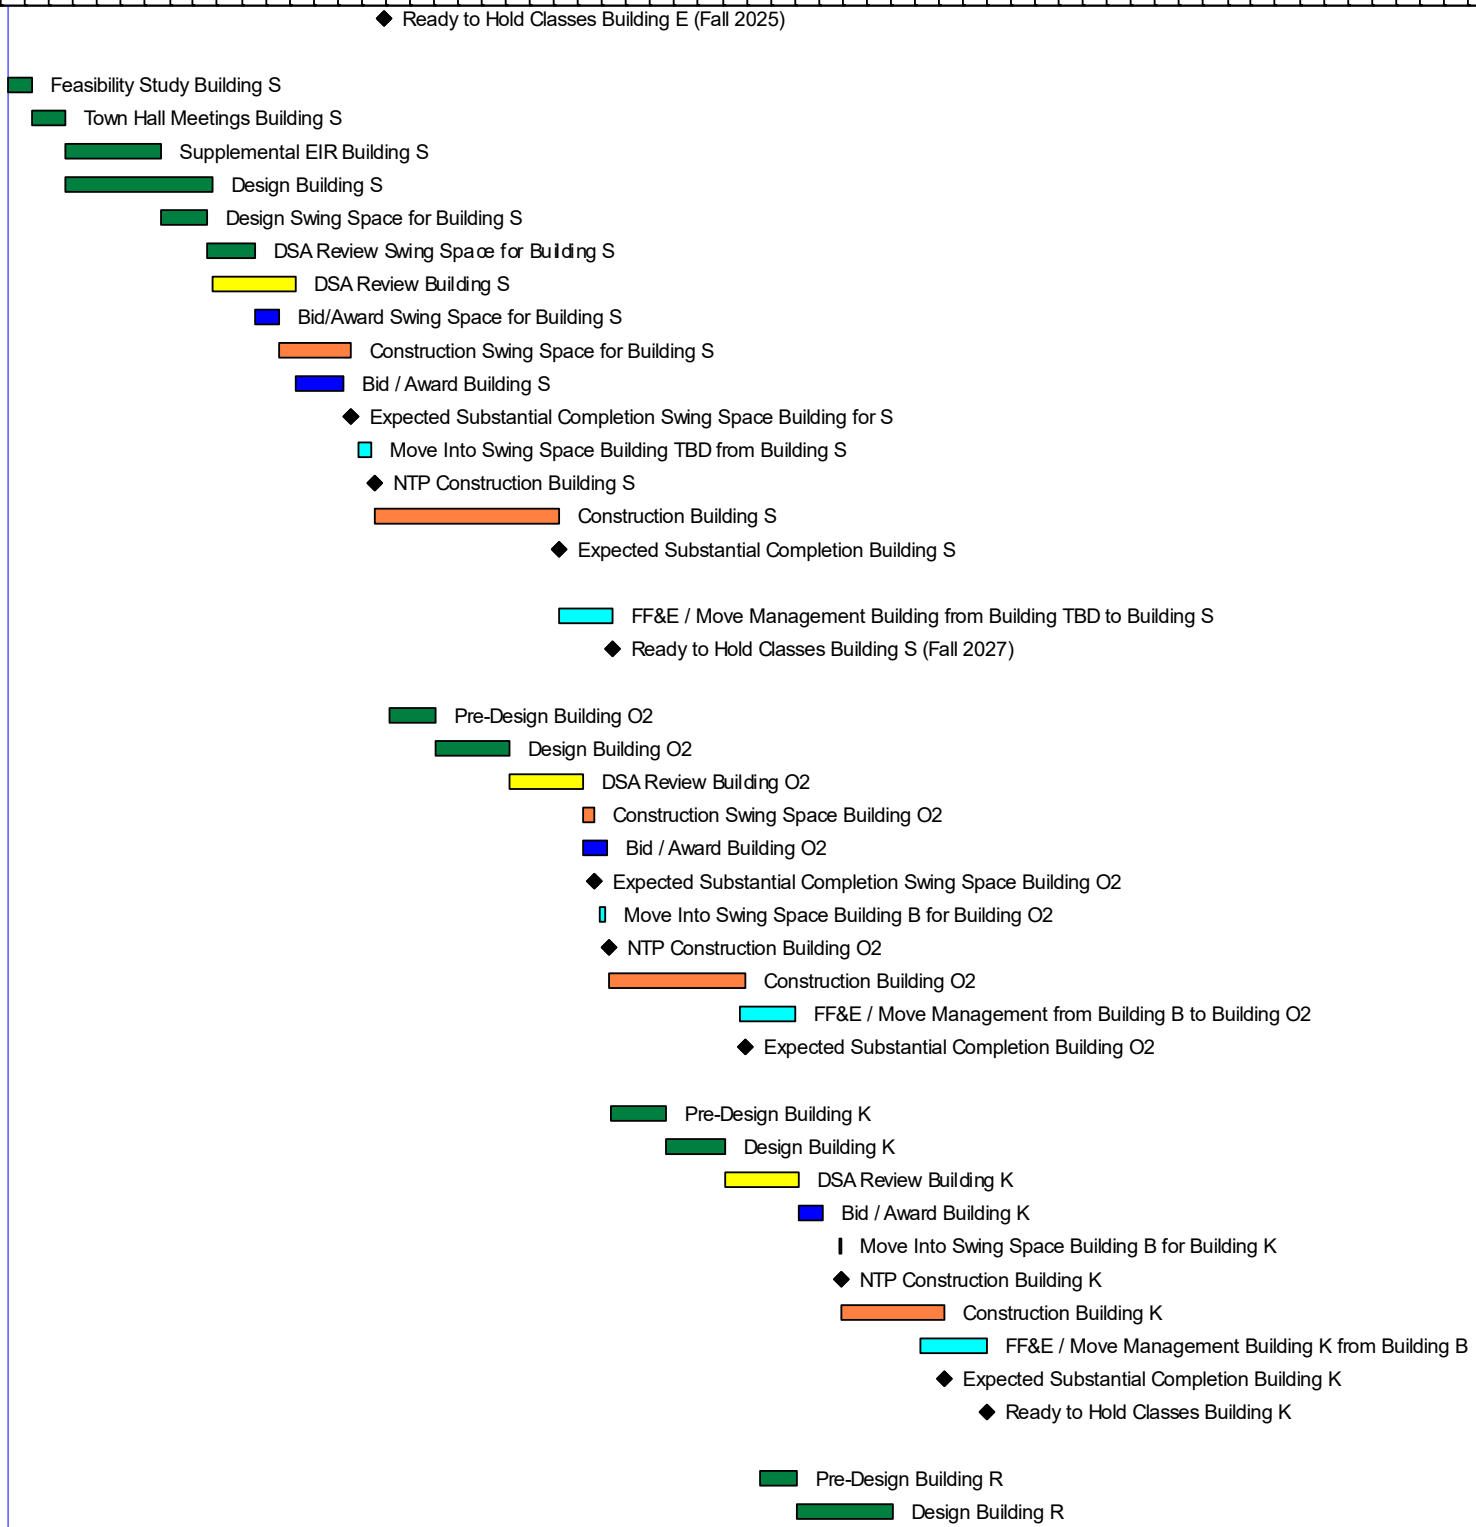

■ PRE ■ Bid/Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of May 1, 2021

Activity Name	At Completion Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
DSA Review Building R	280	11-Jul-30	16-Apr-31																				
Bid / Award Building R	90	17-Apr-31	15-Jul-31																				
Move Into Swing Space Building Q & Aquatic	30	16-Jul-31	14-Aug-31																				
NTP Construction Building R	0	15-Aug-31																					
Construction Building R	730	15-Aug-31	13-Aug-33																				
FF&E / Move Management Building R	180	15-Jul-33	10-Jan-34																				
Expected Substantial Completion Building R	0		13-Aug-33																				
Ready to Hold Classes Building R	0		10-Jan-34																				
Building Q - Secondary Gymnasium																							
Pre-Design Building Q	320	07-Jan-32*	21-Nov-32																				
Design Building Q	246	22-Nov-32	25-Jul-33																				
DSA Review Building Q	280	26-Jul-33	01-May-34																				
Bid / Award Building Q	90	02-May-34	30-Jul-34																				
Move Into Swing Space Building R & Aquatic	30	01-Jun-34	30-Jun-34																				
NTP Construction Building Q	0	05-Aug-34																					
Construction Building Q	610	05-Aug-34	05-Apr-36																				
FF&E / Move Management Building Q	195	08-Dec-35	19-Jun-36																				
Expected Substantial Completion Building Q	0		05-Apr-36																				
Ready to Hold Classes Building Q	0		19-Jun-36																				
Building B - Tech Studies																							
Pre-Design Building B	170	20-Mar-34*	05-Sep-34																				
Design Building B	276	06-Sep-34	08-Jun-35																				
DSA Review Building B	280	09-Jun-35	14-Mar-36																				
Bid / Award Building B	90	15-Mar-36	12-Jun-36																				
NTP Construction Building B	0	13-Jun-36																					
Construction Building B	730	13-Jun-36	12-Jun-38																				
Expected Substantial Completion Building B	0		12-Jun-38																				
Building F - Demo Family/Consumer Education/New Courtyard																							
Design Building F	245	08-Jan-37*	09-Sep-37																				
DSA Review Building F	160	10-Sep-37	16-Feb-38																				
Bid / Award Building F	55	17-Feb-38	12-Apr-38																				
Move Into Building B from Building F	60	13-Jul-38	10-Sep-38																				
Demo & Courtyard Building F	365	11-Sep-38	10-Sep-39																				
Building O1 - IITS/ Warehouse																							
Pre-Design Building O1	200	02-May-36*	17-Nov-36																				
Design Building O1	244	18-Nov-36	19-Jul-37																				
DSA Review Building O1	280	20-Jul-37	25-Apr-38																				
Bid / Award Building O1	90	26-Apr-38	24-Jul-38																				
Move Into Swing Space Building O2	30	25-Jun-38	24-Jul-38																				
NTP Construction Building O1	0	30-Jul-38																					
Construction Building O1	420	30-Jul-38	22-Sep-39																				
FF&E / Move Management Building O1 from Building O2	213	26-May-39	24-Dec-39																				
Expected Substantial Completion Building O1	0		22-Sep-39																				
Building CDC - Child Development Center																							
Pre-Design Building	49	01-Jun-38*	19-Jul-38																				
Design Building	154	20-Jul-38	20-Dec-38																				

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of May 1, 2021

Activity Name	At Completion Duration	Start	Finish	Timeline (2020-2037)																																			
				2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037																		
Ready to Hold Classes Building Humanities (Spring 2028)	0		02-Jan-28																																		◆ Ready to Hold Classes Building Humanities (Spring 2028)		
Building FF - Demo Fine Arts & Senior Center/Turnabout																																							
Design Building FF Demo & Turnabout	189	01-Sep-23	07-Mar-24																																				
DSA Review Building FF	280	08-Mar-24	12-Dec-24																																				
Bid / Award Building FF Demo & Turnabout	86	13-Dec-24	08-Mar-25																																				
Construction Building FF Demo	155	09-Mar-25	10-Aug-25																																				
PCC Walkways & Wayfinding																																							
PCC Walkways and Wayfindings	8773	01-Jul-17 A	07-Jul-41																																				
District Wide																																							
Joint Use Facility w/ LBUSD & CSULB #12																																							
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21 A																																				
Energy/Water Conservation Projects																																							
Energy Water Conservation Projects	9115	01-Jul-16 A	14-Jun-41																																				
Districtwide Solar Projects																																							
Pre-Design, Criteria Documents, RFP	860	21-Mar-19 A	27-Jul-21																																				
Award Districtwide Solar	40	28-Jul-21	05-Sep-21																																				
Design Districtwide Solar	119	06-Sep-21	02-Jan-22																																				
DSA Districtwide Solar	120	03-Jan-22	02-May-22																																				
NTP PCC Construction Solar	0	03-May-22																																					
PCC Construction Solar	120	03-May-22	30-Aug-22																																				
Expected Substantial Completion PCC Solar	0		30-Aug-22																																				
SCE Charge Ready																																							
Design SCE Charge Ready	113	01-Apr-19 A	22-Jul-19 A																																				
Permit and Easement SCE Charge Ready	147	23-Jul-19 A	17-Dec-19 A																																				
PCC Construction Infrastructure SCE Charge Ready	70	16-Jan-20 A	25-Mar-20 A																																				
LAC Construction SCE Infrastructure SCE Charge Ready	72	20-Jan-20 A	31-Mar-20 A																																				
PCC Construction Install ChargePoint SCE Charge Ready	60	26-Mar-20 A	24-May-20 A																																				
LAC Construction Install ChargePoint SCE Charge Ready	60	01-Apr-20 A	30-May-20 A																																				
Technology Refresh/Replacement																																							
Technology Refresh/Replacement	8923	01-Feb-17 A	07-Jul-41																																				
Enterprise Wide Computer System																																							
Enterprise Wide Computer System	8923	01-Feb-17 A	07-Jul-41																																				
Landscaping																																							
Landscaping	8923	01-Feb-17 A	07-Jul-41																																				
Infrastructure Projectss																																							
Infrastructure Projects	8923	01-Feb-17 A	07-Jul-41																																				
Minor Campus Improvements																																							
Minor Campus Improvements	8923	01-Feb-17 A	07-Jul-41																																				
Surface Parking Improvements																																							
Surface Parking Improvements	8923	01-Feb-17 A	07-Jul-41																																				

■ PRE ■ Bid /Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ ◆ Milestone
