


LBCC Bond Program Master Schedule

Status as of October 1, 2021

Activity Name	At Completion Duration	Start	Finish	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Long Beach Community College Bond Program Schedule - October 1, 2021																					
Liberal Arts Campus																					
Building J - Auditorium																					
Design Swing Space for Building J	516	01-Oct-15 A	28-Feb-17 A																		
Design Building J	145	01-Nov-15 A	24-Mar-16 A																		
DSA Building J	398	03-Sep-16 A	06-Oct-17 A																		
Bid / Award Building J	89	07-Oct-17 A	04-Jan-18 A																		
Construction Building J (Spring 2018 - Summer 2020)	914	12-Jan-18 A	14-Jul-20 A																		
FF&E / Move Management from Building J from Public Theater & Building FF	568	24-Nov-19 A	14-Jun-21 A																		
Expected Substantial Completion Building J	0		14-Jul-20 A																		
Ready to Hold Classes Building J (Spring 2021)	0		03-Dec-20 A																		
Kinesiology Labs & Aquatics Center																					
Pre-Design Kinesiology Labs & Aquatic Center	271	01-Sep-16 A	30-May-17 A																		
Design Kinesiology Labs & Aquatic Center	615	01-Jun-17 A	06-Feb-19 A																		
DSA Kinesiology Labs & Aquatic Center	241	29-Jan-19 A	26-Sep-19 A																		
Bid / Award Kinesiology Labs & Aquatic Center	138	19-Sep-19 A	03-Feb-20 A																		
NTP Kinesiology Labs & Aquatic Center	0	10-Feb-20 A																			
Phase 1 Aquatic Complex & North Fields	629	10-Feb-20 A	30-Oct-21																		
Phase 2 Softball Complex	629	10-Feb-20 A	30-Oct-21																		
FF&E / Move Management Kinesiology Labs & Aquatic Center	261	25-Apr-21 A	10-Jan-22																		
Phase 3 Parking Lot etc.	187	27-Apr-21 A	31-Oct-21																		
Ready to Hold Classes Kinesiology Labs & Aquatic Center (Spring 2022)	0		10-Jan-22																		
Building X - Central Plant Expansion																					
Design	413	23-Jan-18 A	12-Mar-19 A																		
DSA LAC Central Plant	146	13-Apr-19 A	06-Sep-19 A																		
Bid / Award LAC Central Plant	107	19-Aug-19 A	03-Dec-19 A																		
Construction LAC Central Plant Phase 1	130	09-Dec-19 A	16-Apr-20 A																		
Construction LAC Central Plant Phase 2	130	09-Dec-19 A	16-Apr-20 A																		
Expected Substantial Completion Phase 1	0		12-Jan-21 A																		
Expected Substantial Completion Phase 2	0		12-Jan-21 A																		
LAC Site Barrier Removal																					
Design Campus Improvements	924	12-Sep-17 A	23-Mar-20 A																		
DSA Review LAC Site Barrier Removal	166	24-Mar-20 A	05-Sep-20 A																		
Bid / Award LAC Site Barrier Removal	156	06-Sep-20 A	08-Feb-21 A																		
Construction LAC Site Barrier Removal	318	16-Feb-21 A	30-Dec-21																		
Expected Substantial Completion	0		30-Dec-21																		
LAC Building Barrier Removal																					
Design Campus Improvements	952	12-Sep-17 A	20-Apr-20 A																		
DSA Review LAC Building Barrier Removal	155	12-Jun-20 A	13-Nov-20 A																		
DSA Addendum Approval	150	03-Nov-21	01-Apr-22																		
Bid / Award LAC Building Barrier Removal	130	02-Apr-22	09-Aug-22																		
Construction LAC Building Barrier Removal	518	18-Aug-22	17-Jan-24																		
Expected Substantial Completion	0		17-Jan-24																		
Building M - Liberal Arts																					
Pre-Design Building M	329	01-Aug-17 A	26-Jun-18 A																		
Award DBE Building M	120	27-Jun-18 A	25-Oct-18 A																		

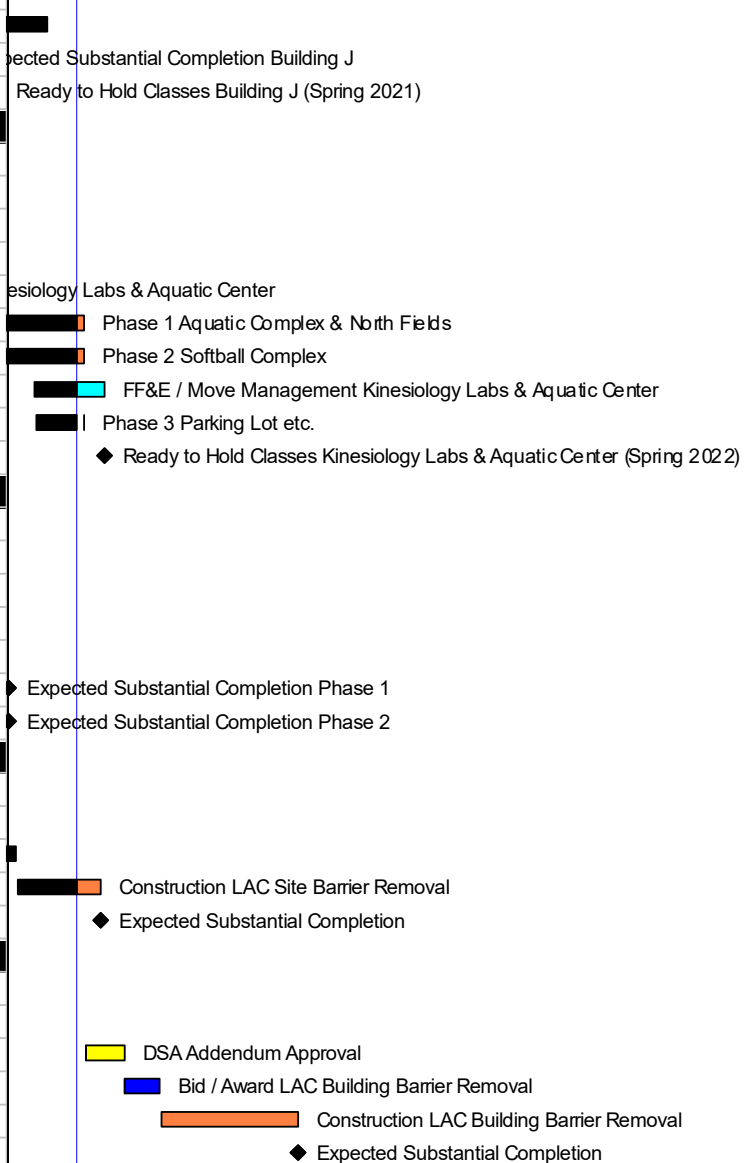

■ PRE ■ Bid/Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of October 1, 2021

Activity Name	At Completion Duration	Start	Finish	Year																																			
				2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038																		
Building M				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q		
Design and DSA Review Building M	517	05-Nov-18 A	04-Apr-20 A																																				
FF&E / Move Management Swing Spaces Building B for Building M	245	06-Jun-19 A	05-Feb-20 A																																				
Move Into Swing Spaces Bldg B for Building M (Jan 2020)	1	17-Jan-20 A	17-Jan-20 A																																				
Move Into Swing Spaces Portables for Building M (Jan 2020)	1	26-Jan-20 A	26-Jan-20 A																																				
NTP Construction Building M	0	13-Feb-20 A																																					
Construction Building M	610	08-Apr-20 A	08-Dec-21																																				
FF&E / Move Management Building M	234	09-Nov-21	01-Jul-22																																				
Expected Substantial Completion Building M	0		08-Dec-21																																				
Ready to Hold Classes Building M (Fall 2022)	0		01-Jul-22																																				
Building G - Music & Theater Arts																																							
Design Building G/H	434	11-Sep-19 A	17-Nov-20 A																																				
Design Swing Space for Building G/H	300	01-May-20 A	25-Feb-21 A																																				
DSA Review Building G/H	318	18-Nov-20 A	01-Oct-21																																				
DSA Review Swing Space for Building G/H	128	31-Jan-21 A	08-Jun-21 A																																				
Bid / Award Swing Space for Building G/H	90	26-Apr-21 A	24-Jul-21 A																																				
Approve Working Documents and Proceed to Bid	52	02-Oct-21	23-Nov-21																																				
Construction Swing Space Building for G/H	90	02-Oct-21	30-Dec-21																																				
Bid / Award Building G/H	122	23-Nov-21	24-Mar-22																																				
Expected Substantial Completion Swing Space Building for G/H	0		30-Dec-21																																				
Move Into Swing Space (TBD) for Building G/H (Dec 2021/Jan 2022)	15	31-Dec-21	14-Jan-22																																				
Construction Building G	750	25-Mar-22	12-Apr-24																																				
Expected Substantial Completion Building G	0		12-Apr-24																																				
Ready to Hold Classes Building G (Fall 2024)	0		25-Jul-24																																				
EEM-2C - Thermal Storage Strategy - Bldg P Attic (TBD)																																							
Design EEM-2C	180	01-Apr-22*	27-Sep-22																																				
DSA EEM-2C	180	28-Sep-22*	26-Mar-23																																				
Bid / Award EEM-2C	90	27-Mar-23	24-Jun-23																																				
Construction EEM-2C	160	25-Jun-23	01-Dec-23																																				
EEM-2A - Energy and Portable Water Reductions - LAC (TBD)																																							
Design EEM-2A	180	01-Apr-22*	27-Sep-22																																				
DSA EEM-2A	260	28-Sep-22*	14-Jun-23																																				
Bid / Award EEM-2A	90	15-Jun-23	12-Sep-23																																				
Construction EEM-2A	365	13-Sep-23	11-Sep-24																																				
Building E - College Center																																							
Design Building E	598	01-Dec-20 A	21-Jul-22																																				
Design Swing Space for Building E	166	01-Nov-21	15-Apr-22																																				
DSA Review Swing Space for Building E	90	16-Apr-22	14-Jul-22																																				
Bid / Award Swing Space for Building E	93	15-Jul-22	15-Oct-22																																				
DSA Review Building E	280	22-Jul-22	27-Apr-23																																				
Construction Swing Space for Building E	120	16-Oct-22	12-Feb-23																																				
FF&E / Move Management Swing Space for Building E	199	15-Dec-22	01-Jul-23																																				
Expected Substantial Completion Swing Space for Building E	0		12-Feb-23																																				
Bid / Award Building E	91	28-Apr-23	27-Jul-23																																				
NTP	0	27-Jul-23																																					
Construction Building E	610	28-Jul-23	28-Mar-25																																				
FF&E / Move Management Building E	208	16-Dec-24	11-Jul-25																																				

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of October 1, 2021

Activity Name	At Completion Duration	Start	Finish	Timeline																																			
				2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038																		
Expected Substantial Completion	0		28-Mar-25	◆ Expected Substantial Completion																																			
Ready to Hold Classes Building E (Fall 2025)	0		11-Jul-25	◆ Ready to Hold Classes Building E (Fall 2025)																																			
Building S - Stadium																																							
Feasibility Study Building S	180	01-Jun-21 A	27-Nov-21	<ul style="list-style-type: none"> ■ Feasibility Study Building S ■ Town Hall Meetings Building S ■ Supplemental EIR Building S ■ Design Building S ■ Design Swing Space for Building S ■ DSA Review Swing Space for Building S ■ DSA Review Building S ■ Bid/Award Swing Space for Building S ■ Construction Swing Space for Building S ■ Bid / Award Building S ◆ Expected Substantial Completion Swing Space Building for S ■ Move Into Swing Space Building TBD from Building S ◆ NTP Construction Building S ■ Construction Building S ◆ Expected Substantial Completion Building S ■ FF&E / Move Management Building from Building TBD to Building S ◆ Ready to Hold Classes Building S (Fall 2027) 																																			
Town Hall Meetings Building S	90	28-Nov-21	25-Feb-22																																				
Supplemental EIR Building S	365	26-Feb-22	25-Feb-23																																				
Design Building S	560	26-Feb-22	08-Sep-23																																				
Design Swing Space for Building S	180	28-Nov-22	26-May-23																																				
DSA Review Swing Space for Building S	180	27-May-23	22-Nov-23																																				
DSA Review Building S	320	09-Sep-23	24-Jul-24																																				
Bid/Award Swing Space for Building S	90	23-Nov-23	20-Feb-24																																				
Construction Swing Space for Building S	270	21-Feb-24	16-Nov-24																																				
Bid / Award Building S	150	25-Jul-24	21-Dec-24																																				
Expected Substantial Completion Swing Space Building for S	0		16-Nov-24																																				
Move Into Swing Space Building TBD from Building S	50	16-Dec-24*	03-Feb-25																																				
NTP Construction Building S	0	22-Feb-25																																					
Construction Building S	700	22-Feb-25	22-Jan-27																																				
Expected Substantial Completion Building S	0		22-Jan-27																																				
Punchlist Building S	30	23-Jan-27	21-Feb-27																																				
FF&E / Move Management Building from Building TBD to Building S	200	23-Jan-27	10-Aug-27																																				
Ready to Hold Classes Building S (Fall 2027)	0		10-Aug-27																																				
Building O2 - Economic & Workforce Development/Foundation																																							
Pre-Design Building O2	180	14-Apr-25*	10-Oct-25	<ul style="list-style-type: none"> ■ Pre-Design Building O2 ■ Design Building O2 ■ DSA Review Building O2 ■ Construction Swing Space Building O2 ■ Bid / Award Building O2 ◆ Expected Substantial Completion Swing Space Building O2 ■ Move Into Swing Space Building B for Building O2 ◆ NTP Construction Building O2 ■ Construction Building O2 ■ FF&E / Move Management from Building B to Building O2 ◆ Expected Substantial Completion Building O2 																																			
Design Building O2	280	11-Oct-25	17-Jul-26																																				
DSA Review Building O2	280	18-Jul-26	23-Apr-27																																				
Construction Swing Space Building O2	40	24-Apr-27	02-Jun-27																																				
Bid / Award Building O2	90	24-Apr-27	22-Jul-27																																				
Expected Substantial Completion Swing Space Building O2	0		02-Jun-27																																				
Move Into Swing Space Building B for Building O2	20	23-Jun-27	12-Jul-27																																				
NTP Construction Building O2	0	28-Jul-27																																					
Construction Building O2	520	28-Jul-27	28-Dec-28																																				
FF&E / Move Management from Building B to Building O2	209	09-Dec-28	05-Jul-29																																				
Expected Substantial Completion Building O2	0		28-Dec-28																																				
Building K - Art																																							
Pre-Design Building K	210	06-Aug-27*	02-Mar-28	<ul style="list-style-type: none"> ■ Pre-Design Building K ■ Design Building K ■ DSA Review Building K ■ Bid / Award Building K ■ Move Into Swing Space Building B for Building K ◆ NTP Construction Building K ■ Construction Building K ■ FF&E / Move Management Building K from Building B ◆ Expected Substantial Completion Building K ◆ Ready to Hold Classes Building K 																																			
Design Building K	224	03-Mar-28	12-Oct-28																																				
DSA Review Building K	280	13-Oct-28	19-Jul-29																																				
Bid / Award Building K	90	20-Jul-29	17-Oct-29																																				
Move Into Swing Space Building B for Building K	10	19-Dec-29	28-Dec-29																																				
NTP Construction Building K	0	29-Dec-29																																					
Construction Building K	390	29-Dec-29	22-Jan-31																																				
FF&E / Move Management Building K from Building B	251	25-Oct-30	02-Jul-31																																				
Expected Substantial Completion Building K	0		22-Jan-31																																				
Ready to Hold Classes Building K	0		02-Jul-31																																				
Building R - Primary Gymnasium																																							
Pre-Design Building R	145	18-Feb-29*	12-Jul-29	■ Pre-Design Building R																																			

■ PRE ■ Bid / Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of October 1, 2021

Activity Name	At Completion Duration	Start	Finish	Year																																																																																																																																																																																																															
				2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038																																																																																																																																																																																														
<div style="display: flex; justify-content: space-between; align-items: flex-start; padding: 10px;"> <table style="width: 45%; border-collapse: collapse;"> <tr style="background-color: #333; color: white;"><th colspan="4">Building R - Secondary Gymnasium</th></tr> <tr><td>Design Building R</td><td style="text-align: center;">363</td><td>13-Jul-29</td><td>10-Jul-30</td></tr> <tr><td>DSA Review Building R</td><td style="text-align: center;">280</td><td>11-Jul-30</td><td>16-Apr-31</td></tr> <tr><td>Bid / Award Building R</td><td style="text-align: center;">90</td><td>17-Apr-31</td><td>15-Jul-31</td></tr> <tr><td>Move Into Swing Space Building Q & Aquatic</td><td style="text-align: center;">30</td><td>16-Jul-31</td><td>14-Aug-31</td></tr> <tr><td>NTP Construction Building R</td><td style="text-align: center;">0</td><td>15-Aug-31</td><td></td></tr> <tr><td>Construction Building R</td><td style="text-align: center;">730</td><td>15-Aug-31</td><td>13-Aug-33</td></tr> <tr><td>FF&E / Move Management Building R</td><td style="text-align: center;">180</td><td>15-Jul-33</td><td>10-Jan-34</td></tr> <tr><td>Expected Substantial Completion Building R</td><td style="text-align: center;">0</td><td></td><td>13-Aug-33</td></tr> <tr><td>Ready to Hold Classes Building R</td><td style="text-align: center;">0</td><td></td><td>10-Jan-34</td></tr> <tr style="background-color: #333; color: white;"><th colspan="4">Building Q - Secondary Gymnasium</th></tr> <tr><td>Pre-Design Building Q</td><td style="text-align: center;">320</td><td>07-Jan-32*</td><td>21-Nov-32</td></tr> <tr><td>Design Building Q</td><td style="text-align: center;">246</td><td>22-Nov-32</td><td>25-Jul-33</td></tr> <tr><td>DSA Review Building Q</td><td style="text-align: center;">280</td><td>26-Jul-33</td><td>01-May-34</td></tr> <tr><td>Bid / Award Building Q</td><td style="text-align: center;">90</td><td>02-May-34</td><td>30-Jul-34</td></tr> <tr><td>Move Into Swing Space Building R & Aquatic</td><td style="text-align: center;">30</td><td>01-Jun-34</td><td>30-Jun-34</td></tr> <tr><td>NTP Construction Building Q</td><td style="text-align: center;">0</td><td>05-Aug-34</td><td></td></tr> <tr><td>Construction Building Q</td><td style="text-align: center;">610</td><td>05-Aug-34</td><td>05-Apr-36</td></tr> <tr><td>FF&E / Move Management Building Q</td><td style="text-align: center;">195</td><td>08-Dec-35</td><td>19-Jun-36</td></tr> <tr><td>Expected Substantial Completion Building Q</td><td style="text-align: center;">0</td><td></td><td>05-Apr-36</td></tr> <tr><td>Ready to Hold Classes Building Q</td><td style="text-align: center;">0</td><td></td><td>19-Jun-36</td></tr> <tr style="background-color: #333; color: white;"><th colspan="4">Building B - Tech Studies</th></tr> <tr><td>Pre-Design Building B</td><td style="text-align: center;">170</td><td>20-Mar-34*</td><td>05-Sep-34</td></tr> <tr><td>Design Building B</td><td style="text-align: center;">276</td><td>06-Sep-34</td><td>08-Jun-35</td></tr> <tr><td>DSA Review Building B</td><td style="text-align: center;">280</td><td>09-Jun-35</td><td>14-Mar-36</td></tr> <tr><td>Bid / Award Building B</td><td style="text-align: center;">90</td><td>15-Mar-36</td><td>12-Jun-36</td></tr> <tr><td>NTP Construction Building B</td><td style="text-align: center;">0</td><td>13-Jun-36</td><td></td></tr> <tr><td>Construction Building B</td><td style="text-align: center;">730</td><td>13-Jun-36</td><td>12-Jun-38</td></tr> <tr><td>Expected Substantial Completion Building B</td><td style="text-align: center;">0</td><td></td><td>12-Jun-38</td></tr> <tr style="background-color: #333; color: white;"><th colspan="4">Building F - Demo Family/Consumer Education/New Courtyard</th></tr> <tr><td>Design Building F</td><td style="text-align: center;">245</td><td>08-Jan-37*</td><td>09-Sep-37</td></tr> <tr><td>DSA Review Building F</td><td style="text-align: center;">160</td><td>10-Sep-37</td><td>16-Feb-38</td></tr> <tr><td>Bid / Award Building F</td><td style="text-align: center;">55</td><td>17-Feb-38</td><td>12-Apr-38</td></tr> <tr><td>Move Into Building B from Building F</td><td style="text-align: center;">60</td><td>13-Jul-38</td><td>10-Sep-38</td></tr> <tr><td>Demo & Courtyard Building F</td><td style="text-align: center;">365</td><td>11-Sep-38</td><td>10-Sep-39</td></tr> <tr style="background-color: #333; color: white;"><th colspan="4">Building O1 - IITS/ Warehouse</th></tr> <tr><td>Pre-Design Building O1</td><td style="text-align: center;">200</td><td>02-May-36*</td><td>17-Nov-36</td></tr> <tr><td>Design Building O1</td><td style="text-align: center;">244</td><td>18-Nov-36</td><td>19-Jul-37</td></tr> <tr><td>DSA Review Building O1</td><td style="text-align: center;">280</td><td>20-Jul-37</td><td>25-Apr-38</td></tr> <tr><td>Bid / Award Building O1</td><td style="text-align: center;">90</td><td>26-Apr-38</td><td>24-Jul-38</td></tr> <tr><td>Move Into Swing Space Building O2</td><td style="text-align: center;">30</td><td>25-Jun-38</td><td>24-Jul-38</td></tr> <tr><td>NTP Construction Building O1</td><td style="text-align: center;">0</td><td>30-Jul-38</td><td></td></tr> <tr><td>Construction Building O1</td><td style="text-align: center;">420</td><td>30-Jul-38</td><td>22-Sep-39</td></tr> <tr><td>FF&E / Move Management Building O1 from Building O2</td><td style="text-align: center;">213</td><td>26-May-39</td><td>24-Dec-39</td></tr> <tr><td>Expected Substantial Completion Building O1</td><td style="text-align: center;">0</td><td></td><td>22-Sep-39</td></tr> <tr style="background-color: #333; color: white;"><th colspan="4">Building CDC - Child Development Center</th></tr> <tr><td>Pre-Design Building</td><td style="text-align: center;">49</td><td>01-Jun-38*</td><td>19-Jul-38</td></tr> </table> <div style="width: 55%;"> <p>Legend:</p> <ul style="list-style-type: none"> ■ Design Building R ■ DSA Review Building R ■ Bid / Award Building R ■ Move Into Swing Space Building Q & Aquatic ■ Construction Building R ■ FF&E / Move Management Building R ◆ Expected Substantial Completion Building R ◆ Ready to Hold Classes Building R <ul style="list-style-type: none"> ■ Pre-Design Building Q ■ Design Building Q ■ DSA Review Building Q ■ Bid / Award Building Q ■ Move Into Swing Space Building R & Aquatic ■ Construction Building Q ■ FF&E / Move Management Building Q ◆ Expected Substantial Completion Building Q ◆ Ready to Hold Classes Building Q <ul style="list-style-type: none"> ■ Pre-Design Building B ■ Design Building B ■ DSA Review Building B ■ Bid / Award Building B ■ Construction Building B <ul style="list-style-type: none"> ■ Design Building F ■ DSA Review Building F ■ Bid / Award Building F <ul style="list-style-type: none"> ■ Pre-Design Building O1 ■ Design Building O1 ■ DSA Review Building O1 </div> </div>																								Building R - Secondary Gymnasium				Design Building R	363	13-Jul-29	10-Jul-30	DSA Review Building R	280	11-Jul-30	16-Apr-31	Bid / Award Building R	90	17-Apr-31	15-Jul-31	Move Into Swing Space Building Q & Aquatic	30	16-Jul-31	14-Aug-31	NTP Construction Building R	0	15-Aug-31		Construction Building R	730	15-Aug-31	13-Aug-33	FF&E / Move Management Building R	180	15-Jul-33	10-Jan-34	Expected Substantial Completion Building R	0		13-Aug-33	Ready to Hold Classes Building R	0		10-Jan-34	Building Q - Secondary Gymnasium				Pre-Design Building Q	320	07-Jan-32*	21-Nov-32	Design Building Q	246	22-Nov-32	25-Jul-33	DSA Review Building Q	280	26-Jul-33	01-May-34	Bid / Award Building Q	90	02-May-34	30-Jul-34	Move Into Swing Space Building R & Aquatic	30	01-Jun-34	30-Jun-34	NTP Construction Building Q	0	05-Aug-34		Construction Building Q	610	05-Aug-34	05-Apr-36	FF&E / Move Management Building Q	195	08-Dec-35	19-Jun-36	Expected Substantial Completion Building Q	0		05-Apr-36	Ready to Hold Classes Building Q	0		19-Jun-36	Building B - Tech Studies				Pre-Design Building B	170	20-Mar-34*	05-Sep-34	Design Building B	276	06-Sep-34	08-Jun-35	DSA Review Building B	280	09-Jun-35	14-Mar-36	Bid / Award Building B	90	15-Mar-36	12-Jun-36	NTP Construction Building B	0	13-Jun-36		Construction Building B	730	13-Jun-36	12-Jun-38	Expected Substantial Completion Building B	0		12-Jun-38	Building F - Demo Family/Consumer Education/New Courtyard				Design Building F	245	08-Jan-37*	09-Sep-37	DSA Review Building F	160	10-Sep-37	16-Feb-38	Bid / Award Building F	55	17-Feb-38	12-Apr-38	Move Into Building B from Building F	60	13-Jul-38	10-Sep-38	Demo & Courtyard Building F	365	11-Sep-38	10-Sep-39	Building O1 - IITS/ Warehouse				Pre-Design Building O1	200	02-May-36*	17-Nov-36	Design Building O1	244	18-Nov-36	19-Jul-37	DSA Review Building O1	280	20-Jul-37	25-Apr-38	Bid / Award Building O1	90	26-Apr-38	24-Jul-38	Move Into Swing Space Building O2	30	25-Jun-38	24-Jul-38	NTP Construction Building O1	0	30-Jul-38		Construction Building O1	420	30-Jul-38	22-Sep-39	FF&E / Move Management Building O1 from Building O2	213	26-May-39	24-Dec-39	Expected Substantial Completion Building O1	0		22-Sep-39	Building CDC - Child Development Center				Pre-Design Building	49	01-Jun-38*	19-Jul-38
Building R - Secondary Gymnasium																																																																																																																																																																																																																			
Design Building R	363	13-Jul-29	10-Jul-30																																																																																																																																																																																																																
DSA Review Building R	280	11-Jul-30	16-Apr-31																																																																																																																																																																																																																
Bid / Award Building R	90	17-Apr-31	15-Jul-31																																																																																																																																																																																																																
Move Into Swing Space Building Q & Aquatic	30	16-Jul-31	14-Aug-31																																																																																																																																																																																																																
NTP Construction Building R	0	15-Aug-31																																																																																																																																																																																																																	
Construction Building R	730	15-Aug-31	13-Aug-33																																																																																																																																																																																																																
FF&E / Move Management Building R	180	15-Jul-33	10-Jan-34																																																																																																																																																																																																																
Expected Substantial Completion Building R	0		13-Aug-33																																																																																																																																																																																																																
Ready to Hold Classes Building R	0		10-Jan-34																																																																																																																																																																																																																
Building Q - Secondary Gymnasium																																																																																																																																																																																																																			
Pre-Design Building Q	320	07-Jan-32*	21-Nov-32																																																																																																																																																																																																																
Design Building Q	246	22-Nov-32	25-Jul-33																																																																																																																																																																																																																
DSA Review Building Q	280	26-Jul-33	01-May-34																																																																																																																																																																																																																
Bid / Award Building Q	90	02-May-34	30-Jul-34																																																																																																																																																																																																																
Move Into Swing Space Building R & Aquatic	30	01-Jun-34	30-Jun-34																																																																																																																																																																																																																
NTP Construction Building Q	0	05-Aug-34																																																																																																																																																																																																																	
Construction Building Q	610	05-Aug-34	05-Apr-36																																																																																																																																																																																																																
FF&E / Move Management Building Q	195	08-Dec-35	19-Jun-36																																																																																																																																																																																																																
Expected Substantial Completion Building Q	0		05-Apr-36																																																																																																																																																																																																																
Ready to Hold Classes Building Q	0		19-Jun-36																																																																																																																																																																																																																
Building B - Tech Studies																																																																																																																																																																																																																			
Pre-Design Building B	170	20-Mar-34*	05-Sep-34																																																																																																																																																																																																																
Design Building B	276	06-Sep-34	08-Jun-35																																																																																																																																																																																																																
DSA Review Building B	280	09-Jun-35	14-Mar-36																																																																																																																																																																																																																
Bid / Award Building B	90	15-Mar-36	12-Jun-36																																																																																																																																																																																																																
NTP Construction Building B	0	13-Jun-36																																																																																																																																																																																																																	
Construction Building B	730	13-Jun-36	12-Jun-38																																																																																																																																																																																																																
Expected Substantial Completion Building B	0		12-Jun-38																																																																																																																																																																																																																
Building F - Demo Family/Consumer Education/New Courtyard																																																																																																																																																																																																																			
Design Building F	245	08-Jan-37*	09-Sep-37																																																																																																																																																																																																																
DSA Review Building F	160	10-Sep-37	16-Feb-38																																																																																																																																																																																																																
Bid / Award Building F	55	17-Feb-38	12-Apr-38																																																																																																																																																																																																																
Move Into Building B from Building F	60	13-Jul-38	10-Sep-38																																																																																																																																																																																																																
Demo & Courtyard Building F	365	11-Sep-38	10-Sep-39																																																																																																																																																																																																																
Building O1 - IITS/ Warehouse																																																																																																																																																																																																																			
Pre-Design Building O1	200	02-May-36*	17-Nov-36																																																																																																																																																																																																																
Design Building O1	244	18-Nov-36	19-Jul-37																																																																																																																																																																																																																
DSA Review Building O1	280	20-Jul-37	25-Apr-38																																																																																																																																																																																																																
Bid / Award Building O1	90	26-Apr-38	24-Jul-38																																																																																																																																																																																																																
Move Into Swing Space Building O2	30	25-Jun-38	24-Jul-38																																																																																																																																																																																																																
NTP Construction Building O1	0	30-Jul-38																																																																																																																																																																																																																	
Construction Building O1	420	30-Jul-38	22-Sep-39																																																																																																																																																																																																																
FF&E / Move Management Building O1 from Building O2	213	26-May-39	24-Dec-39																																																																																																																																																																																																																
Expected Substantial Completion Building O1	0		22-Sep-39																																																																																																																																																																																																																
Building CDC - Child Development Center																																																																																																																																																																																																																			
Pre-Design Building	49	01-Jun-38*	19-Jul-38																																																																																																																																																																																																																


■ PRE ■ Bid/Award ■ CONST ■ Actual
■ DESIGN ■ DSA ■ FF&E ◆ Milestone

LBCC Bond Program Master Schedule

Status as of October 1, 2021

Activity Name	At Completion Duration	Start	Finish	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Design Building	154	20-Jul-38	20-Dec-38																			
DSA Review Building	280	21-Dec-38	26-Sep-39																			
Move Into Swing Space TBD from CDC	60	20-May-39	18-Jul-39																			
Bid / Award Building	90	27-Sep-39	25-Dec-39																			
NTP Construction Building	0	26-Dec-39																				
Construction Building	290	26-Dec-39	10-Oct-40																			
FF&E / Move Management	201	12-Jun-40	29-Dec-40																			
Expected Substantial Completion Building	0		10-Sep-40																			
Pacific Coast Campus																						
Building P2 - PCC Parking Structure																						
Design Parking Structure	224	16-Jul-18 A	25-Feb-19 A																			
DSA Review Parking Structure	290	16-Jan-19 A	01-Nov-19 A																			
NTP Construction Parking Structure	0	11-Oct-19 A																				
Construction Parking Structure	381	11-Oct-19 A	26-Oct-20 A																			
Expected Substantial Completion Parking Structure	0		26-Oct-20 A																			
Closeout Parking Structure	91	01-Nov-20 A	30-Jan-21 A																			
Building MM - Construction Trades Ph 1																						
DSA Review Building MM Ph 1	385	10-Jan-19 A	30-Jan-20 A																			
Approve Working Documents and Proceed to Bid Ph 1	128	01-Feb-20 A	08-Jun-20 A																			
Approval to Award Construction Contract	123	09-May-20 A	08-Sep-20 A																			
Construction Building MM Ph 1	420	01-Dec-20 A	24-Jan-22																			
FF&E / Move Management Building MM for Building MM Ph 1	278	01-Oct-21	06-Jul-22																			
Expected Substantial Completion Building MM Ph 1	0		24-Jan-22																			
Ready to Hold Classes Building MM Ph 1 (Fall 2022)	0		06-Jul-22																			
EEM-2A - Energy and Portable Water Reductions - PCC (TBD)																						
Design EEM-2A	180	01-Apr-22*	27-Sep-22																			
DSA EEM-2A	260	28-Sep-22	14-Jun-23																			
Bid / Award EEM-2A	90	15-Jun-23	12-Sep-23																			
Construction EEM-2A	365	13-Sep-23	11-Sep-24																			
Building MM - Construction Trades Ph 2																						
Design Building MM Ph 2	304	01-Oct-20 A	01-Aug-21 A																			
DSA Review Building MM Ph 2	280	02-Aug-21 A	09-May-22																			
Chancellor's Office Review DSA Permit & Bid	56	09-May-22	04-Jul-22																			
Bid Process for Building Building MM Ph 2	91	04-Jul-22	03-Oct-22																			
Chancellor's Office Review & Approve Award of Contract	28	03-Oct-22	31-Oct-22																			
Construction Building MM Ph 2	600	31-Oct-22	22-Jun-24																			
FF&E / Move Management Building MM to Building MM Ph 2	195	23-Apr-24	04-Nov-24																			
Expected Substantial Completion Building MM Ph 2	0		22-Jun-24																			
Ready to Hold Classes Building MM Ph 2 (Spring 2025)	0		27-Dec-24																			
Building OO - Humanities																						
Design Building Humanities	608	03-Oct-22*	01-Jun-24																			
DSA Review Building Humanities	280	02-Jun-24	08-Mar-25																			
Bid / Award Building Humanities	90	09-Mar-25	06-Jun-25																			
NTP Construction Building Humanities	0		11-Jun-25																			
Construction Building Humanities	770	12-Jun-25	21-Jul-27																			
FF&E / Move Management Building Humanities from Building Humanities	265	13-Apr-27	02-Jan-28																			

PRE Bid/Award CONST Actual
DESIGN DSA FF&E Milestone

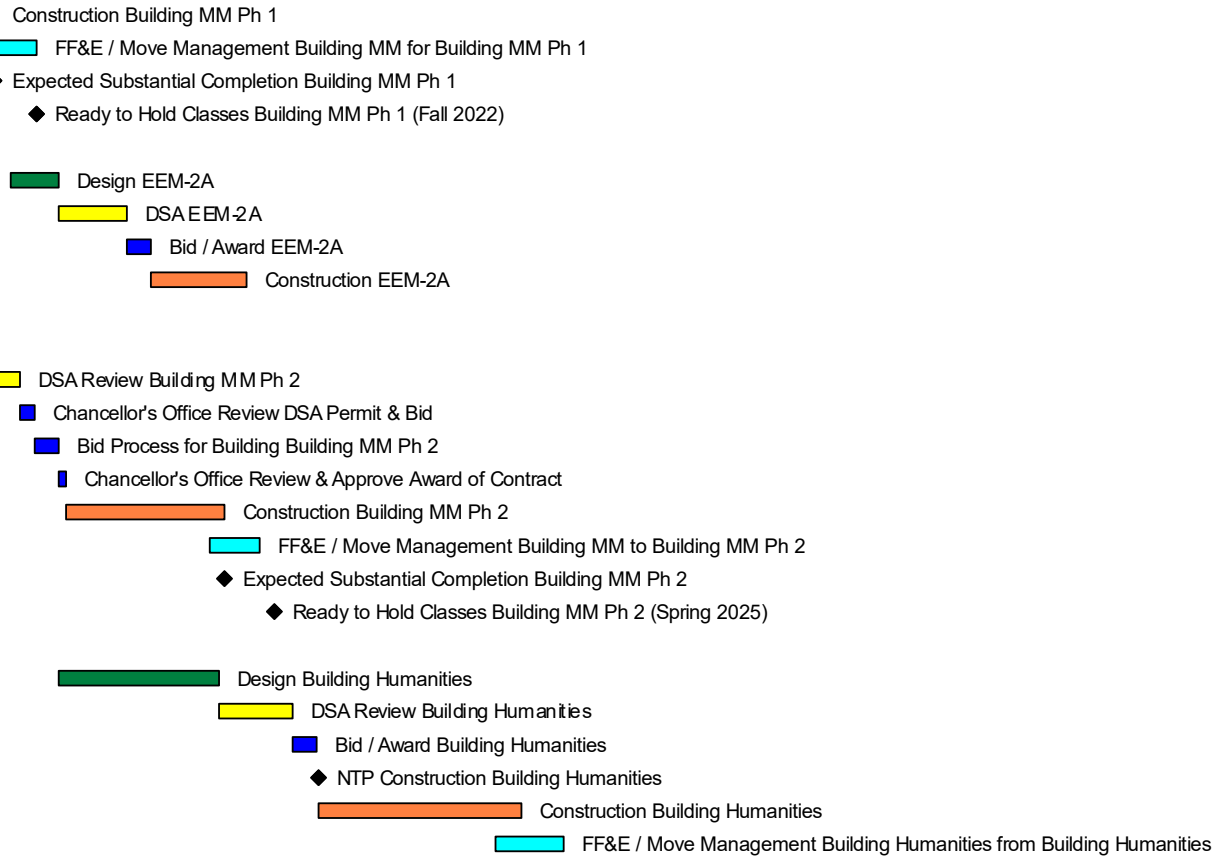

LBCC Bond Program Master Schedule

Status as of October 1, 2021

Activity Name	At Completion Duration	Start	Finish	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038		
				Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Expected Substantial Completion Building Humanities	0	21-Jul-27									◆												
Ready to Hold Classes Building Humanities (Spring 2028)	0	02-Jan-28									◆												
Building FF - Demo Fine Arts & Senior Center/Turnabout																							
Design Building FF Demo & Turnabout	189	01-Sep-23	07-Mar-24																				
DSA Review Building FF	280	08-Mar-24	12-Dec-24																				
Bid / Award Building FF Demo & Turnabout	86	13-Dec-24	08-Mar-25																				
Construction Building FF Demo	155	09-Mar-25	10-Aug-25																				
PCC Walkways & Wayfinding																							
PCC Walkways and Wayfindings	8803	01-Jul-17 A	06-Aug-41																				
District Wide																							
Joint Use Facility w/ LBUSD & CSULB #12																							
Joint Use w/ LBUSD & CSULB #12	1294	01-Aug-17 A	14-Feb-21 A																				
Energy/Water Conservation Projects																							
Energy Water Conservation Projects	9145	01-Jul-16 A	14-Jul-41																				
Districtwide Solar Projects																							
Pre-Design, Criteria Documents, RFP	1097	21-Mar-19 A	21-Mar-22																				
Award Districtwide Solar	40	22-Mar-22	30-Apr-22																				
Design Districtwide Solar	119	01-May-22	27-Aug-22																				
DSA Districtwide Solar	120	28-Aug-22	25-Dec-22																				
NTP PCC Construction Solar	0	26-Dec-22																					
PCC Construction Solar	120	26-Dec-22	24-Apr-23																				
Expected Substantial Completion PCC Solar	0	24-Apr-23																					
SCE Charge Ready																							
Design SCE Charge Ready	113	01-Apr-19 A	22-Jul-19 A																				
Permit and Easement SCE Charge Ready	147	23-Jul-19 A	17-Dec-19 A																				
PCC Construction Infrastructure SCE Charge Ready	70	16-Jan-20 A	25-Mar-20 A																				
LAC Construction SCE Infrastructure SCE Charge Ready	72	20-Jan-20 A	31-Mar-20 A																				
PCC Construction Install ChargePoint SCE Charge Ready	60	26-Mar-20 A	24-May-20 A																				
LAC Construction Install ChargePoint SCE Charge Ready	60	01-Apr-20 A	30-May-20 A																				
Technology Refresh/Replacement																							
Technology Refresh/Replacement	8953	01-Feb-17 A	06-Aug-41																				
Enterprise Wide Computer System																							
Enterprise Wide Computer System	8953	01-Feb-17 A	06-Aug-41																				
Landscaping																							
Landscaping	8953	01-Feb-17 A	06-Aug-41																				
Infrastructure Projectss																							
Infrastructure Projects	8953	01-Feb-17 A	06-Aug-41																				
Minor Campus Improvements																							
Minor Campus Improvements	8953	01-Feb-17 A	06-Aug-41																				
Surface Parking Improvements																							
Surface Parking Improvements	8953	01-Feb-17 A	06-Aug-41																				

■ PRE	■ Bid /Award	■ CONST	■ Actual
■ DESIGN	■ DSA	■ FF&E	◆ Milestone
